



# PANDEMIC RECOVERY OFFICE

## Female Youth Residential Facility Design Final Report

### Submitted by State of Rhode Island Pandemic Recovery Office

Paul L. Dion, Ph.D., Director

Brianna Ruggiero, Chief of Staff

Nicholas R. Fanuele, Project Lead

Ross Lancaster, Data Analyst III

Derek Gomes, Chief Public Affairs Officer

<https://pandemicrecovery.ri.gov>

This project was supported, in whole or in part, by federal award number SLFRP0136 awarded to the State of Rhode Island by the U.S. Department of Treasury.

**Female Youth Residential Treatment Facility Design**

Project Identification Number: 10027

Pandemic Recovery Office Approval Date: August 30, 2022

Project Completion Date: September 18, 2024

Funded Amount: \$1,000,000

Expended Amount: \$999,850

Project Expenditure Category: 6.1 Revenue Replacement: Provision of Government Services

Project Overview: The funds paid design and architectural planning costs for a new, residential facility to address the behavioral health needs of female youth ages 13 to 18. The approximately 30,000-square-foot facility on State-owned property in Exeter will include two, eight-bedroom suites, activity rooms, classrooms, a media center, visitor space, and staff offices. Recreational spaces will include a fitness center, gym, multi-use outdoor courts, and a sports field. Construction is scheduled for completion by late spring 2026.


Financial Overview: All program payments can be found on the [Pandemic Recovery Office’s website](#) by filtering the “Project” box for “Female Youth Residential Facility Design.” The table below shows planned expenditures by fiscal quarter and actual expenditures by fiscal quarter:

<b>Fiscal Year Quarter</b>	<b>Planned Expenditures</b>	<b>Actual Expenditures</b>
FY 2023 Q3	\$249,775	-
FY 2023 Q4	\$750,225	\$218,098
FY 2024 Q1	-	\$239,908
FY 2024 Q2	-	\$230,652
FY 2024 Q3	-	\$311,150
FY 2024 Q4	-	\$42
<b>Total</b>	<b>\$1,000,000</b>	<b>\$999,850</b>
<i>Notes: A single audit fee applies to all State Fiscal Recovery Fund projects and accounts for \$300 of the funds shown in the above table.</i>		


Key Performance Indicators: The following are the key performance indicators based on quarterly goals and monthly data collections.

**Legend:**      ● Actual KPI Value Reported      ◆ Quarterly Goals

**1. Completion of programming, schematic, and preliminary design documents\***

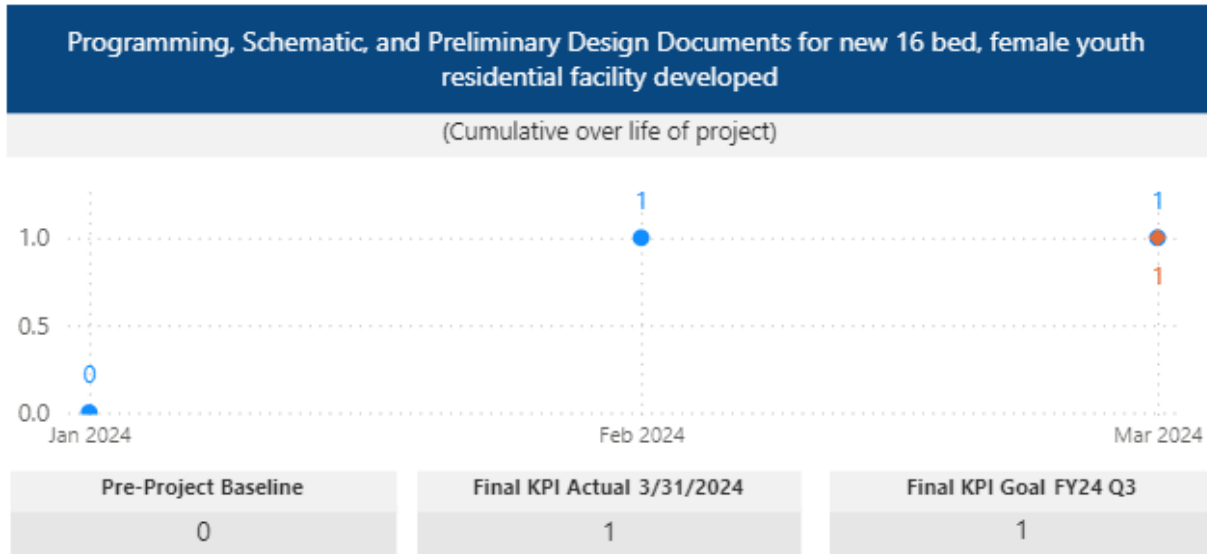

**2. Construction of female youth residential facility begins\***

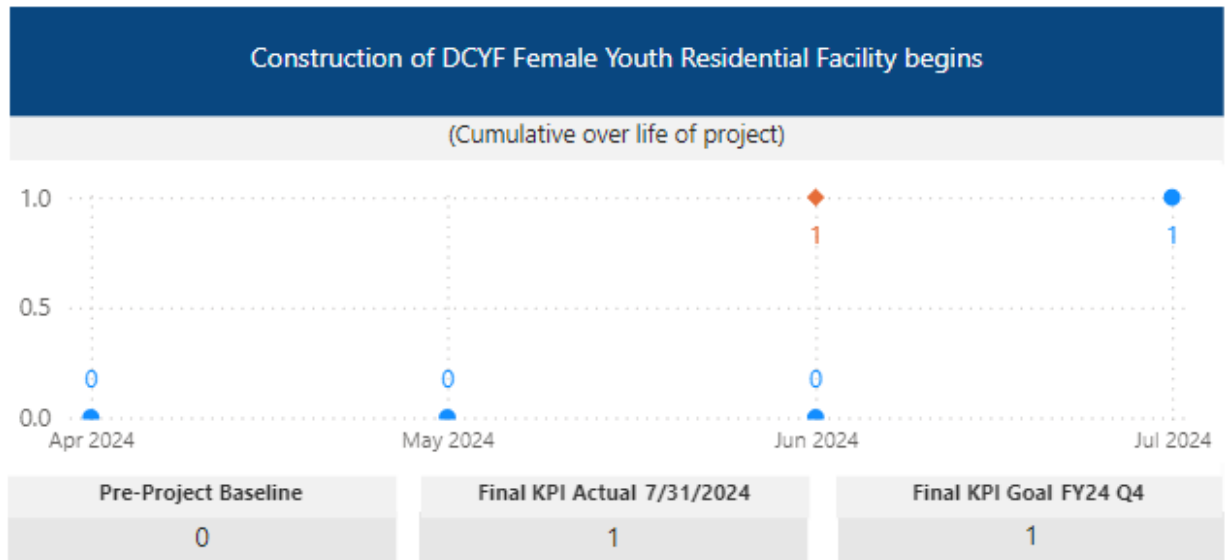

*\*These are yes/no binary indicators: 0 meaning 'no', 1 meaning 'yes'.*

Auxiliary Information: Members of Governor Dan McKee’s administration and legislative leaders participated in a groundbreaking ceremony at the site on August 13, 2024.<sup>1</sup> Below is a rendering of the facility provided by DBVW Architects, the architect for the project. Peregrine Group LLC is the project manager, and Gilbane Building Company is the general contractor.



---

<sup>1</sup> [McKee Administration Breaks Ground on New DCYF Female Adolescent Facility](#)
