



PANDEMIC RECOVERY OFFICE

Female Youth Residential Treatment Facility Final Report

Submitted by State of Rhode Island Pandemic Recovery Office

Paul L. Dion, Ph.D., Director

Brianna Ruggiero, Chief of Staff

Ross Lancaster, Data Analyst III

Derek Gomes, Chief Public Affairs Officer

<https://pandemicrecovery.ri.gov>

This project was supported, in whole or in part, by federal award number SLFRP0136 awarded to the State of Rhode Island by the U.S. Department of Treasury.

Female Youth Residential Treatment FacilityProject Identification Number: 10102Pandemic Recovery Office Approval Date: March 10, 2026Project Completion Date: May 8, 2026Funded Amount: \$6,335,635Expended Amount: \$6,335,635Project Expenditure Category: 6.1 Revenue Replacement: Provision of Government Services


Project Overview: The project is the construction of a 32,000-square-foot female youth residential facility for clients between the ages of 13 and 20 on an 11-acre State-owned property in Exeter. The facility design mimics a residential-style atmosphere, with 16 bedrooms, classrooms, treatment rooms, recreation areas, and support spaces for youth, staff, and families.

The total projected cost is \$40.8 million, with the Rhode Island Capital Plan financing the remainder of the cost. The \$6.3 million in State Fiscal Recovery Funds supported technical assistance related to pre-construction services, site mobilization, and award of bid packages for construction activities.


Financial Overview: All program payments can be found on the [Pandemic Recovery Office's website](#) by filtering the "Project" box for "Exeter Female Youth Residential Treatment Facility." The table below shows planned expenditures by fiscal quarter and actual expenditures by fiscal quarter:

Fiscal Year Quarter	Planned Expenditures	Actual Expenditures
FY 2026 Q3	\$6,335,635	-
FY 2026 Q4	-	\$6,335,635
Total	\$6,335,635	\$6,335,635
<i>Note: A single audit fee applies to all State Fiscal Recovery Fund projects and accounts for \$1,901 of the \$6,335,635 in actual expenditures in the above table.</i>		

Key Performance Indicators: The following are the key performance indicators based on quarterly goals and monthly data collections.



1. Award construction project to a Construction Manager at Risk (CMAR)¹

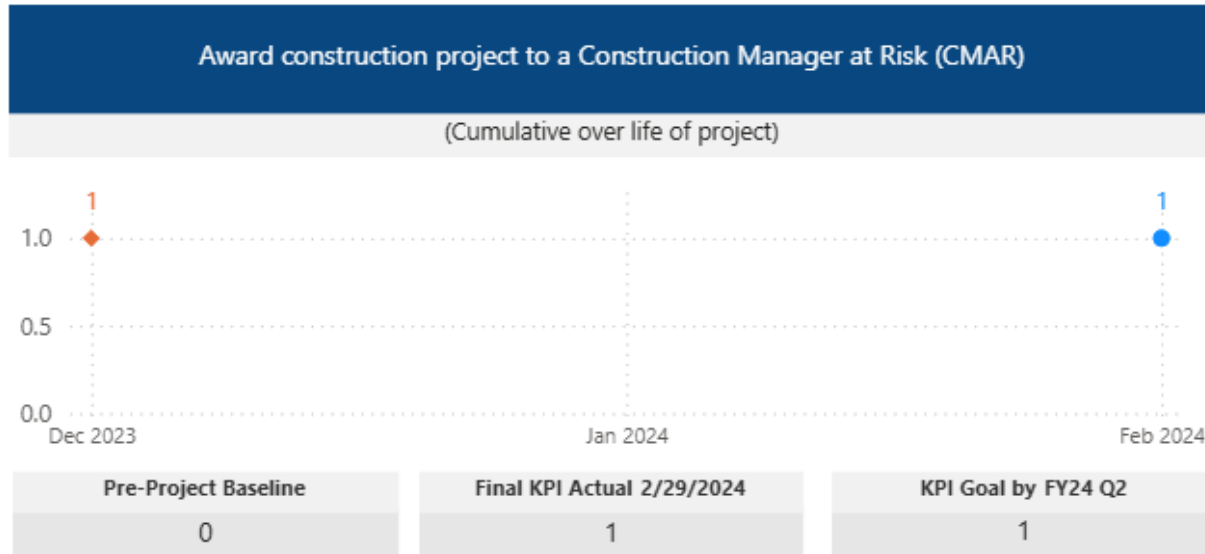

2. Award construction bid packages to trade consultants under the CMAR for construction²




¹ This is a yes/no binary indicator: 0 meaning 'no', 1 meaning 'yes'.

² This is a yes/no binary indicator: 0 meaning 'no', 1 meaning 'yes'.



3. Achieve 75% of construction completion

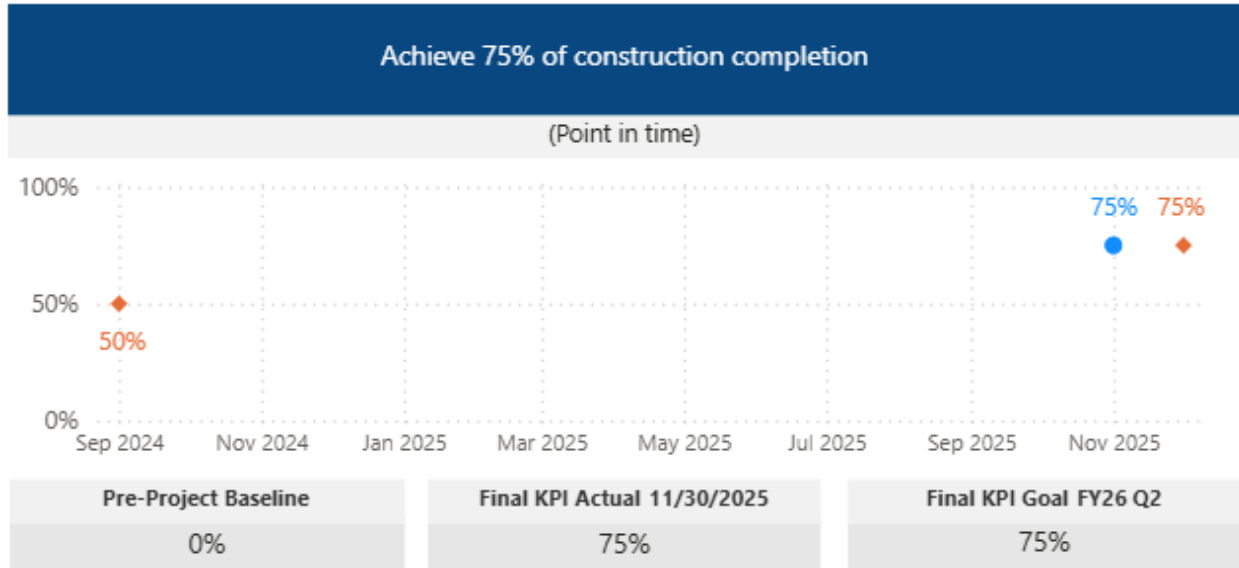

Auxiliary Information: The map below shows the location of the female youth residential facility under development.



Municipality	Sum of Funding
Exeter	\$6,333,734
Total	\$6,333,734
