



RHODE
ISLAND

Capital Projects Fund Update

Pandemic Recovery Office

FY 2026 Q4

Report Outline

- Pandemic Recovery Office Mission
- Capital Project Fund Background & Overview
- Broadband Infrastructure Projects Program Update
- Overview of Broadband Infrastructure Projects
- Community Learning Center Municipal Grant Program Update
- Overview of Community Learning Center Projects
- Overview of Community Library Municipal Grant Projects

Pandemic Recovery Office Mission

The Department of Administration's Pandemic Recovery Office (PRO) serves as the central office for policy coordination and compliance for the federal Coronavirus Capital Projects Fund (CPF), as allocated under the American Rescue Plan Act (ARPA).

The State's \$112.3 million CPF allocation, received in February 2022, can be used to fund critical capital projects that directly and jointly enable work, education, and health monitoring in response to the public health emergency.

The Capital Projects Fund aims to:

- Directly support recovery from the COVID-19 public health emergency by strengthening and improving the infrastructure necessary for participation in work, education, and health monitoring that will last beyond the pandemic.
- Enable investments in capital assets designed to address inequities in access to critical services.
- Contribute to the goal of providing every American with the modern infrastructure necessary to access critical services, including a high-quality and affordable broadband internet connection.

Background on U.S. Treasury's Capital Projects Fund

- Per U.S. Treasury's eligibility criteria, a qualifying CPF project:
 - Invests in capital assets designed to directly and jointly enable work, education, and health monitoring.
 - Is designed to address a critical need that resulted from or was made apparent or exacerbated by the COVID-19 public health emergency
 - Is designed to address a critical need of the community to be served by the capital asset
- A key priority of this program is to make funding available for reliable, affordable broadband infrastructure and other digital connectivity technology projects.
- Recipients may also use funds for multi-purpose community facilities, which provide compliant programming, and at least three private remote-access spaces
- The program encourages recipients to focus on economically distressed areas, support community empowerment, and adopt strong labor practices.


Background on Capital Projects Fund Grant Programs

- The State submitted two program plans that were subsequently approved by Treasury:
 - Broadband Infrastructure Program: \$25M approved on 3/28/2023; reduced to \$24M on 10/22/2024
 - U.S. Treasury is reviewing an allocation reduction of \$1.85M due to a decrease in scope
 - Community Learning Center (CLC) Municipal Grant Program: \$81.7M approved on 7/18/2023 ; increased to \$83.2M on 2/2/2026
 - Community Library Municipal Grant (CLMG), a subset of the CLC program: \$1M approved on 2/2/2026
 - U.S. Treasury is reviewing PRO's proposal to reallocate \$1.85M of broadband funds to CLC and CLMG projects
 - Grant Administration: \$5.6M approved on 2/4/2022; increased to \$6.6M on 10/22/2024; reduced to \$5.1M on 2/2/2026

Background on Capital Projects Fund Grant Programs

- CPF projects must reach substantial completion by 12/31/2026
 - PRO asked U.S. Treasury for an extension of the project completion deadline for the Newport Broadband Infrastructure program project on July 3, 2026
 - Extension request was granted on July 20, 2026
 - For all other projects, substantial completion is achieved on the date at which the capital asset can fulfill the primary operations that it was designed to perform, delivering services to end-users
 - PRO requires construction of all Community Learning Center projects to be complete by 10/31/2026
- Unlike the State Fiscal Recovery Fund (SFRF), CPF does not have an obligation deadline, but all expenses to be paid from CPF funds must be incurred by 12/31/2026

Broadband Infrastructure Projects Program Update




As of June 30, 2026

RI's CPF Broadband Infrastructure Projects Program

- The CPF Broadband Infrastructure Projects Program is administered by Rhode Island Commerce Corporation and is separate from the Infrastructure Investment and Jobs Act (IIJA) Broadband Equity, Access, and Deployment (BEAD) program
 - To date, three RFPs have been completed for the following areas:
 - Jamestown, Newport, and Westerly
 - **\$12.9M** was approved for award in September 2024; Subawards executed in March 2025.
 - Seven project areas with locations in Central Falls, Coventry, Cranston, Cumberland, East Providence, Exeter, Foster, Glocester, Johnston, Lincoln, Narragansett, North Kingstown, North Providence, North Smithfield, Pawtucket, Providence, Scituate, Smithfield, Warwick, West Greenwich, and Woonsocket
 - **\$6.3M** was approved for award in January 2025; Subawards executed in March 2025.
 - Portsmouth and Tiverton
 - **\$4.7M** was approved for award in February 2025; Subawards executed in March 2025.

Broadband Infrastructure Project Areas

- 26 municipalities served
- Over 16,000 locations will be enhanced through this program.

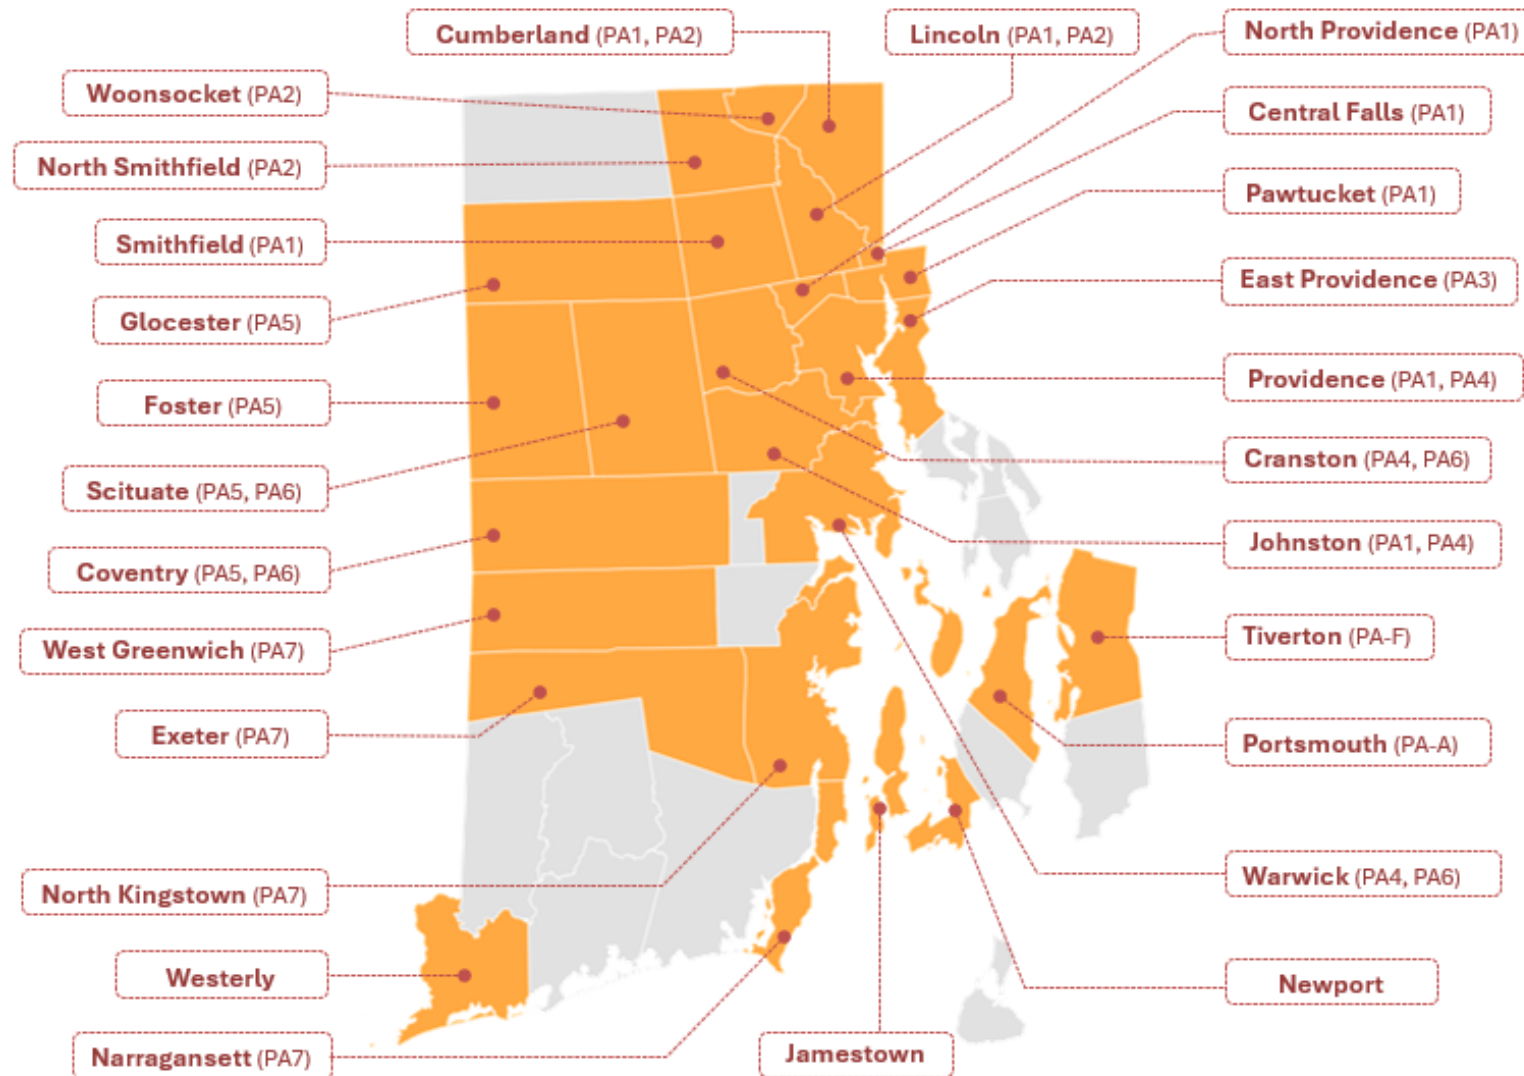

Projects and Broadband Serviceable Locations

A broadband serviceable location (BSL) is a business or residential location at which mass-market fixed broadband internet access service is, or can be, installed.

RFP Round 1 – Awarded 9/2024 – Contract Executed 3/2025 – Total BSLs: 6,676

Jamestown – 1,626

Newport – 4,621

Westerly – 429

RFP Round 2 – Awarded 1/2025 – Contract Executed 3/2025 – Total BSLs: 3,304

Project Area (PA) – 1: Central Falls, Cumberland, Johnston, Lincoln, North Providence, Pawtucket, Providence, Smithfield – 758

PA – 2: Cumberland, Lincoln, North Smithfield, Woonsocket – 523

PA – 3: East Providence – 130

PA – 4: Cranston, Johnston, Providence, Warwick – 299

PA – 5: Coventry, Foster, Glocester, Scituate – 613

PA – 6: Coventry, Cranston, Scituate, Warwick – 560

PA – 7: Exeter, Narragansett, North Kingstown, West Greenwich – 421

RFP Round 3 – Awarded 2/2025 – Contract Executed 3/2025 – Total BSLs: 6,481

PA – A: Portsmouth – 2,198

PA – F: Tiverton – 4,283

Total Number of BSLs in each project area subject to change during project implementation.

Projects and Broadband Serviceable Locations

Project Area	Total BSLs*	Business Locations	Community Anchor Institute Locations	Residential Locations†	Housing Units at Residential Locations
Jamestown	1,626	55	0	1,571	1,982
Newport	4,621	475	85	4,061	4,061
Westerly	429	64	1	364	1,018
PA-1	758	134	0	624	1,702
PA-2	523	61	0	462	1,280
PA-3	130	39	0	91	588
PA-4	299	167	3	129	888
PA-5	613	30	0	583	640
PA-6	560	47	1	512	1,159
PA-7	421	102	1	318	705
PA-A	2,198	115	2	2,081	2,839
PA-F	4,283	299	0	3,984	5,789
Total	16,461	1,588	93	14,780	22,651

*Total Number of BSLs in each project area subject to change during project implementation.

† A residential location is defined by the FCC as a location that is or contains “housing units” or “group quarters” based on the U.S. Census Bureau

Project Area: Jamestown

Data as of FY2026 Q4

CPF award: **\$2,071,245**

Internet Service Provider (ISP) match: **\$2,278,669**


Total Project Cost: **\$4,349,914**

Project is funded through CPF, 48%, & ISP Match, 52%

	Planned	Total to Date
Miles of Fiber	44	47.4
Eligible BSLs Served	1,626	1,514

Start Date: **6/1/2025**

Completion Date: **7/31/2026**



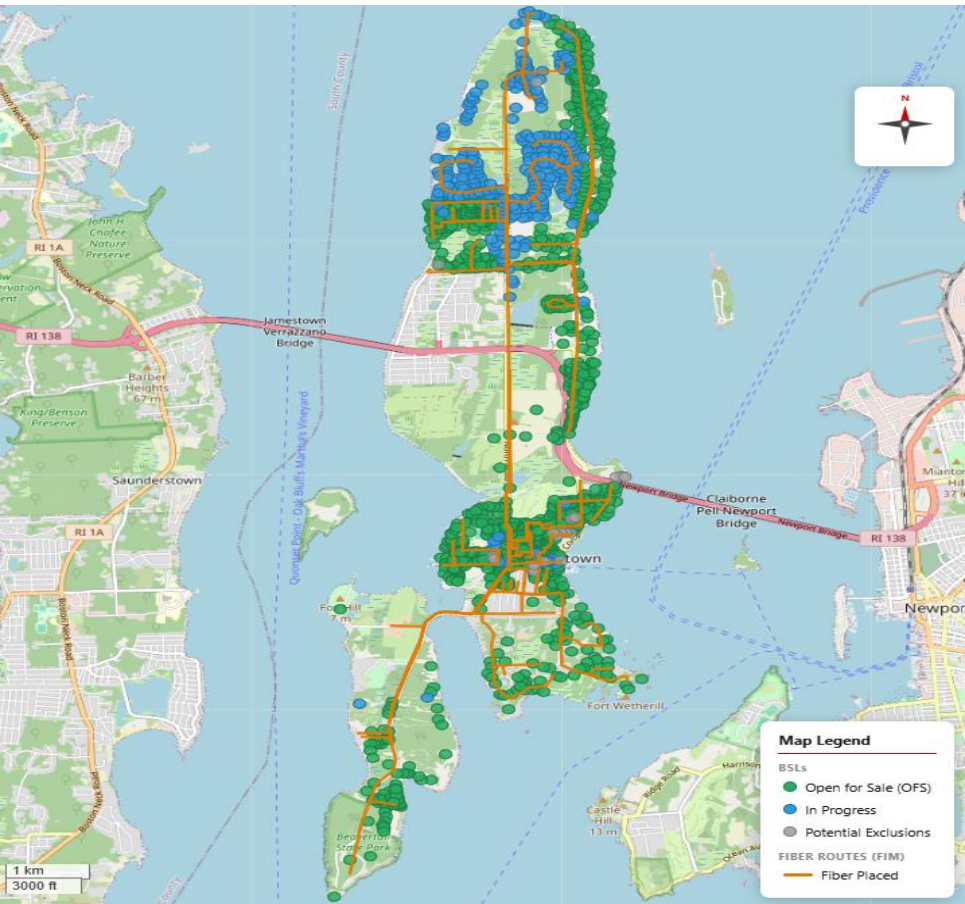


ISP: **Verizon New England, Inc.**

Communities Served: **Jamestown**

Project Area: Jamestown

Data as of FY2026 Q4

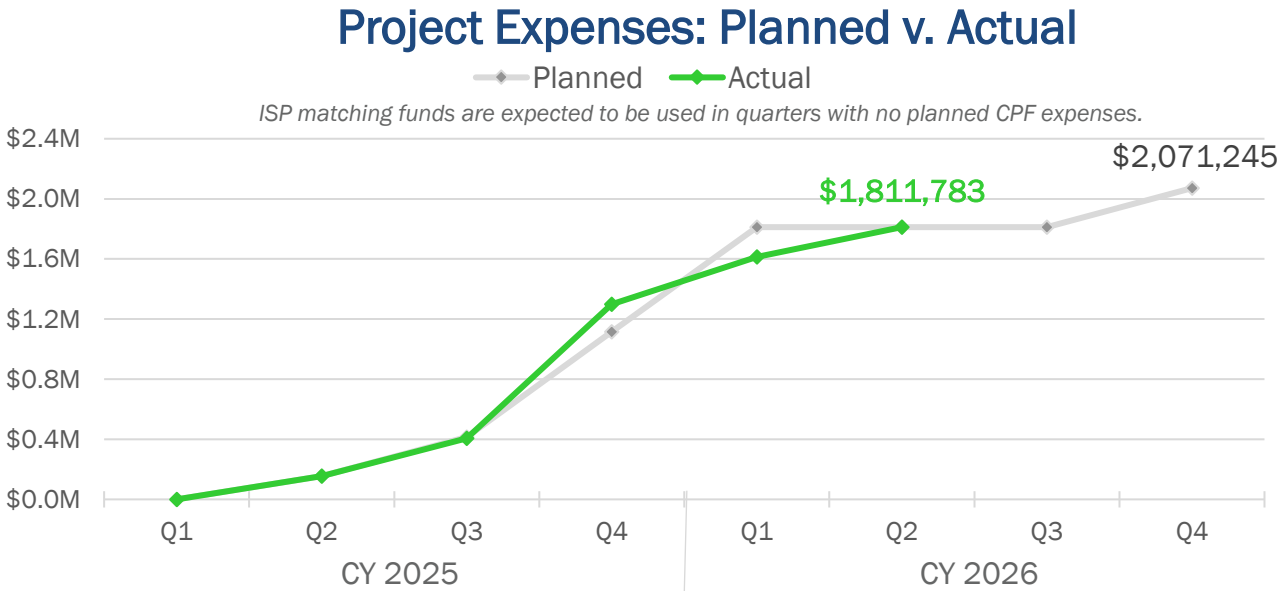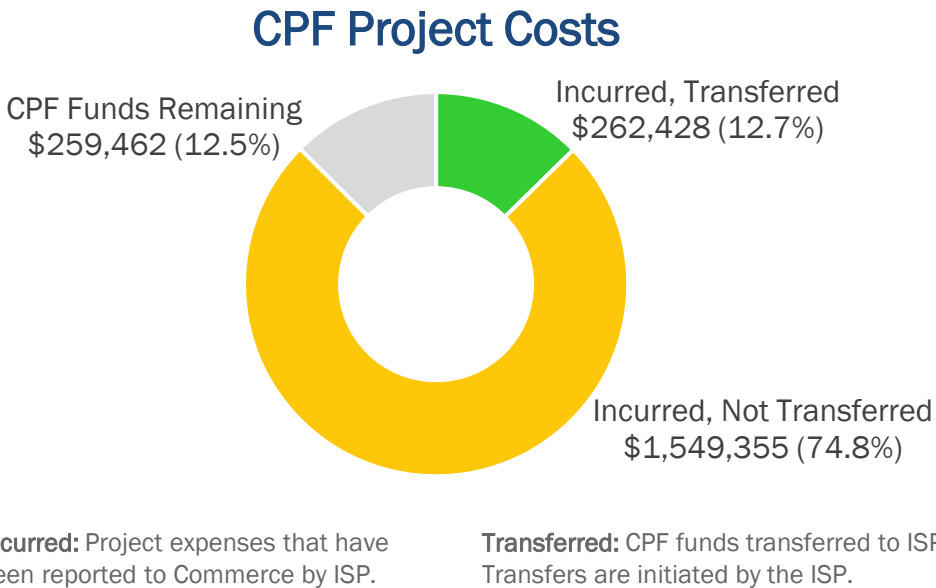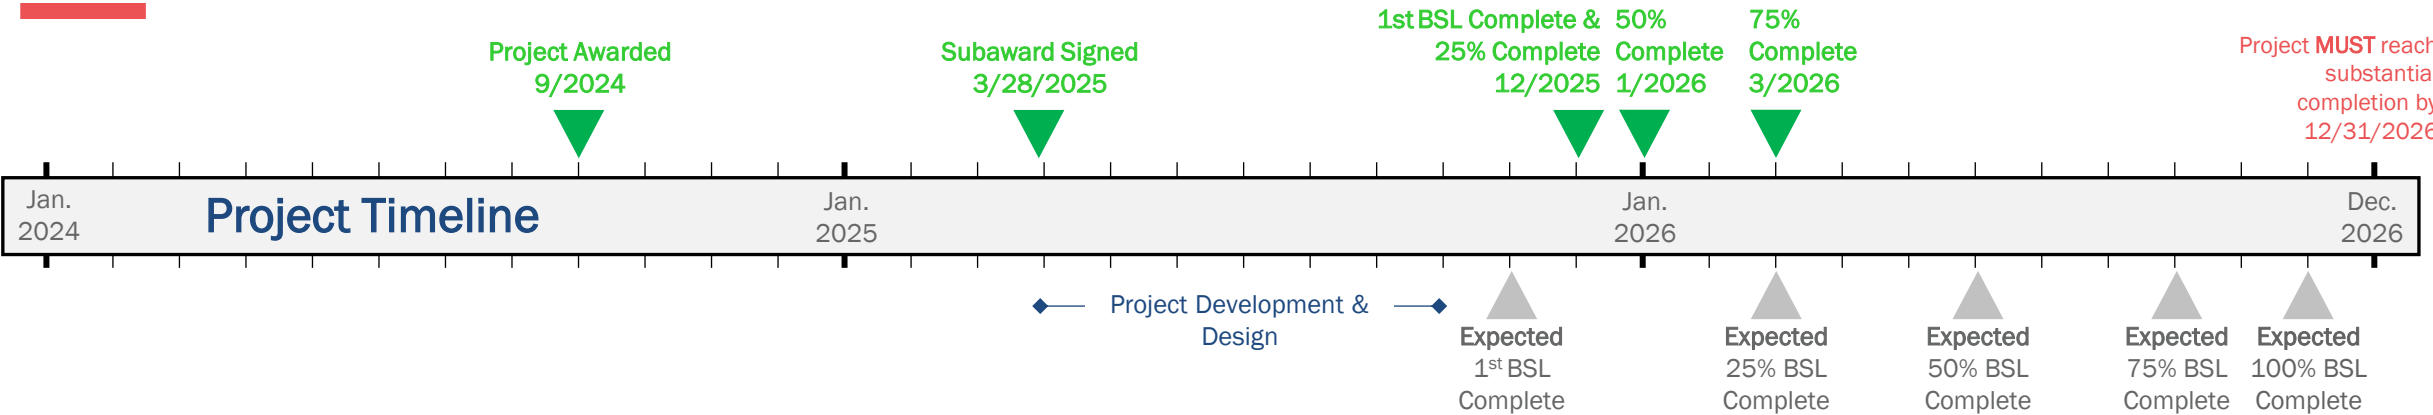

Project Area: Newport

Data as of FY2026 Q4

CPF award: **\$9,308,052**

Internet Service Provider (ISP) match: **\$3,989,165**


Total Project Cost: **\$13,297,217**

Project is funded through CPF, 70%, & ISP Match, 30%

	Planned	Total to Date
Miles of Fiber	83	0
Eligible BSLs Served	4,621	0

Start Date: **9/15/2025**

Completion Date: **11/15/2026**



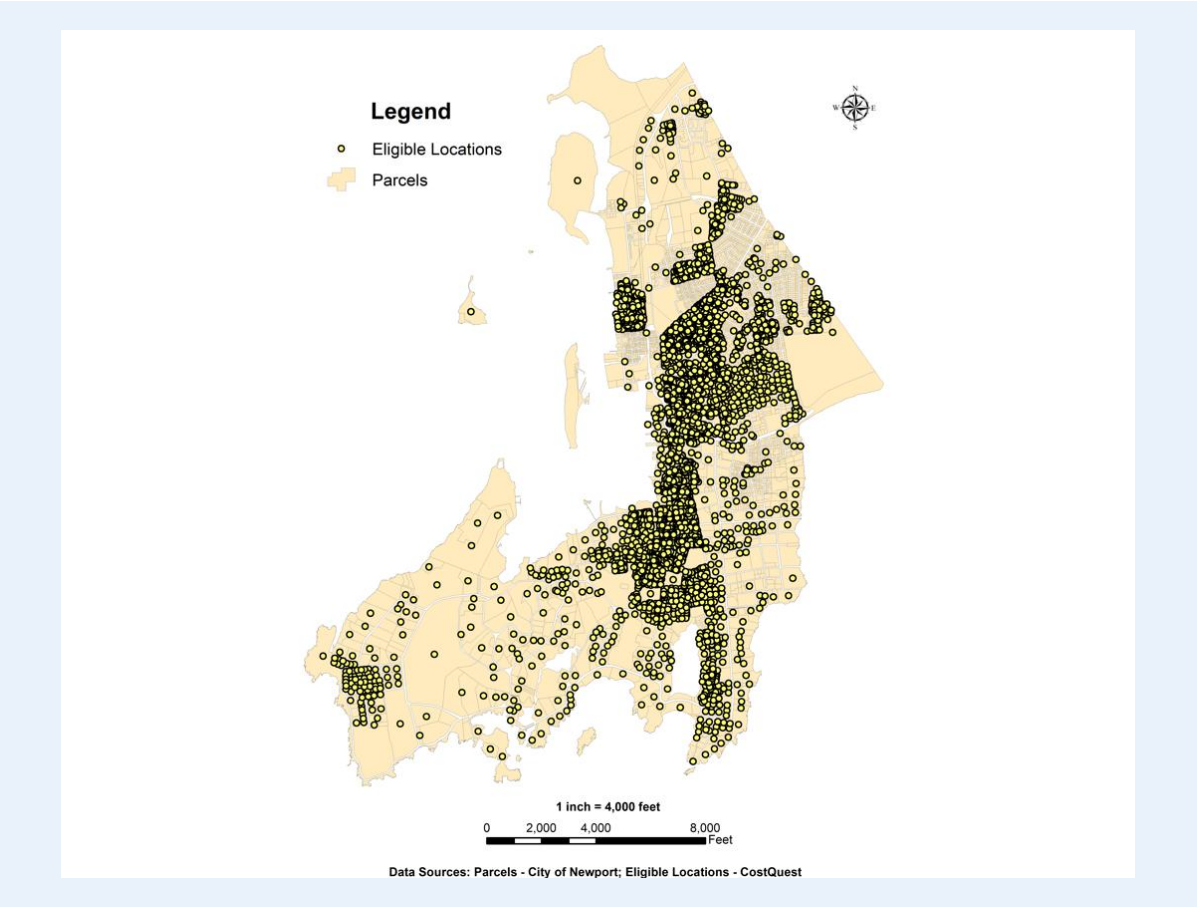


ISP: **GoNetspeed**

Communities Served: **Newport**

Project Area: Newport

Data as of FY2026 Q4

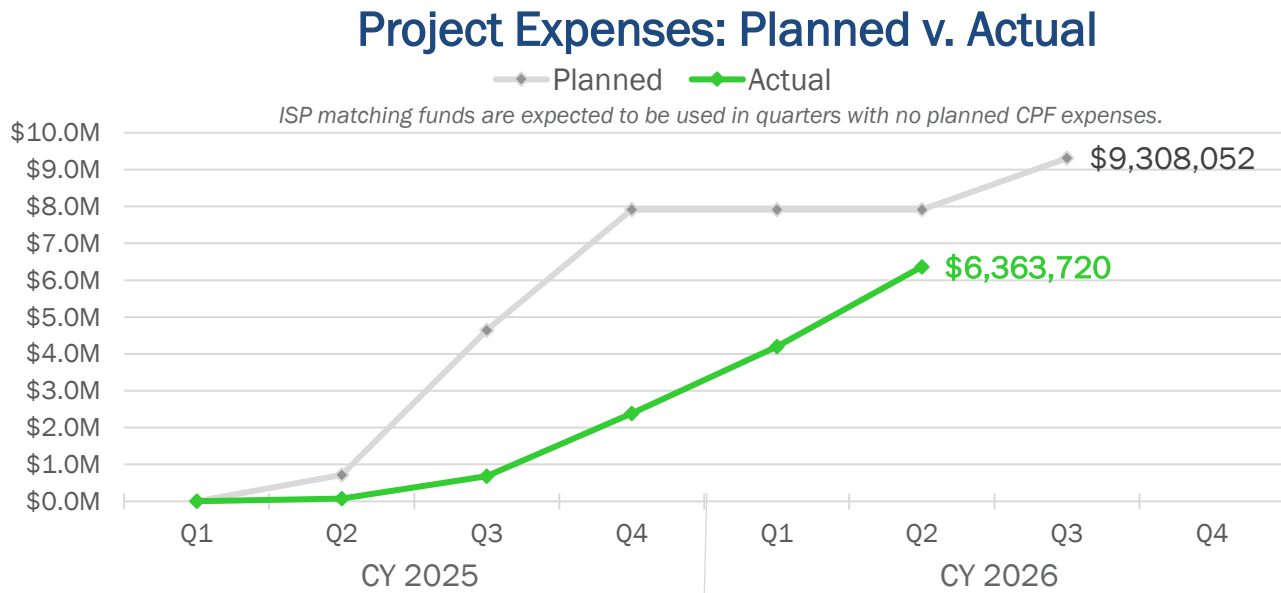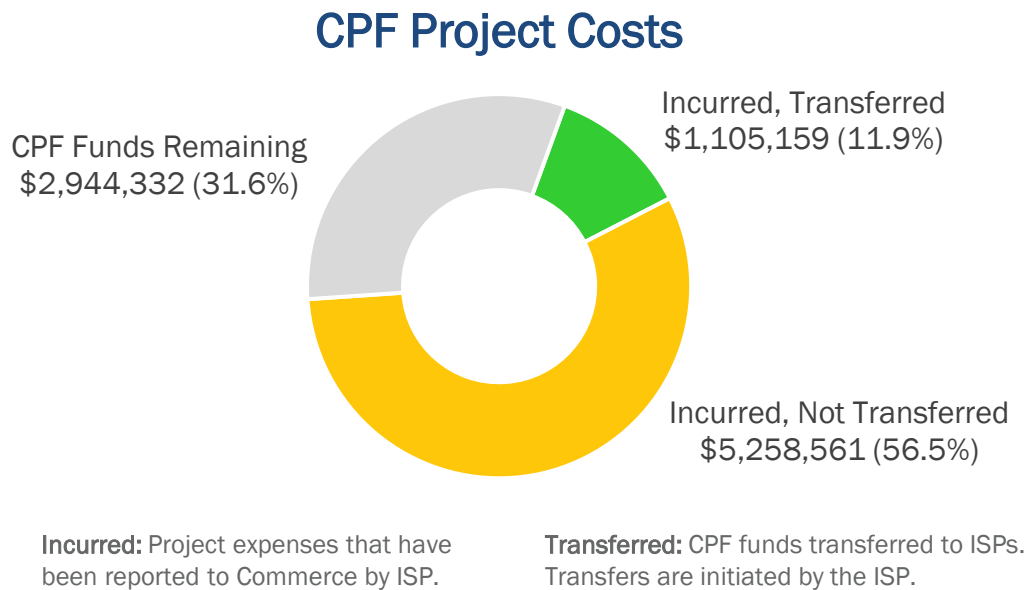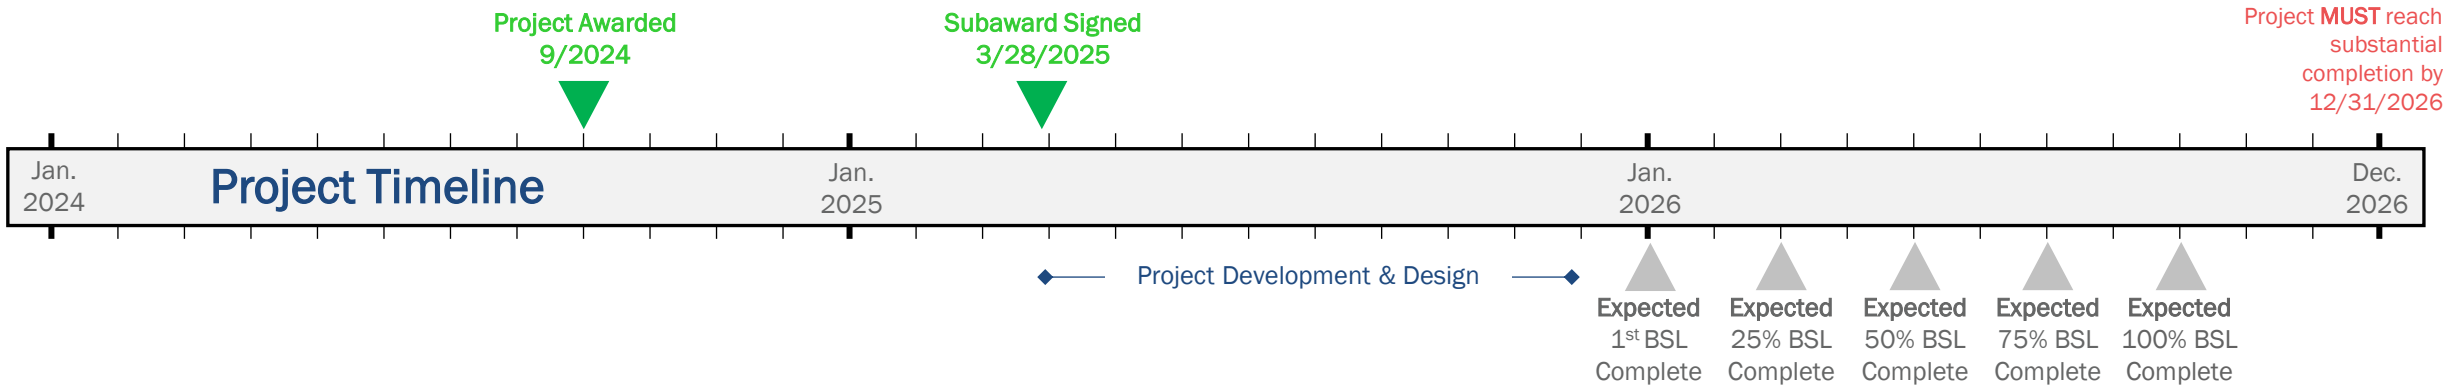

Project Area: Westerly

Data as of FY2026 Q4

CPF award: **\$1,564,635**

Internet Service Provider (ISP) match: **\$907,055**


Total Project Cost: **\$2,471,690**

Project is funded through CPF, 63%, & ISP Match, 37%

	Planned	Total to Date
Miles of Fiber	10	0.65
Eligible BSLs Served	429	136

Start Date: **2/26/2026**

Completion Date: **8/31/2026**



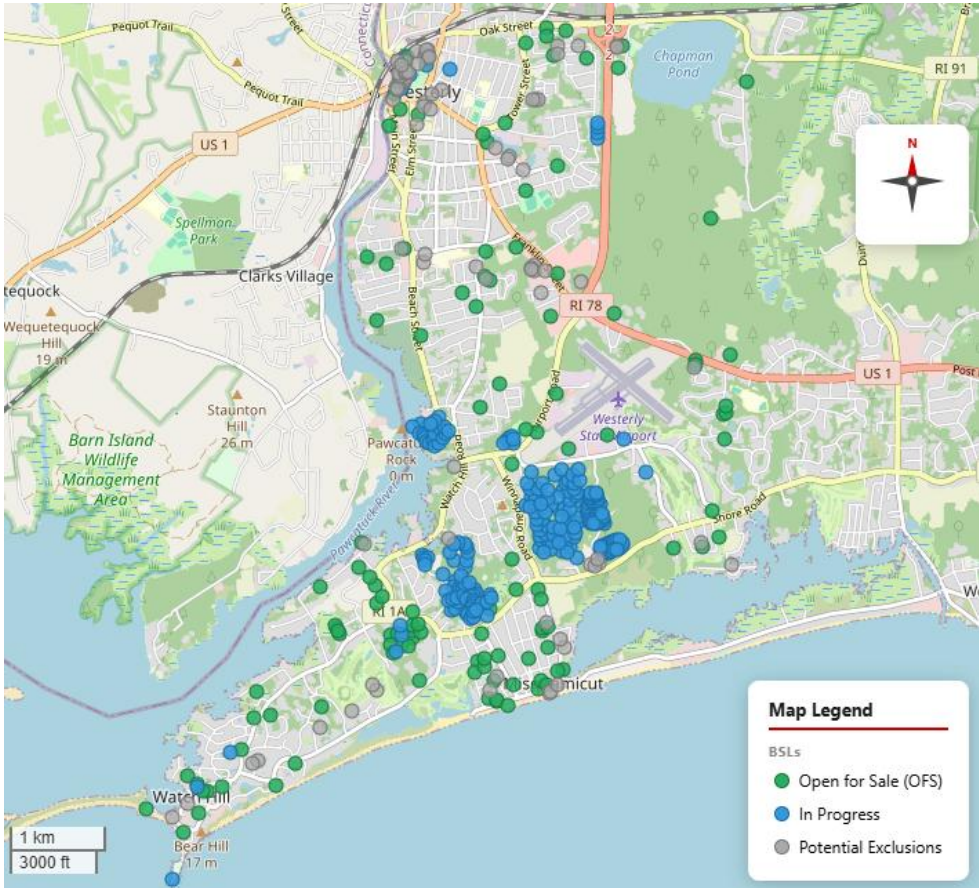


ISP: **Verizon New England, Inc.**

Communities Served: **Westerly**

Project Area: Westerly

Data as of FY2026 Q4

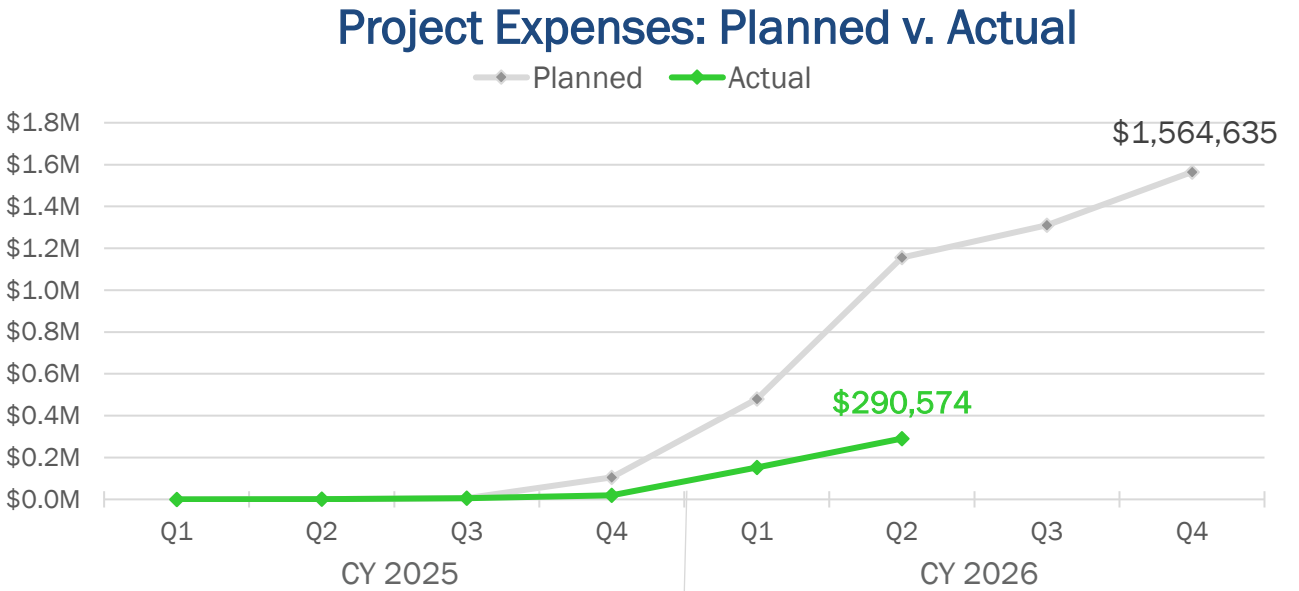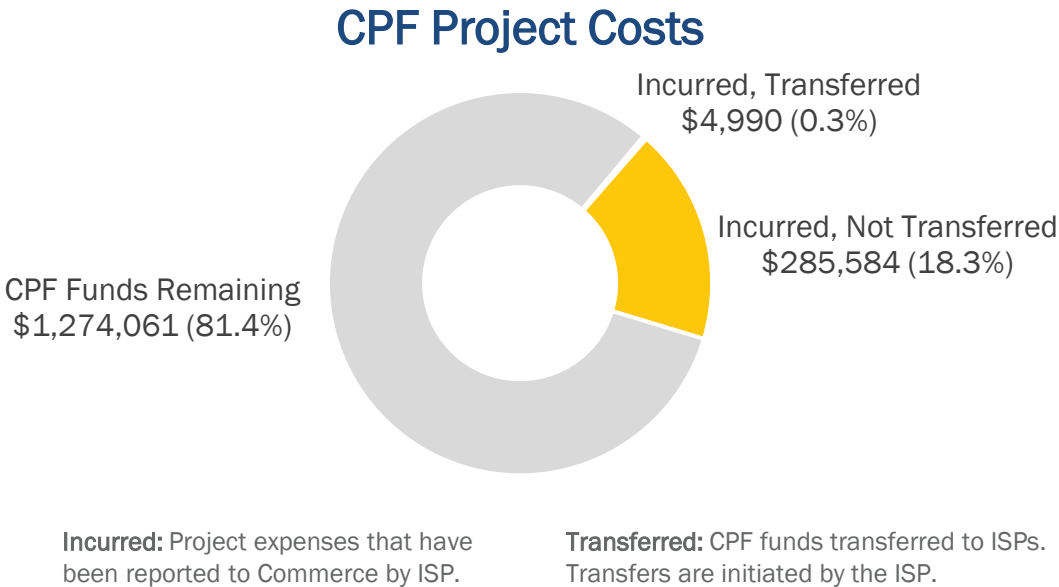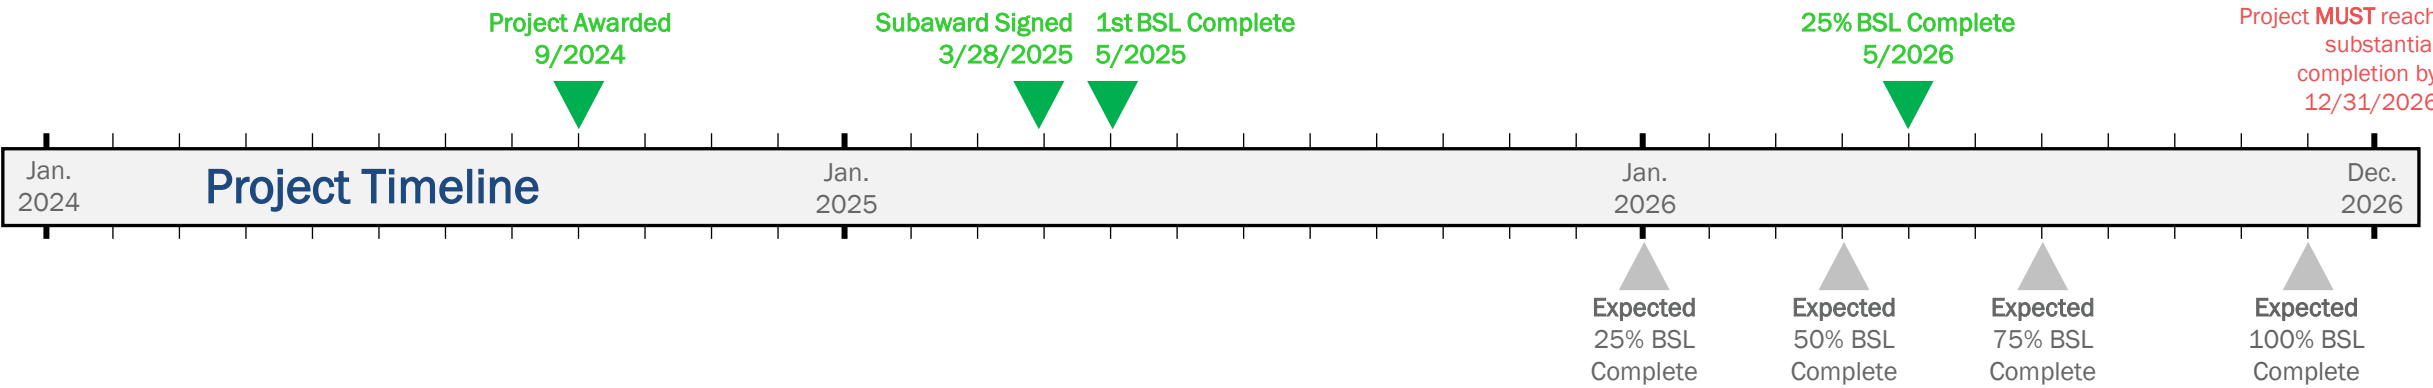

Project Area: PA-1

CPF award: **\$1,560,759**

Internet Service Provider (ISP) match: **\$2,544,116**


Total Project Cost: **\$4,104,875**

Project is funded through CPF, 38%, & ISP Match, 62%

	Planned	Total to Date
Miles of Fiber	45	1.49
Eligible BSLs Served	758	151

Start Date: **1/13/2026**

Completion Date: **9/30/2026**

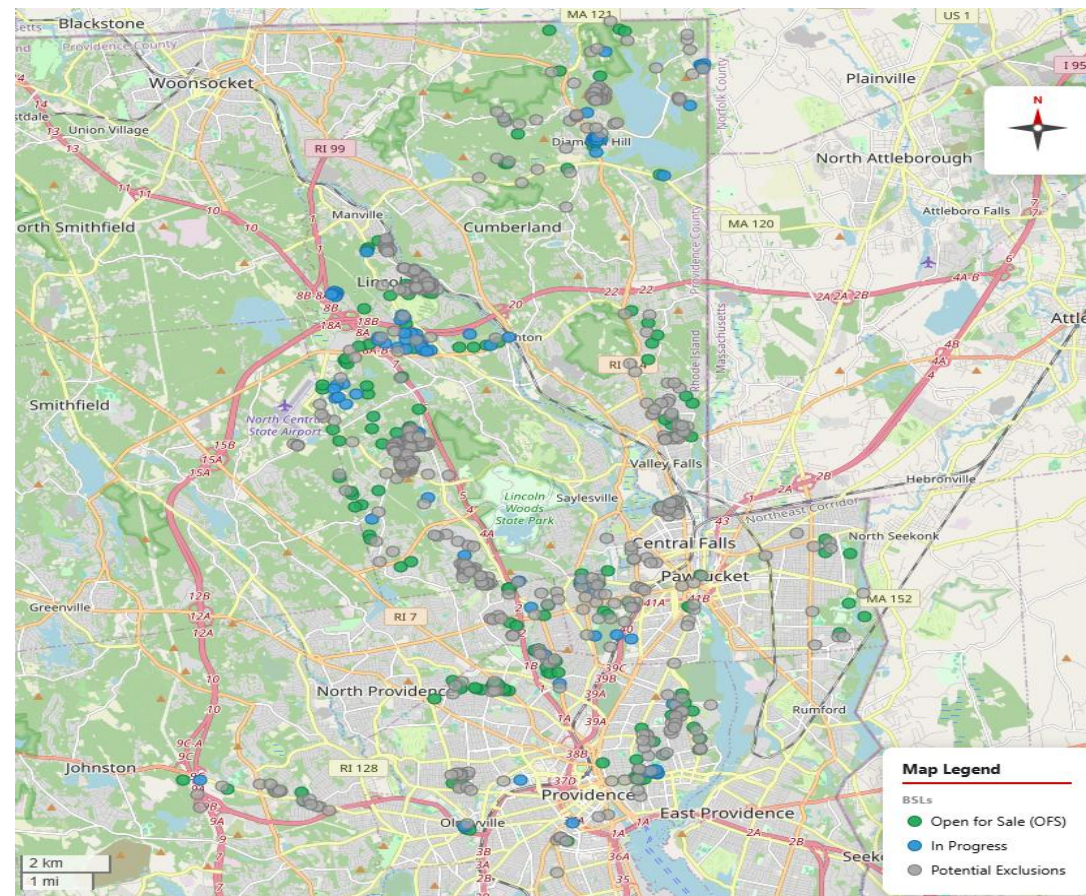


ISP: **Verizon New England, Inc.**


Communities Served: **Central Falls, Cumberland, Johnston, Lincoln, North Providence, Pawtucket, Providence, Smithfield**

Project Area: PA-1


Data as of FY2026 Q4

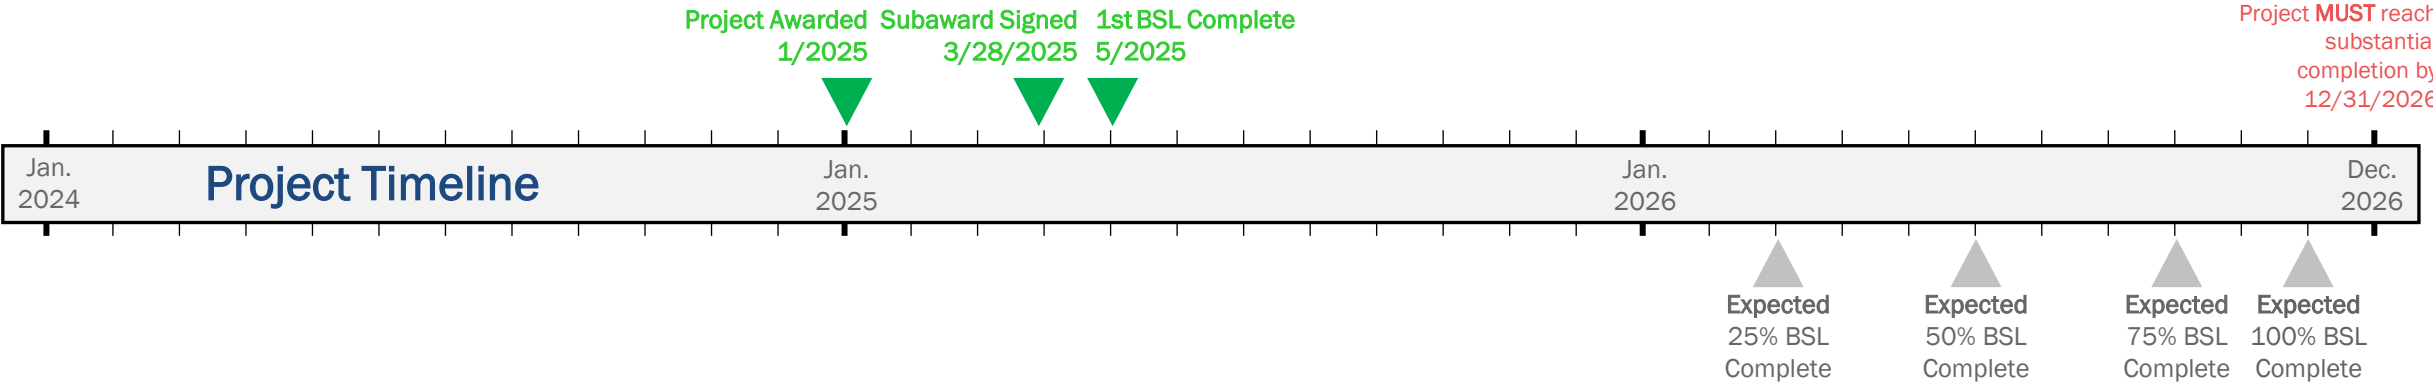

CPF Project Costs

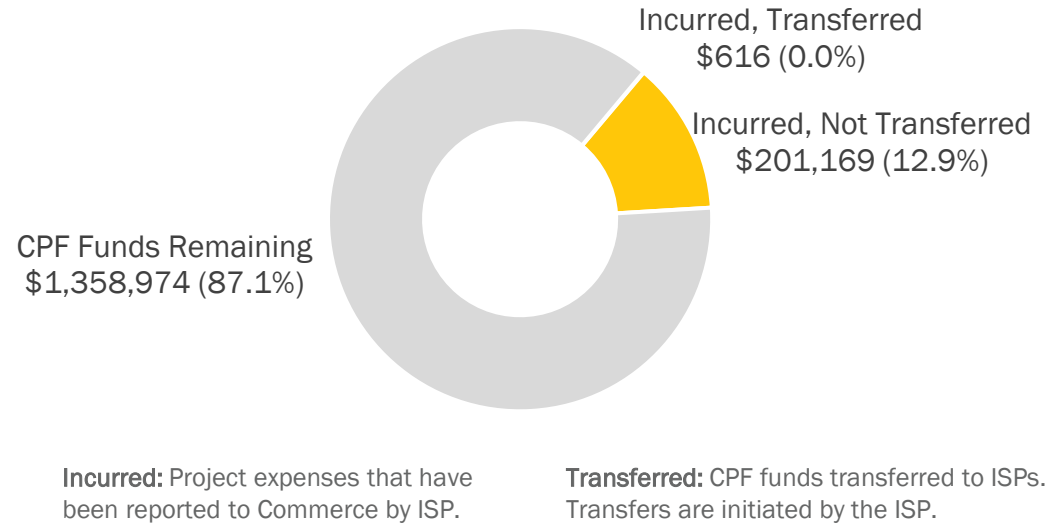

Project Expenses: Planned v. Actual

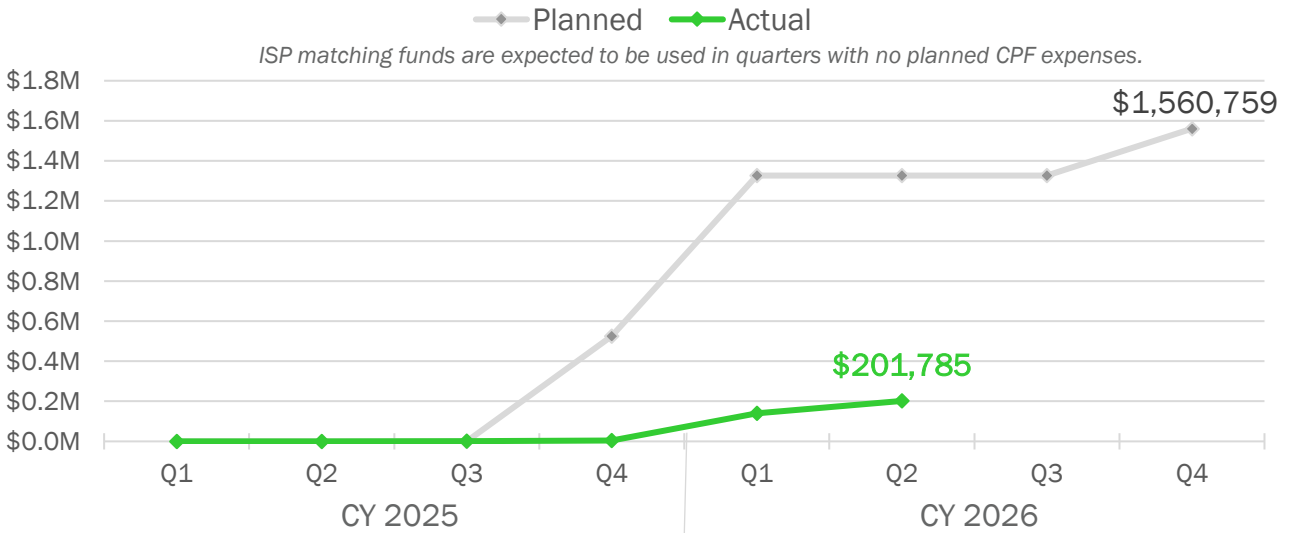

Project Area: PA-2

Data as of FY2026 Q4

CPF award: **\$1,150,928**

Internet Service Provider (ISP) match: **\$1,902,196**


Total Project Cost: **\$3,053,124**

Project is funded through CPF, 38%, & ISP Match, 62%

	Planned	Total to Date
Miles of Fiber	26	1.67
Eligible BSLs Served	523	80

Start Date: **8/4/2025**

Completion Date: **9/30/2026**

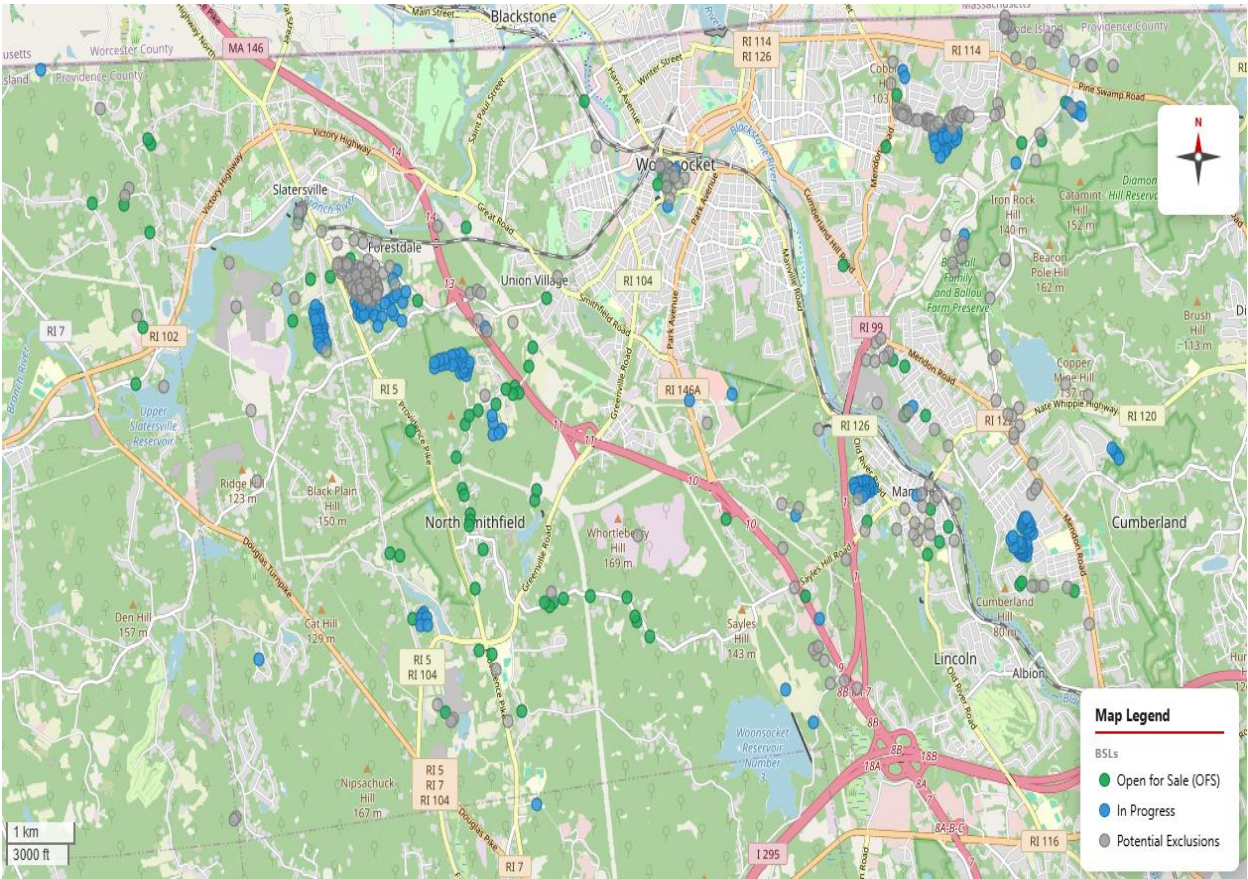


ISP: **Verizon New England, Inc.**


Communities Served: **Cumberland, Lincoln, North Smithfield, Woonsocket**

Project Area: PA-2

Data as of FY2026 Q4

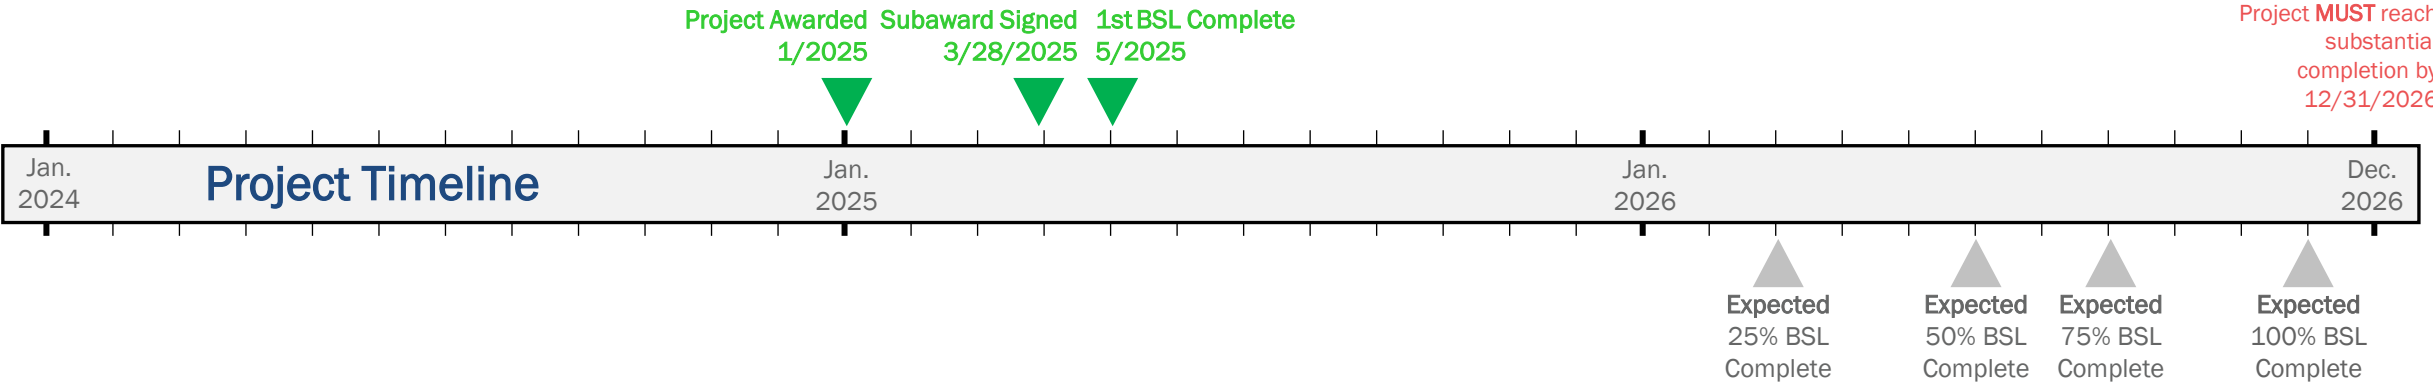


CPF Project Costs

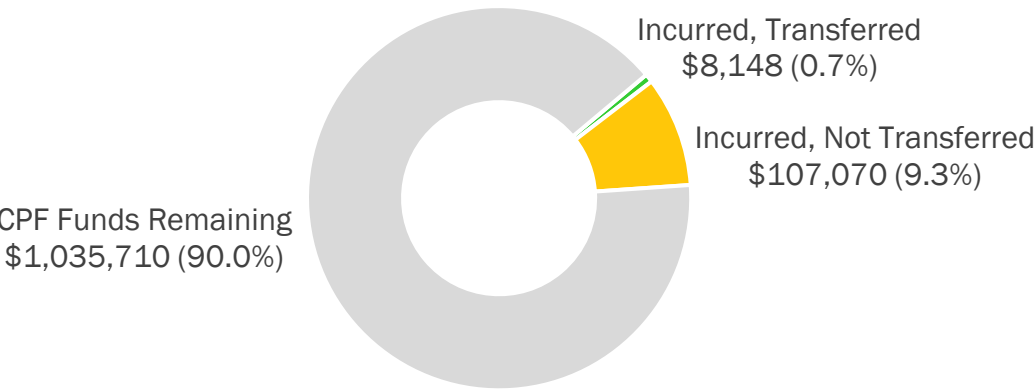

Incurred: Project expenses that have been reported to Commerce by ISP.

Transferred: CPF funds transferred to ISPs. Transfers are initiated by the ISP.

Project Expenses: Planned v. Actual

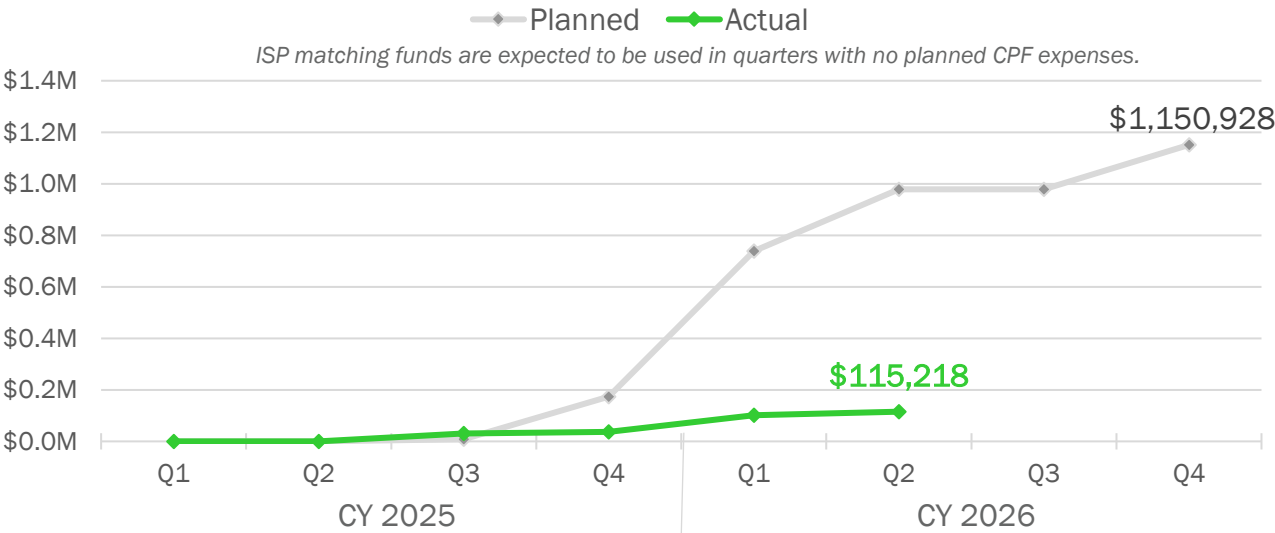

Project Area: PA-3

Data as of FY2026 Q4

CPF award: **\$474,282**

Internet Service Provider (ISP) match: **\$710,310**


Total Project Cost: **\$1,184,592**

Project is funded through CPF, 40%, & ISP Match, 60%

	Planned	Total to Date
Miles of Fiber	6.5	0
Eligible BSLs Served	130	28

Start Date: **1/29/2026**




Completion Date: **9/30/2026**

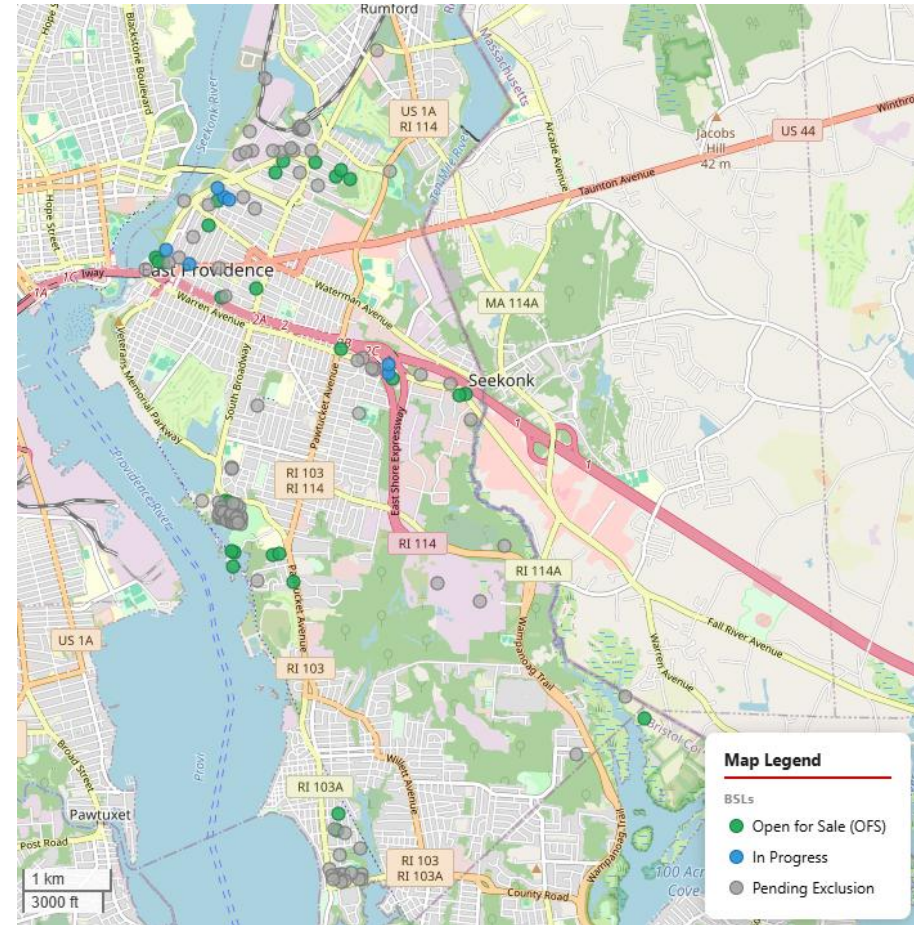

ISP: **Verizon New England, Inc.**

Communities Served: **East Providence**

Project Area: PA-3

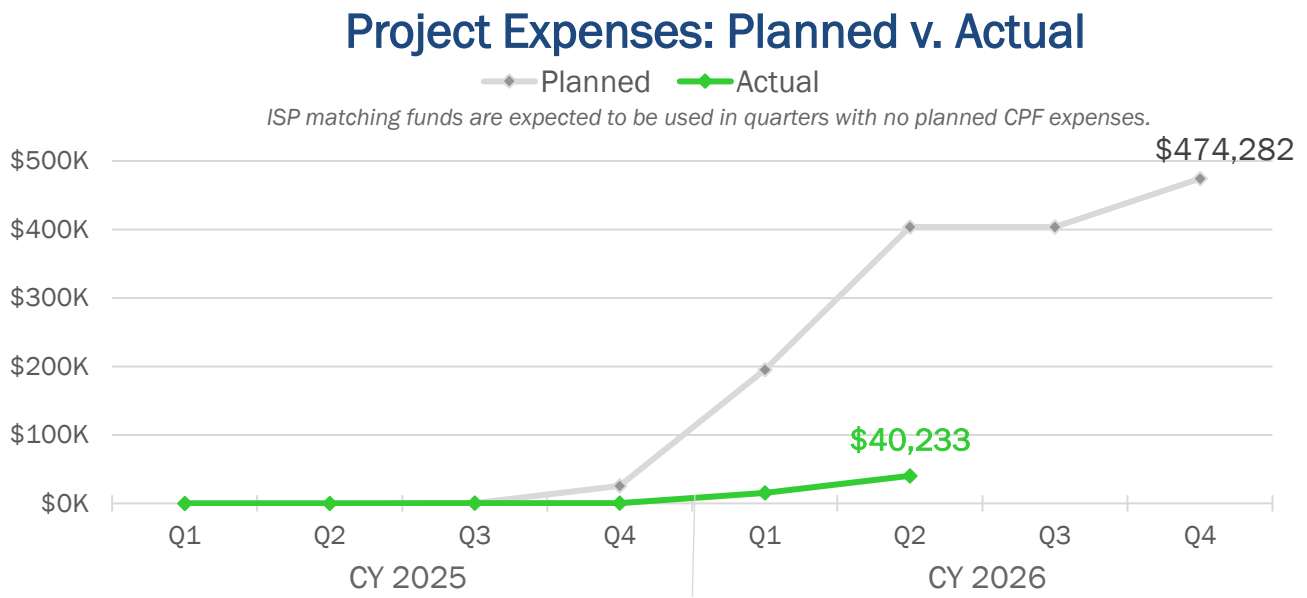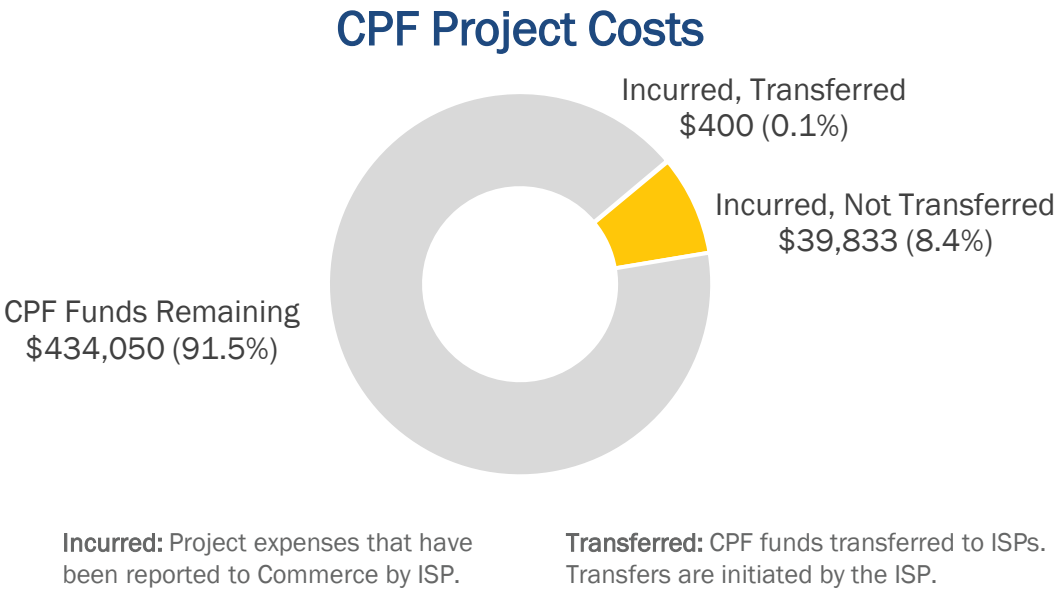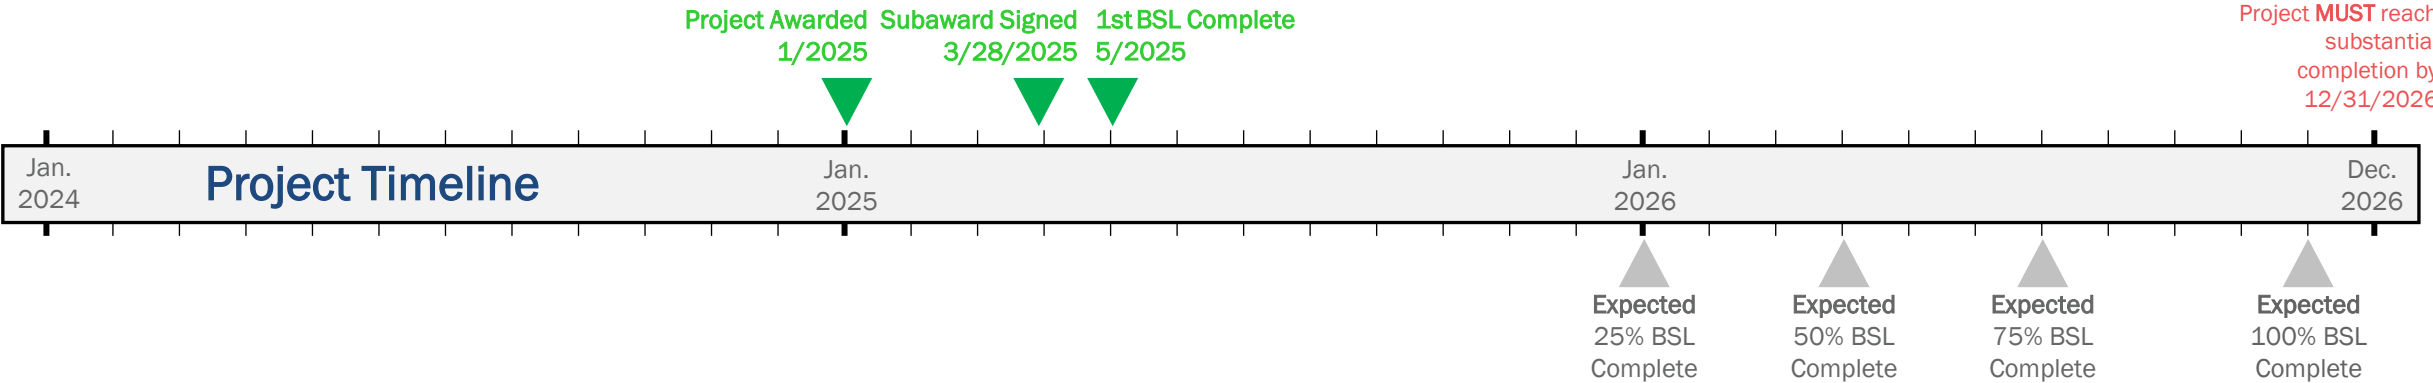

Project Area: PA-4

Data as of FY2026 Q4

CPF award: **\$935,498**

Internet Service Provider (ISP) match: **\$1,560,135**


Total Project Cost: **\$2,495,633**

Project is funded through CPF, 38%, & ISP Match, 62%

	Planned	Total to Date
Miles of Fiber	27	0
Eligible BSLs Served	299	48

Start Date: **1/20/2026**

Completion Date: **9/30/2026**



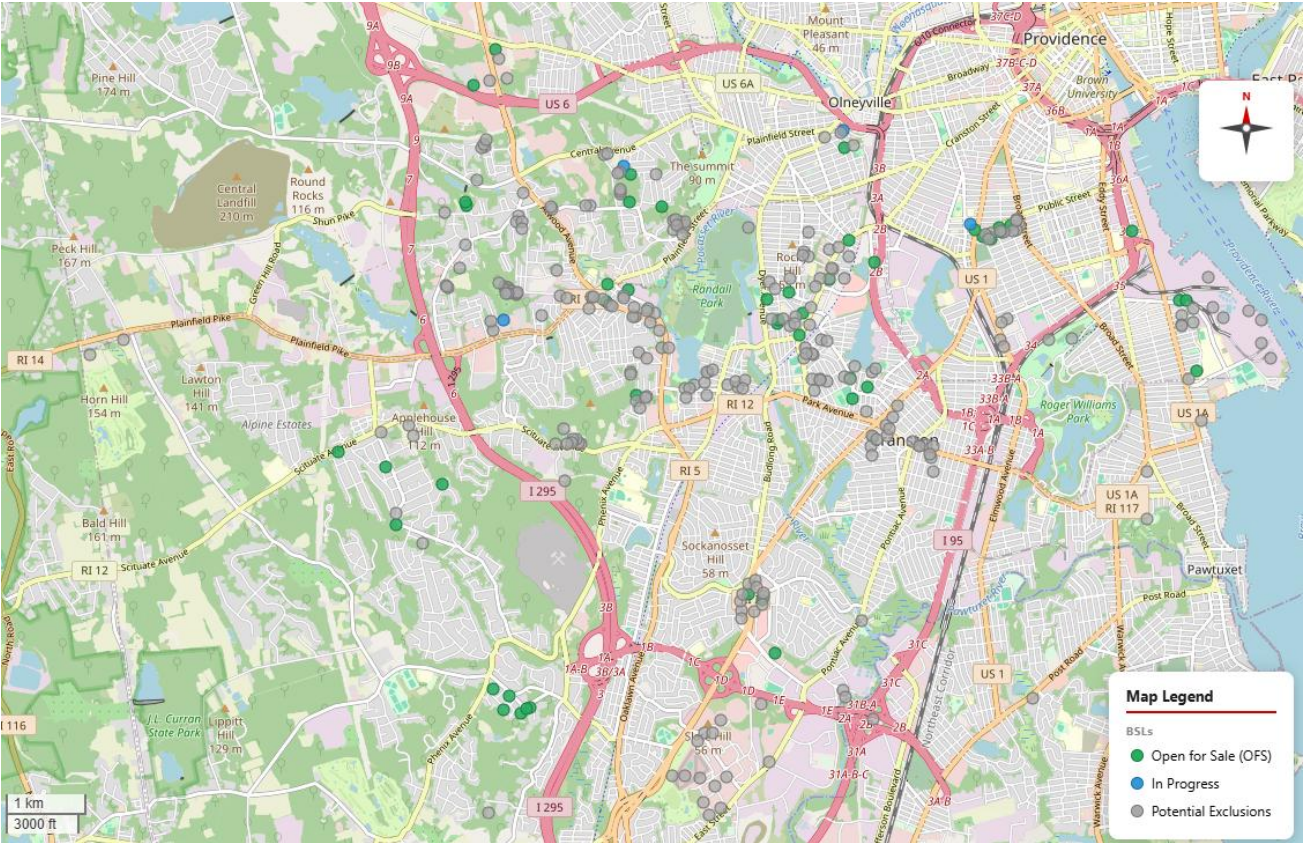


ISP: **Verizon New England, Inc.**

Communities Served: **Cranston, Johnston, Providence, Warwick**

Project Area: PA-4

Data as of FY2026 Q4

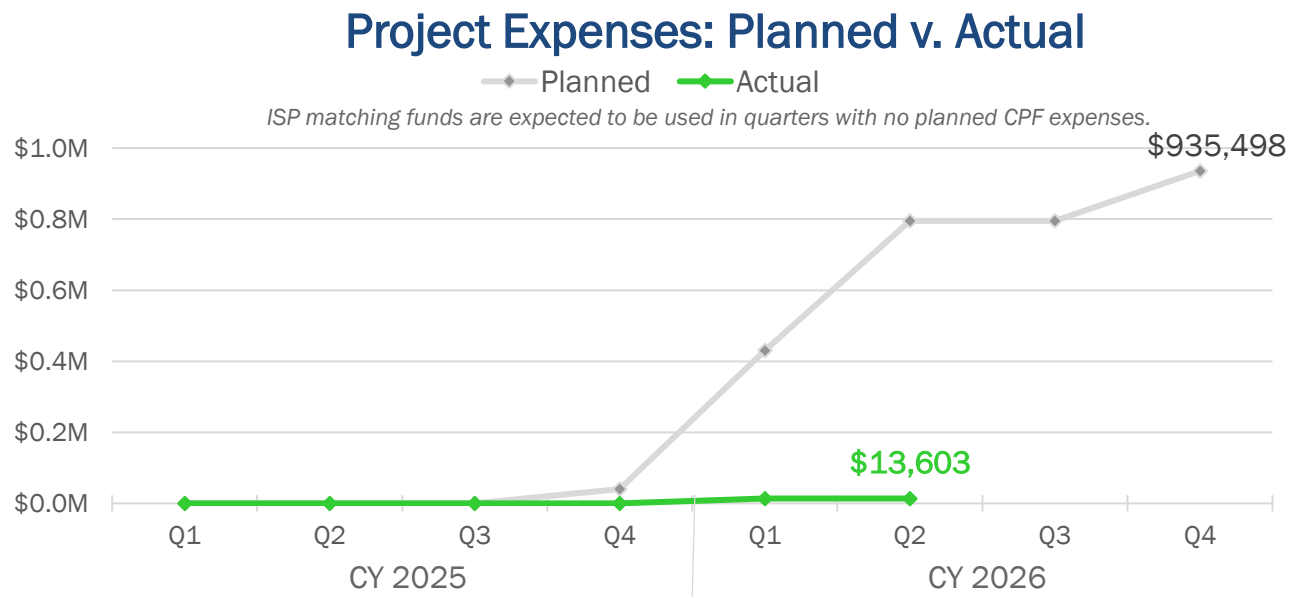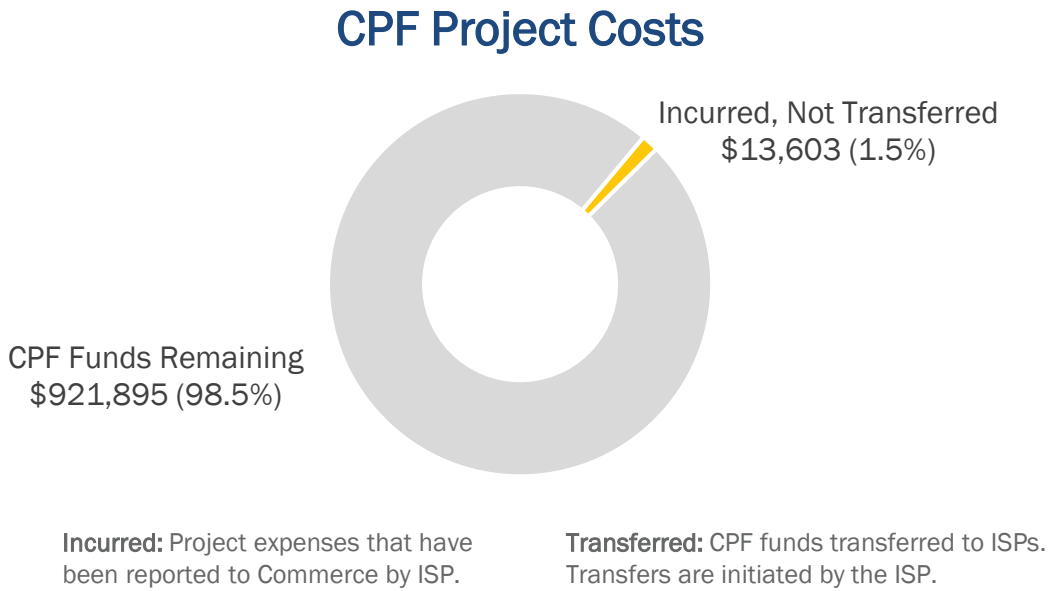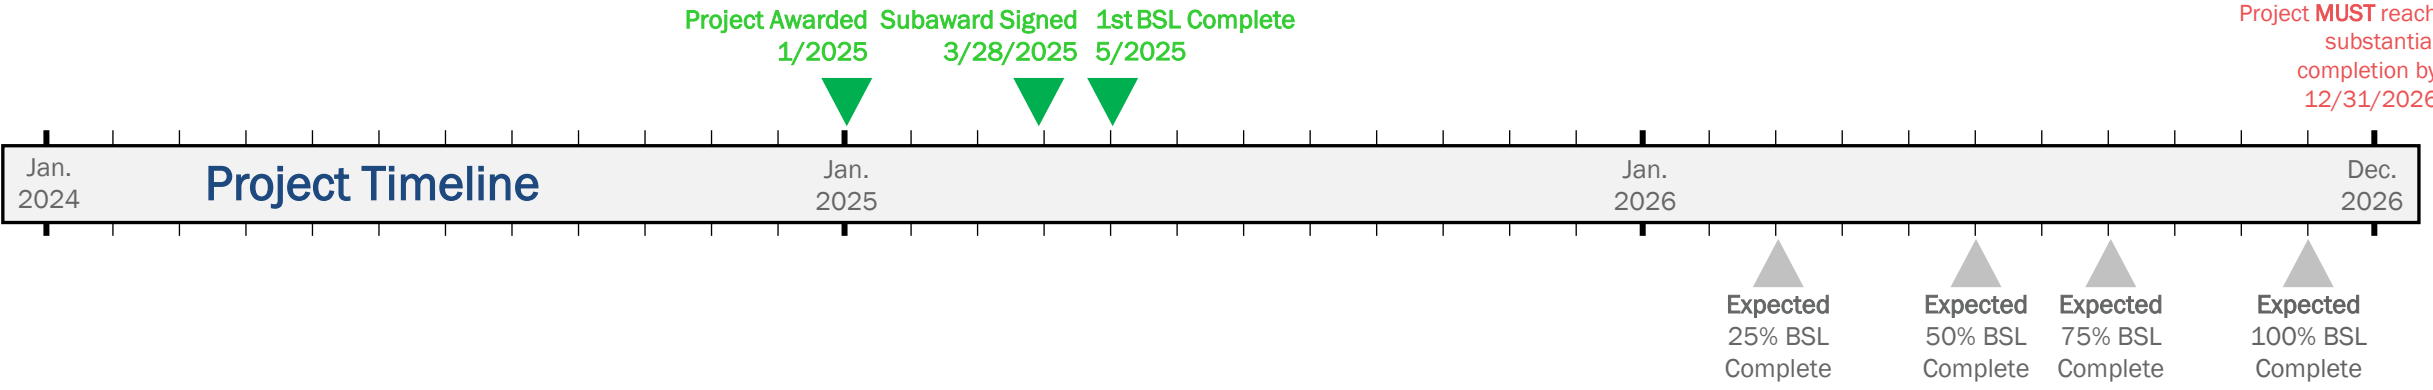

Project Area: PA-5

Data as of FY2026 Q4

CPF award: **\$635,659**

Internet Service Provider (ISP) match: **\$1,142,646**


Total Project Cost: **\$1,778,305**

Project is funded through CPF, 36%, & ISP Match, 64%

	Planned	Total to Date
Miles of Fiber	32	0
Eligible BSLs Served	613	44

Start Date: **12/2/2025**

Completion Date: **9/30/2026**



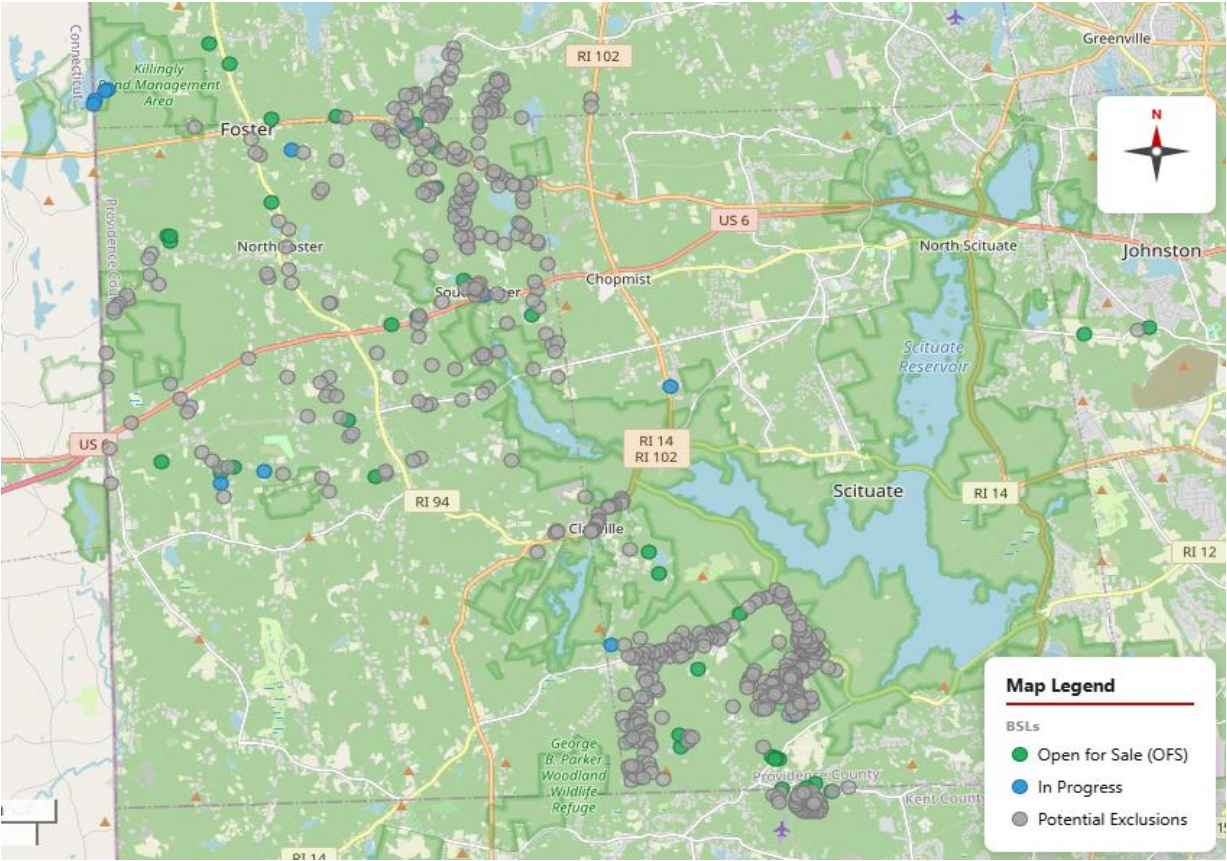


ISP: **Verizon New England, Inc.**

Communities Served: **Coventry, Foster, Glocester, Scituate**

Project Area: PA-5

Data as of FY2026 Q4

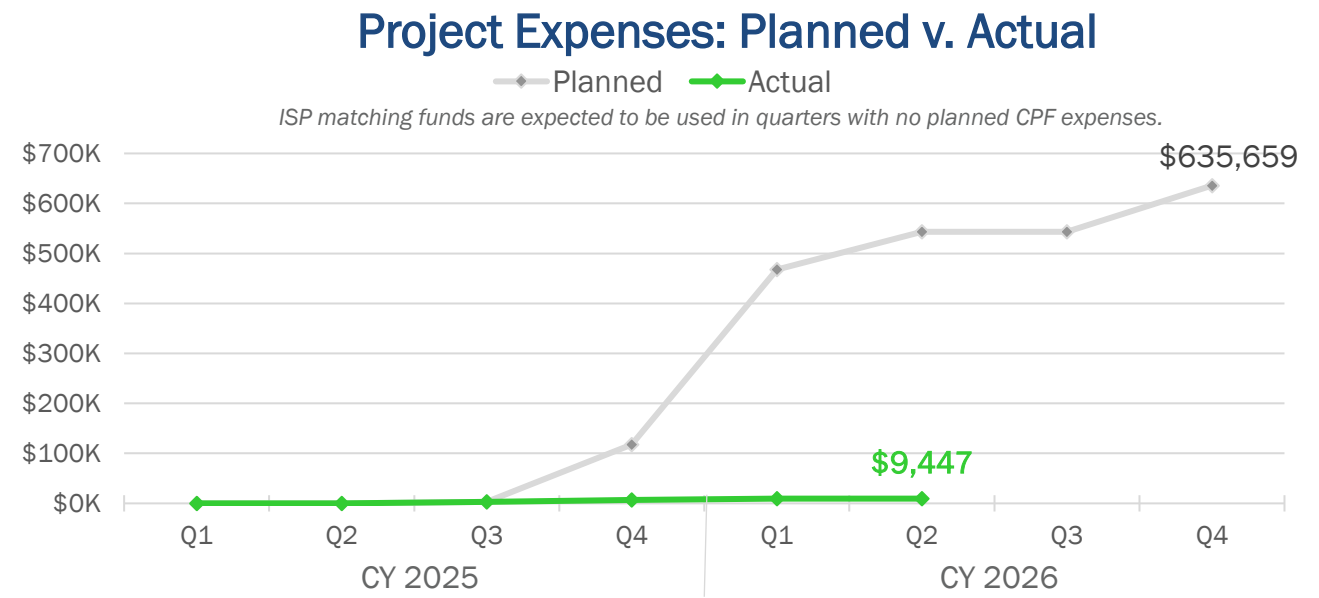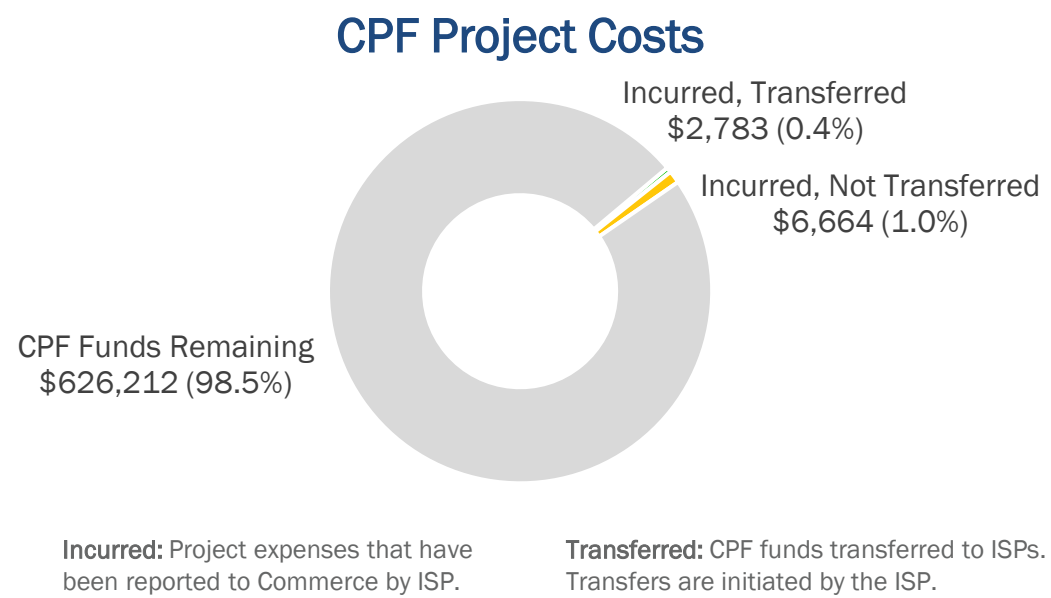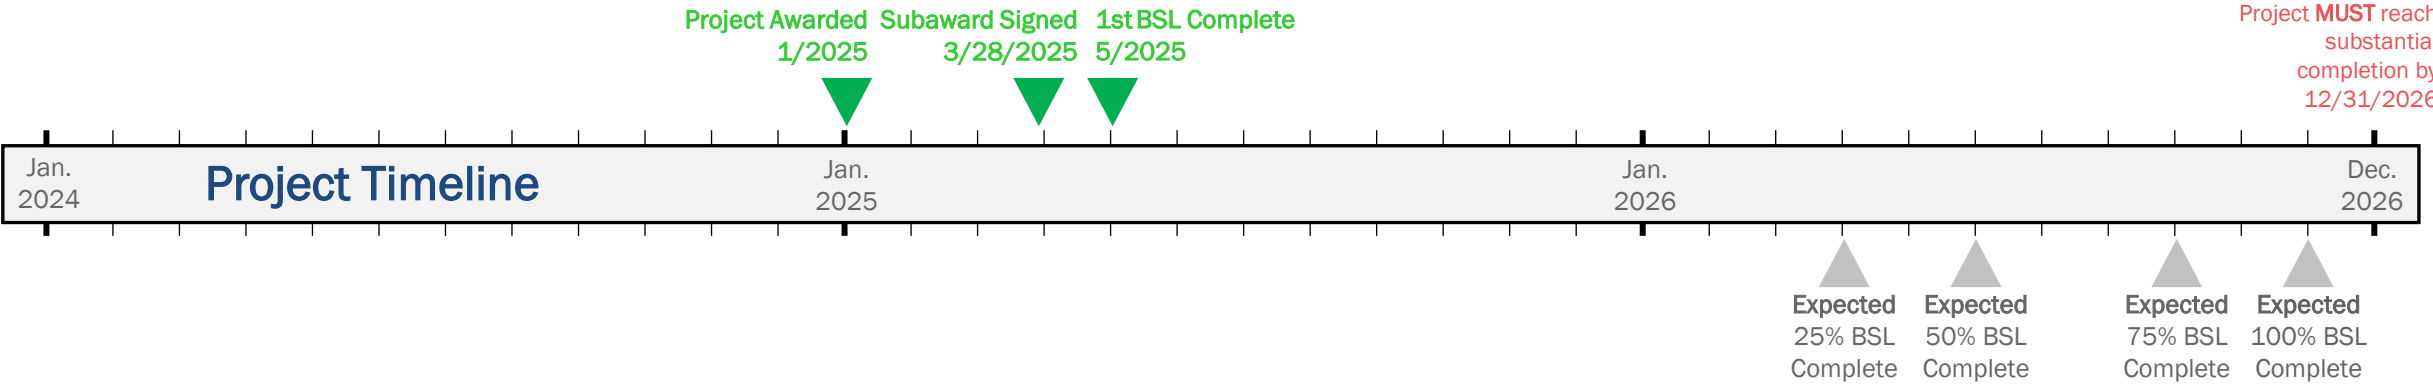

Project Area: PA-6

Data as of FY2026 Q4

CPF award: **\$727,579**

Internet Service Provider (ISP) match: **\$1,181,395**


Total Project Cost: **\$1,908,974**

Project is funded through CPF, 38%, & ISP Match, 62%

	Planned	Total to Date
Miles of Fiber	18	0.6
Eligible BSLs Served	560	77

Start Date: **1/9/2026**

Completion Date: **9/30/2026**



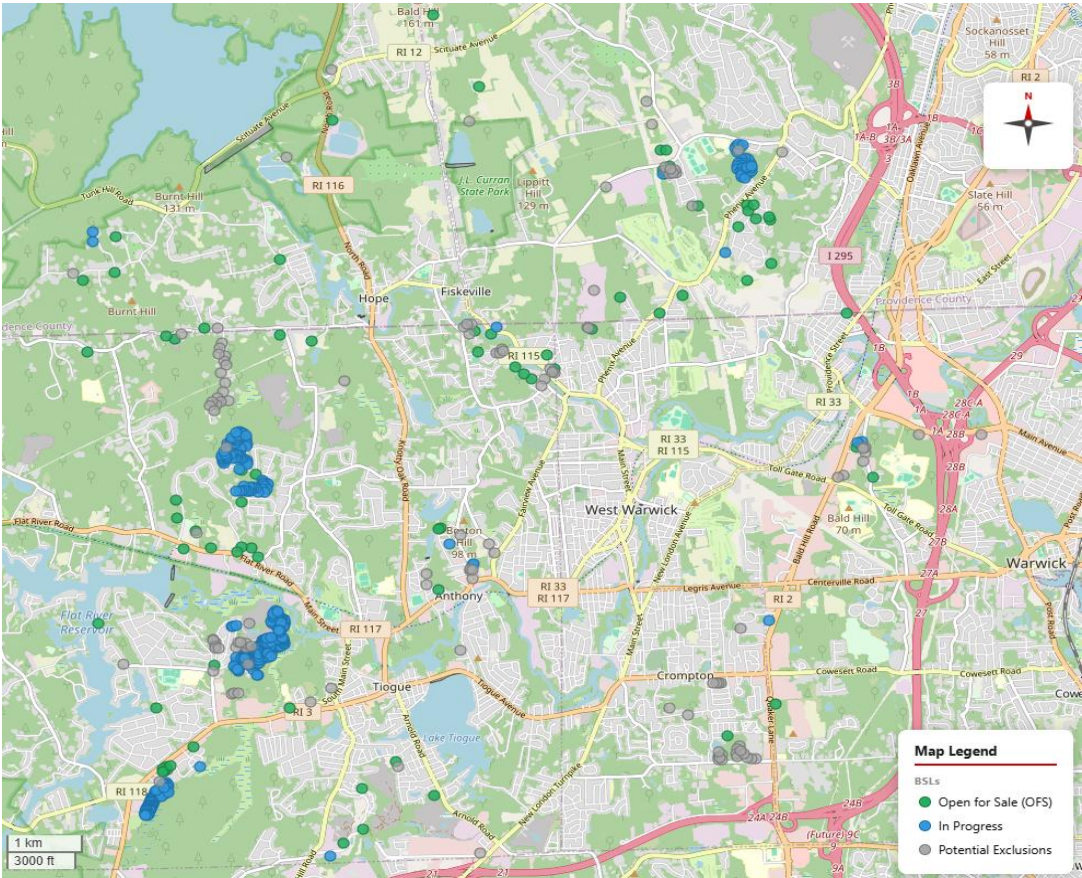


ISP: **Verizon New England, Inc.**

Communities Served: **Coventry, Cranston, Scituate, Warwick**

Project Area: PA-6

Data as of FY2026 Q4

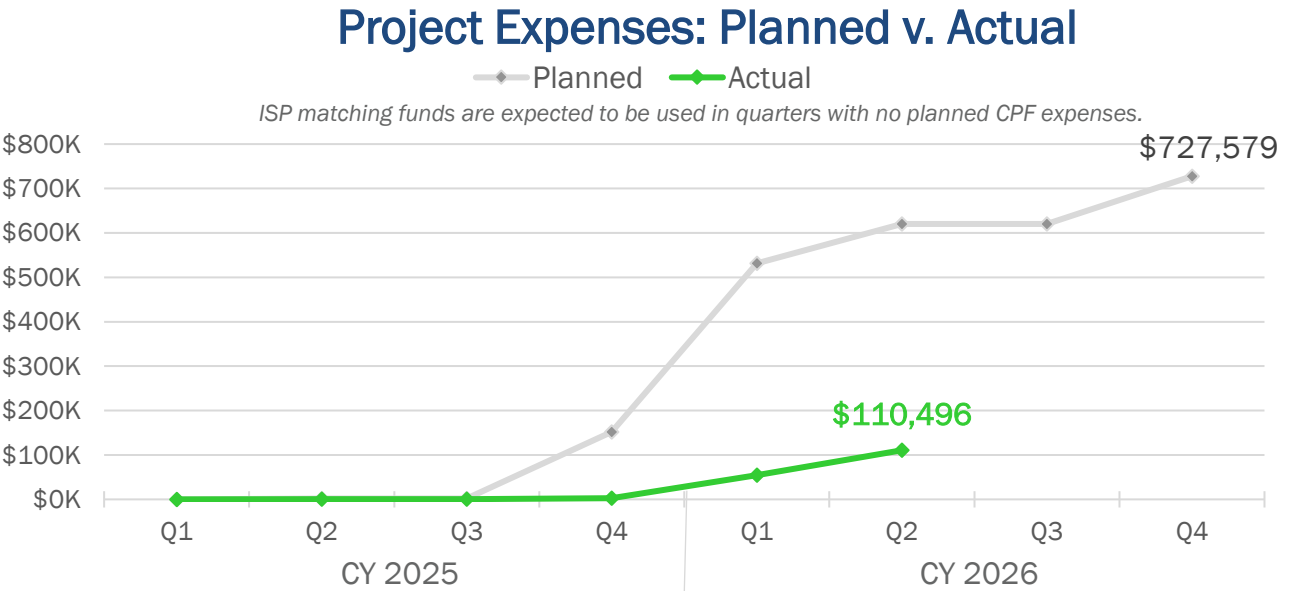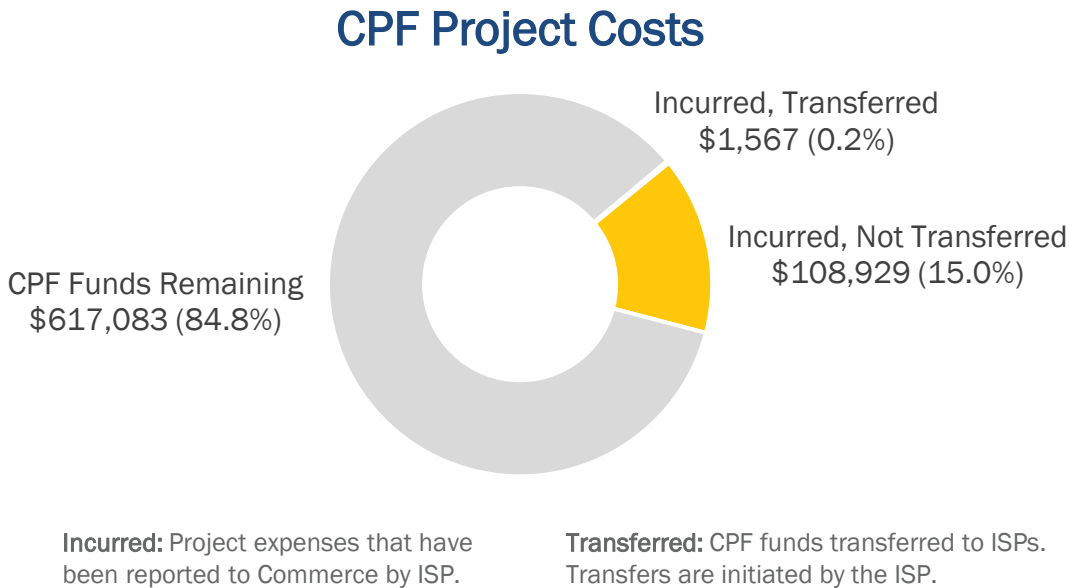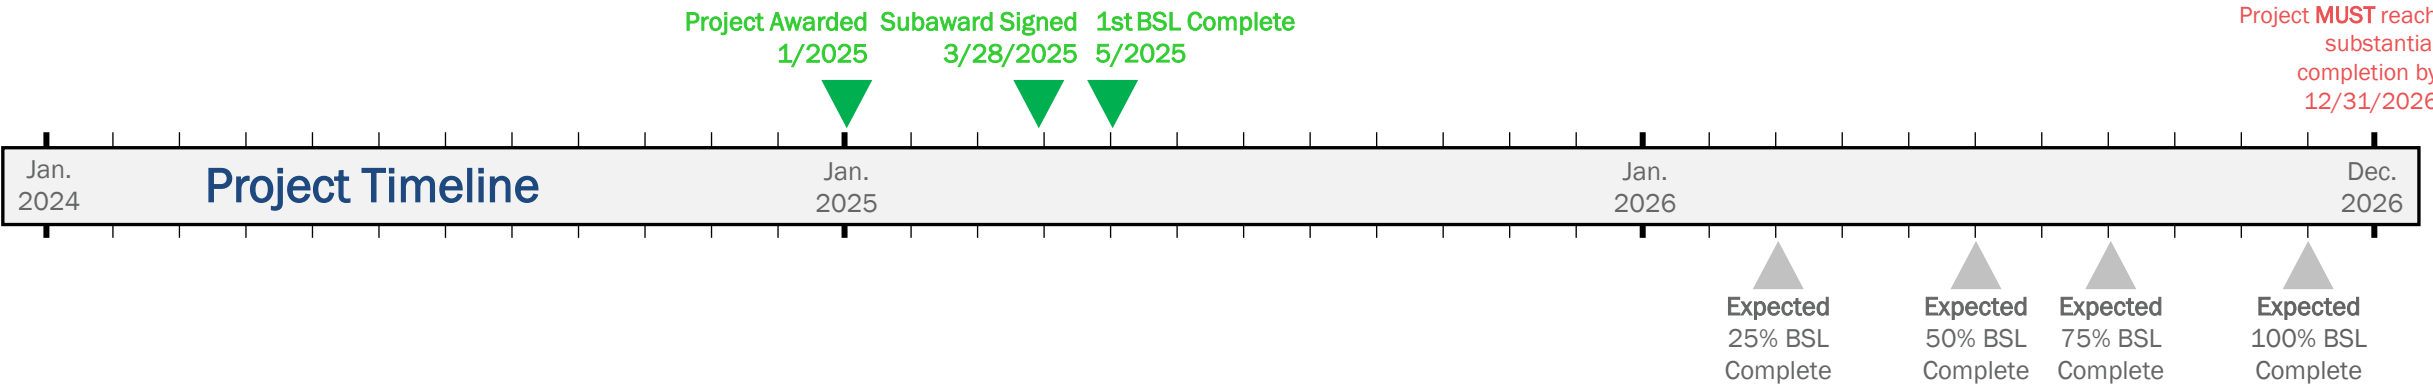

Project Area: PA-7

Data as of FY2026 Q4

CPF award: **\$821,947**

Internet Service Provider (ISP) match: **\$1,425,428**


Total Project Cost: **\$2,247,375**

Project is funded through CPF, 37%, & ISP Match, 63%

	Planned	Total to Date
Miles of Fiber	32	0.4
Eligible BSLs Served	421	103

Start Date: **3/4/2026**

Completion Date: **9/30/2026**



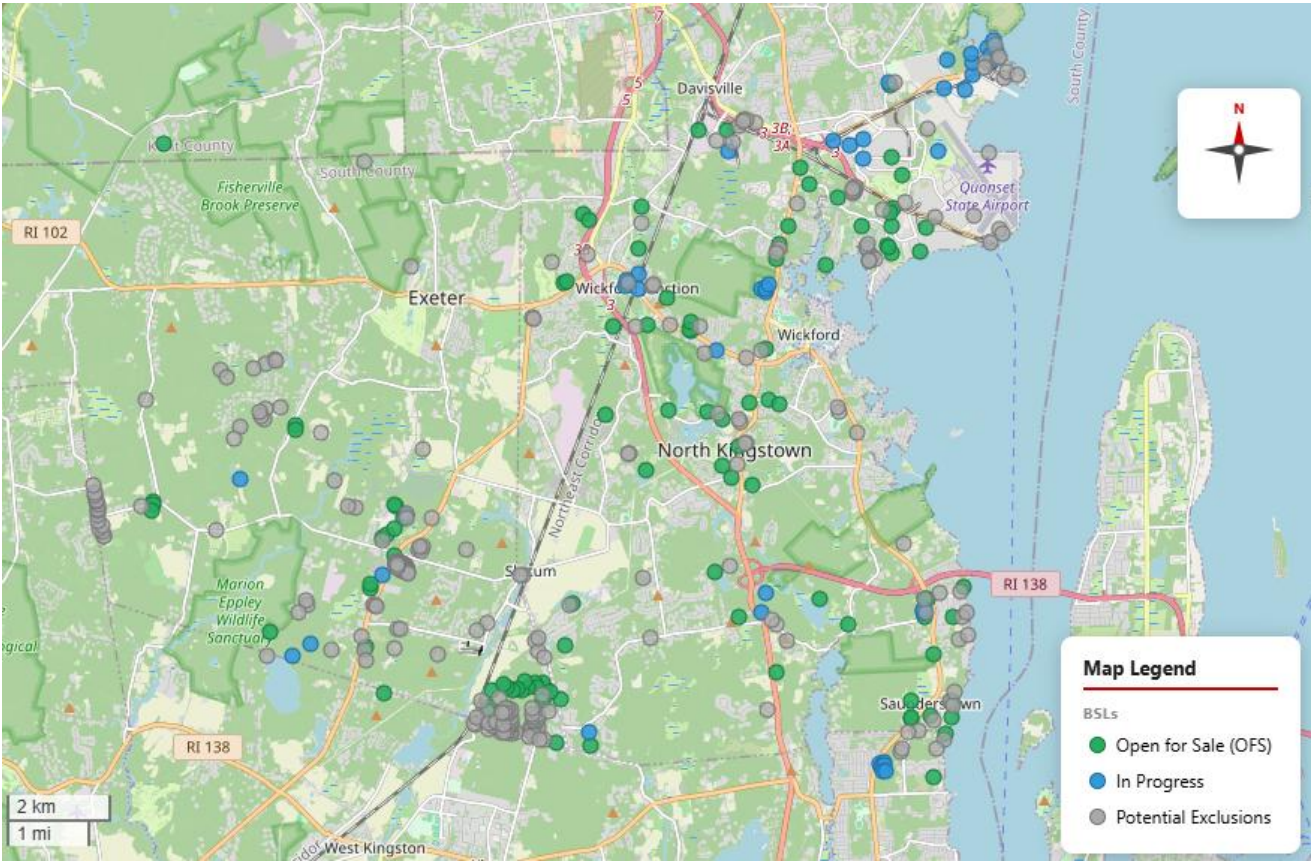


ISP: **Verizon New England, Inc.**

Communities Served: **Exeter, Narragansett, North Kingstown, West Greenwich**

Project Area: PA-7

Data as of FY2026 Q4

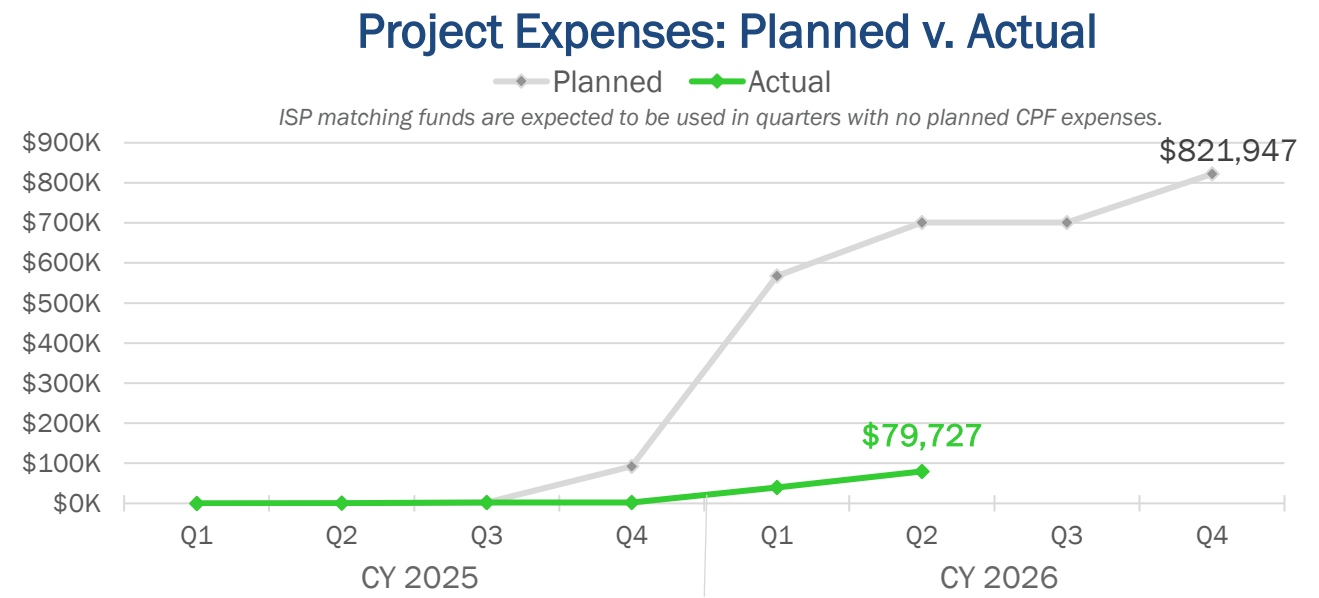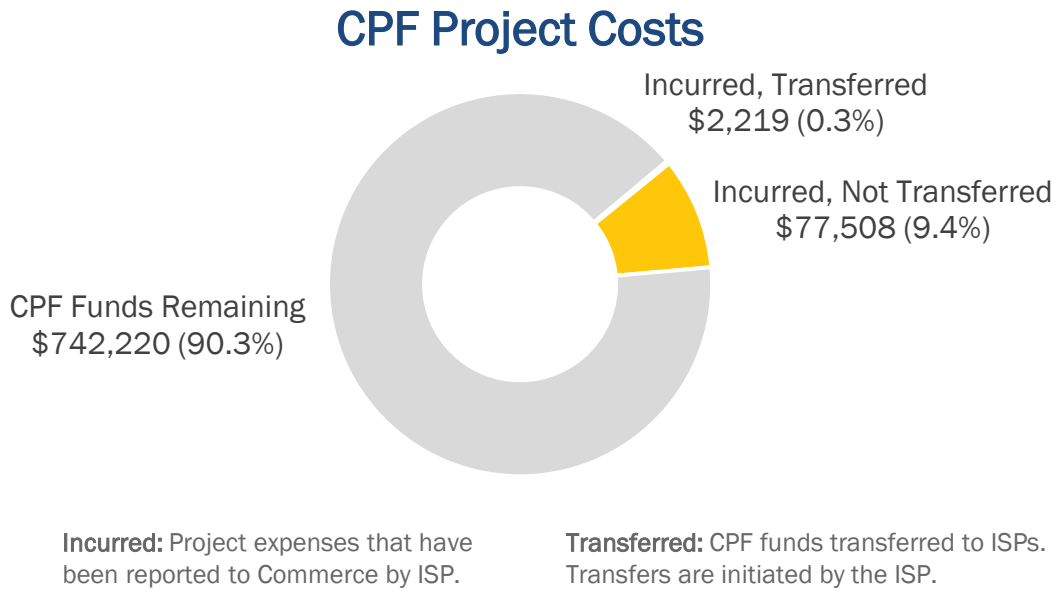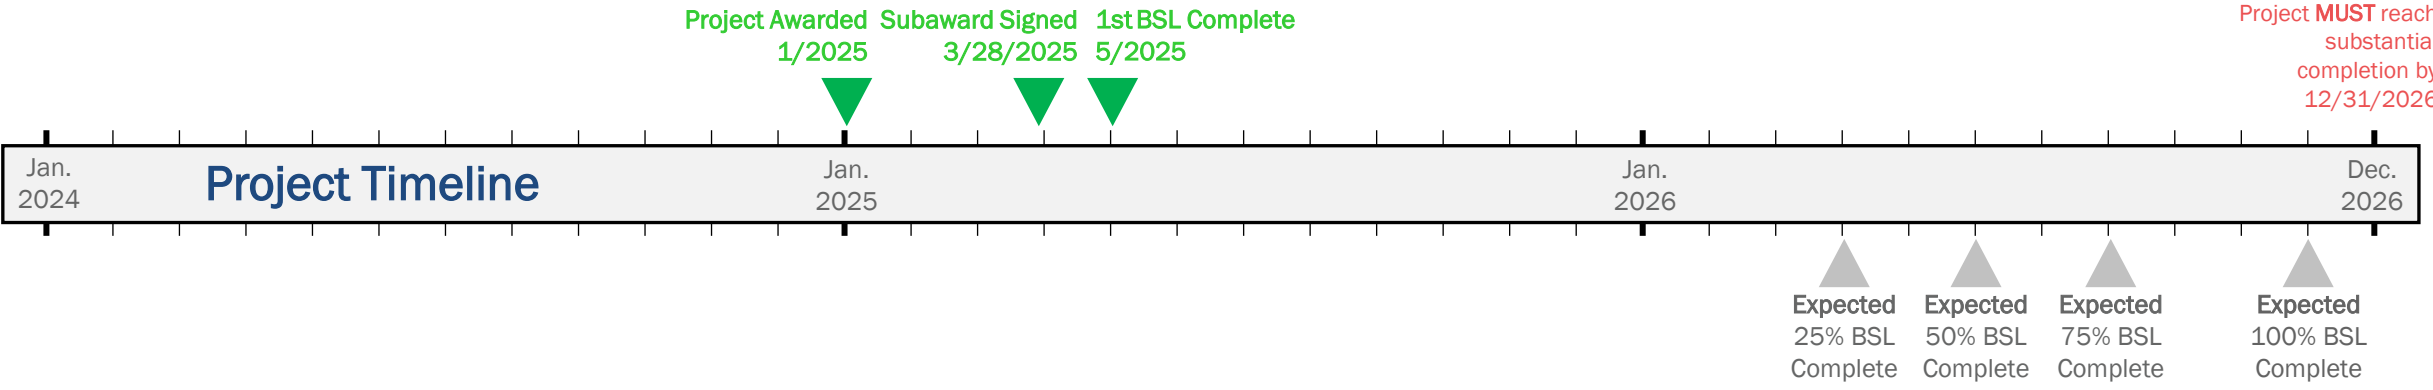

Project Area: PA-A

Data as of FY2026 Q4

CPF award: **\$1,651,334**

Internet Service Provider (ISP) match: **\$3,066,762**


Total Project Cost: **\$4,718,096**

Project is fully funded through CPF, 35%, & ISP Match, 65%

	Planned	Total to Date
Miles of Fiber	55	45.5
Eligible BSLs Served	2,198	857

Start Date: **7/24/2025**

Completion Date: **10/31/2026**



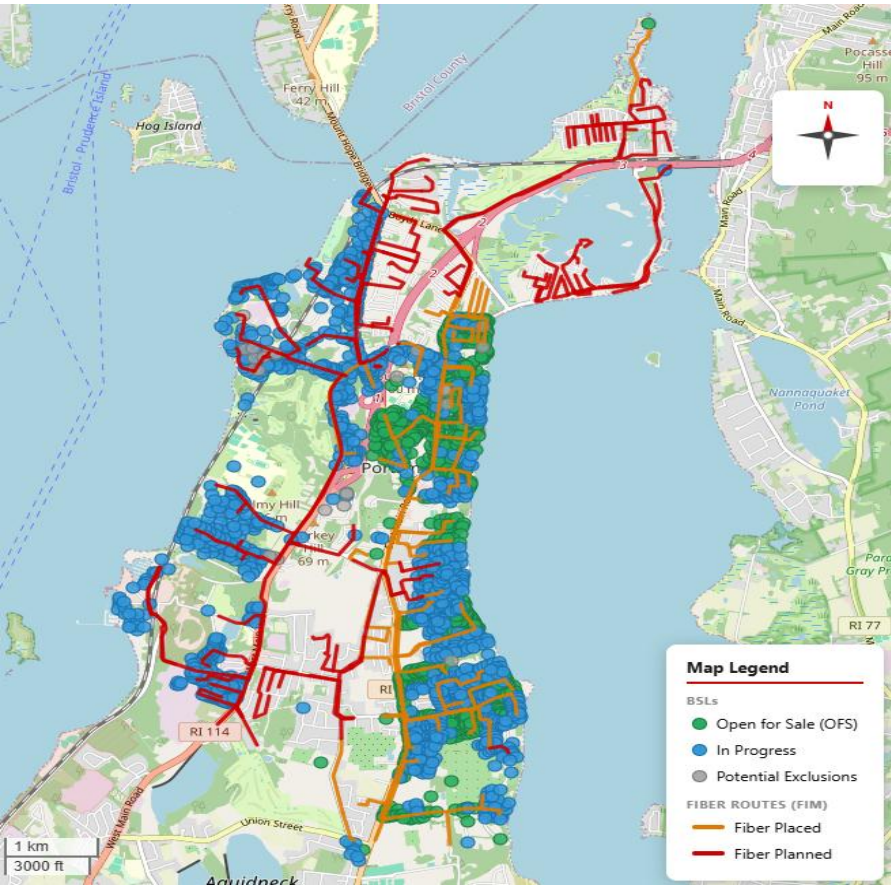


ISP: **Verizon New England, Inc.**

Communities Served: **Portsmouth**

Project Area: PA-A

Data as of FY2026 Q4

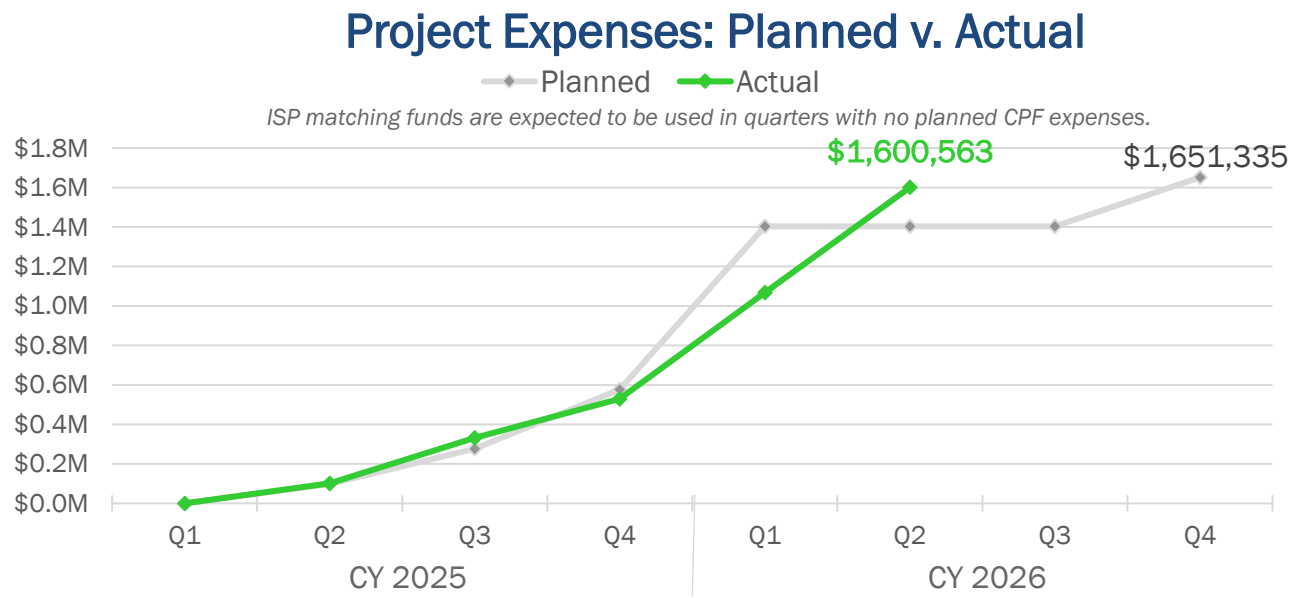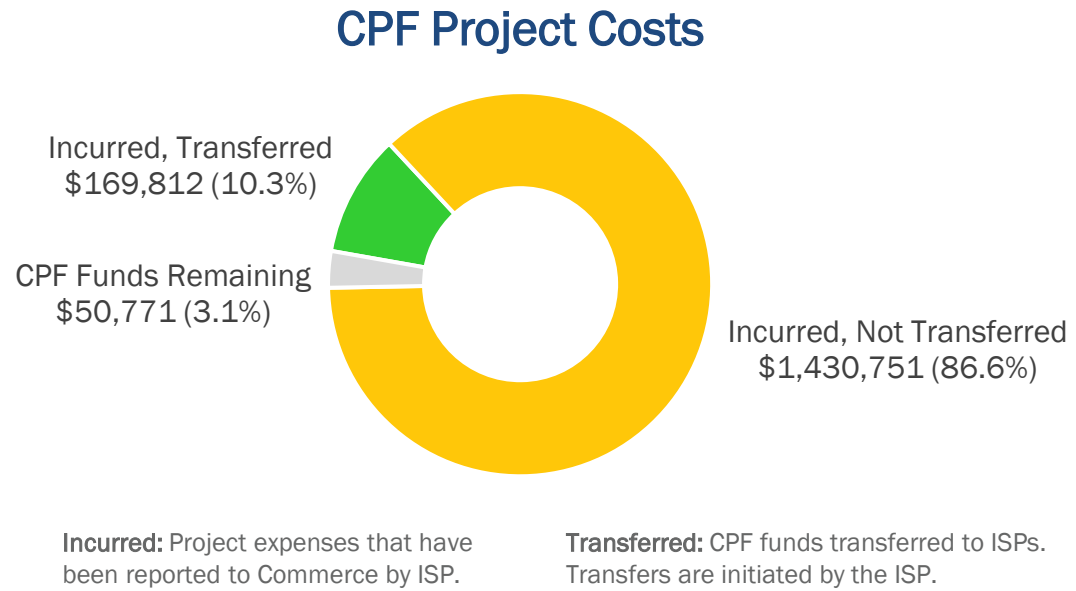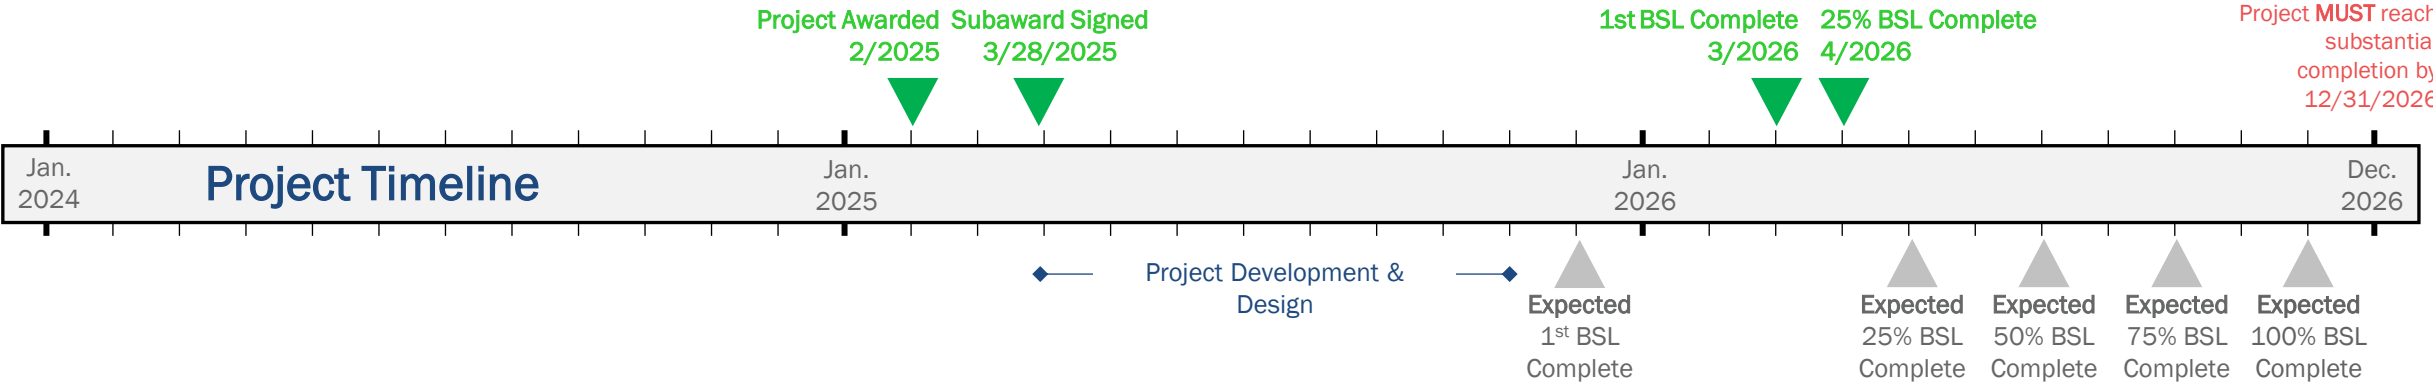

Project Area: PA-F

CPF award: **\$3,054,582**

Internet Service Provider (ISP) match: **\$6,963,087**

Total Project Cost: **\$10,017,669**

Project is funded through CPF, 31%, & ISP Match, 69%

	Planned	Total to Date
Miles of Fiber	120	49.3
Eligible BSLs Served	4,283	1,168

Start Date: **12/29/2025**

Completion Date: **10/31/2026**






ISP: **Verizon New England, Inc.**

Communities Served: **Tiverton**

Project Area: PA-F

Data as of FY2026 Q4

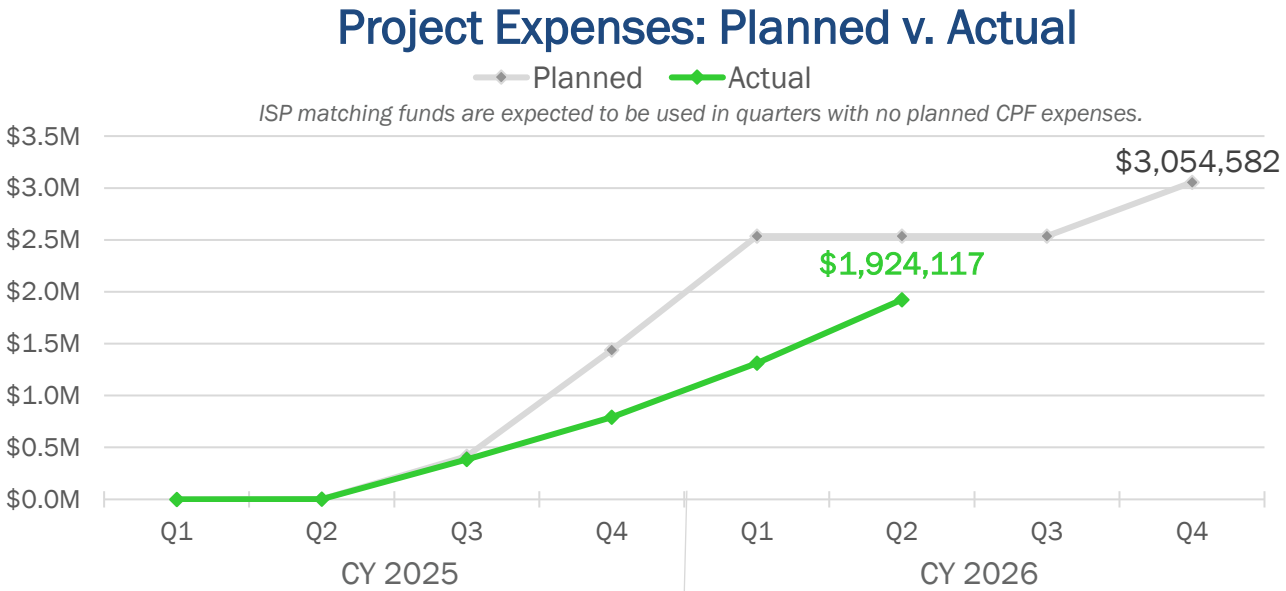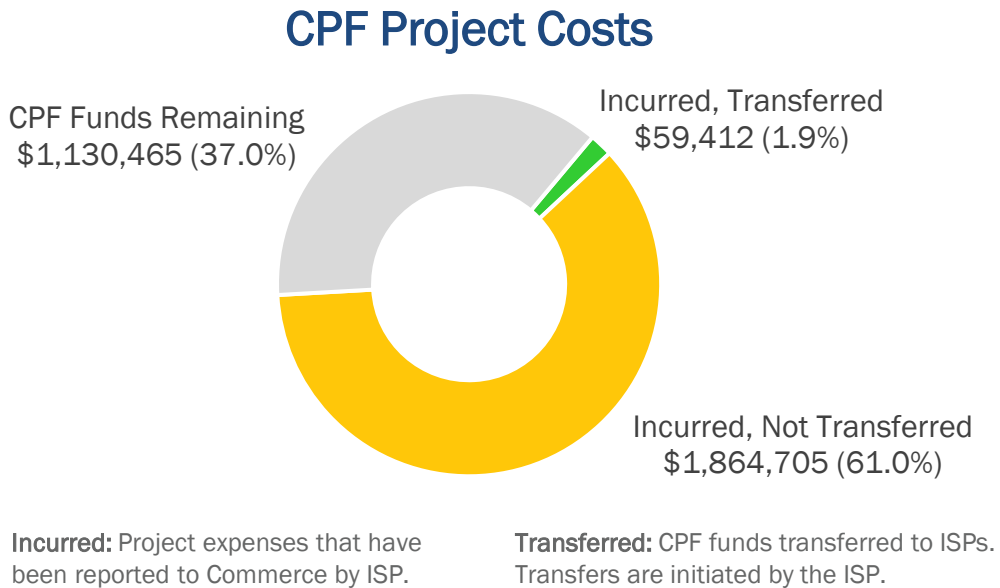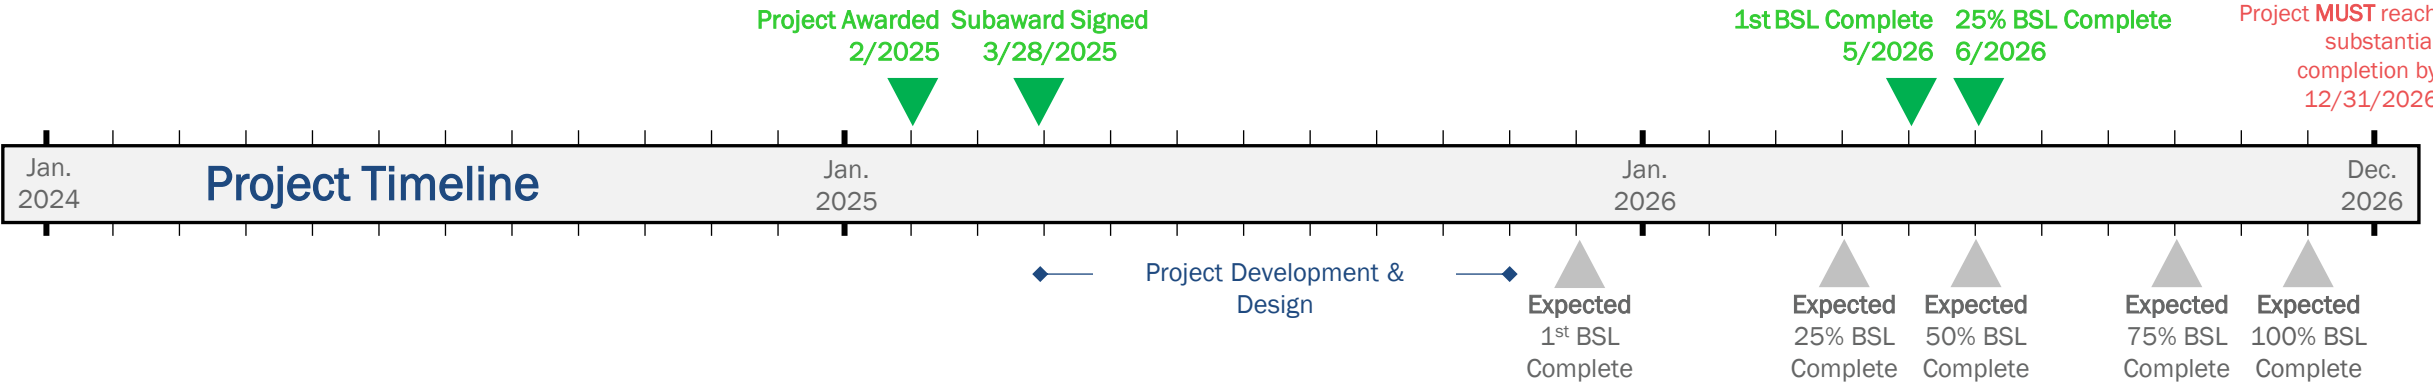

Community Learning Center Municipal Grant Program



As of June 30, 2026


RI's CPF Community Learning Center Program

- State of Rhode Island structured its CPF Multipurpose Community Facilities program as a Community Learning Center (CLC) Municipal Grant administered by DOA through PRO
 - Multiple stages of award throughout the program's existence
 - \$81.7M allocated to all 39 municipalities on 8/3/2023 with each municipality guaranteed at least \$300K
 - Stage 1 ended on 8/15/2023 with 34 municipalities opting into the program for 49 projects
 - Stage 2 ended on 10/23/2023 with 29 municipalities submitting formal applications for 31 projects
 - Stage 3 consisted of due diligence reviews by PRO prior to issuance of subaward agreements
 - Subaward agreements signed with 18 municipalities for 21 projects
 - \$81.7M of CPF funds sub-awarded by 6/30/2025:
 - 13 projects fully funded by CPF; Eight projects fully funded by CPF and at least one other source
 - Allocation increased to \$82.2M on 2/2/2026 to provide contingency funding as needed

RI's CPF Community Learning Center Program

- State of Rhode Island launched a second round of the CLC Municipal Grant program titled Community Library Municipal Grant (CLMG) on 2/6/2026
 - Multiple stages of award throughout the program's existence
 - One million allocated on 1/27/2026 to 17 Learn365RI municipalities that were not part of round one, with each municipality guaranteed at least \$25K
 - Stage 1 ended on 2/6/2026 with 17 municipalities opting into the program
 - Stage 2 ended on 3/6/2026 with 14 municipalities submitting scopes for 23 projects
 - Stage 3 ended on 3/20/2026 with 13 municipalities submitting budgets for 21 projects
 - As of 6/30/2026, subaward agreements signed with 12 municipalities for 17 projects

Community Learning Center Locations

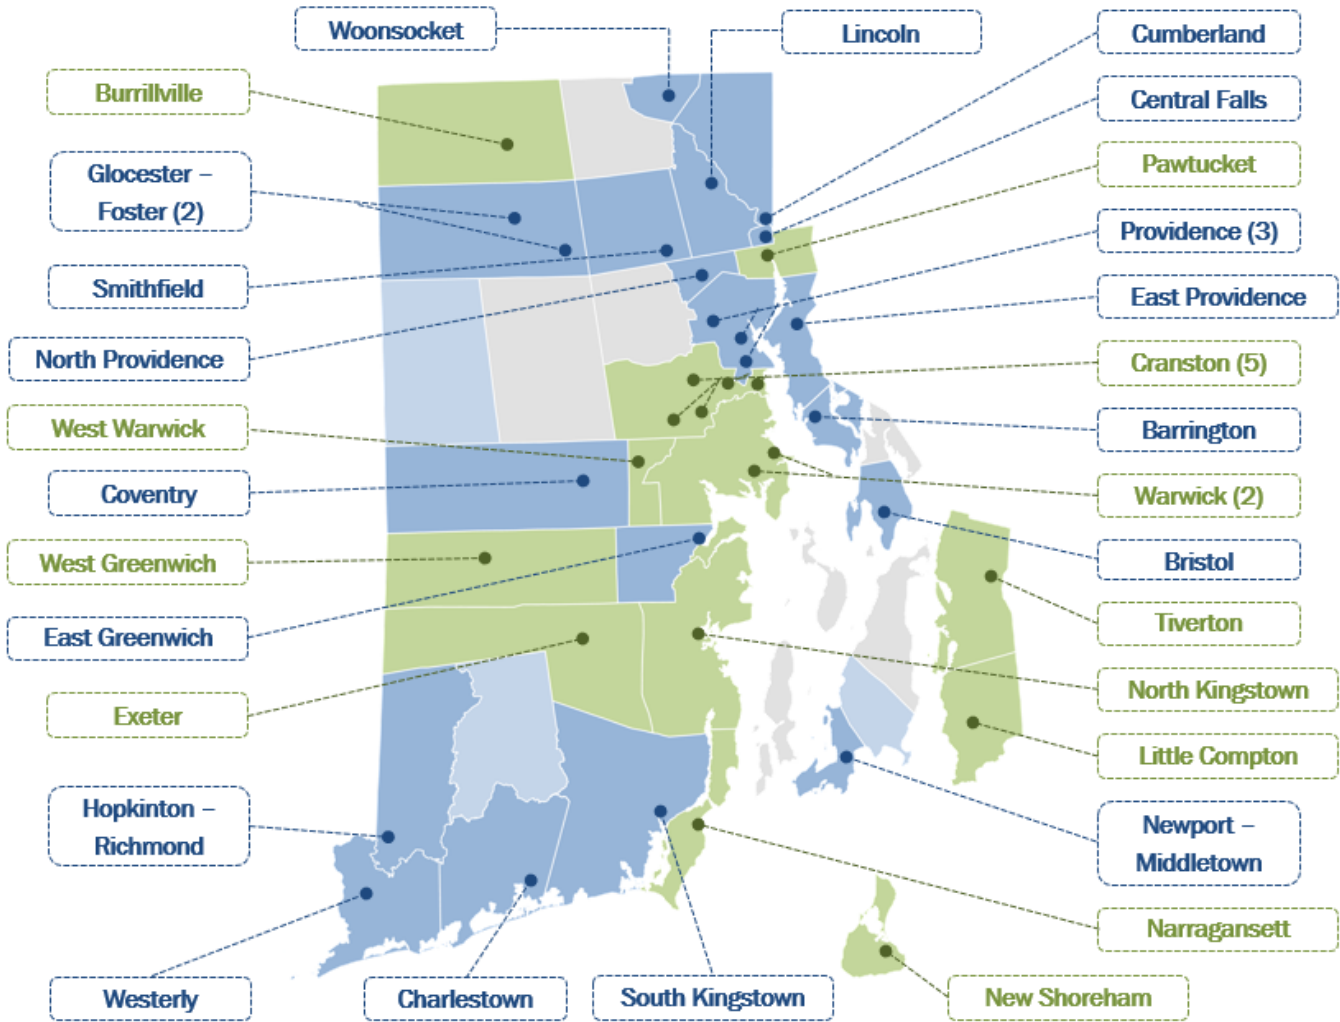

- Eighteen municipalities are participating in round 1 and are building 21 Community Learning Centers across the State of Rhode Island
- Twelve municipalities are participating in round 2 and are enhancing 17 community libraries across the State of Rhode Island

- Primary municipalities participating in round 1 (CLC projects)
- Partnering municipalities in round 1
- Municipalities participating in round 2 (CLMG projects)




Community Learning Center Municipal Grant

Round 1 Program Update

As of June 30, 2026

Community Learning Center Locations

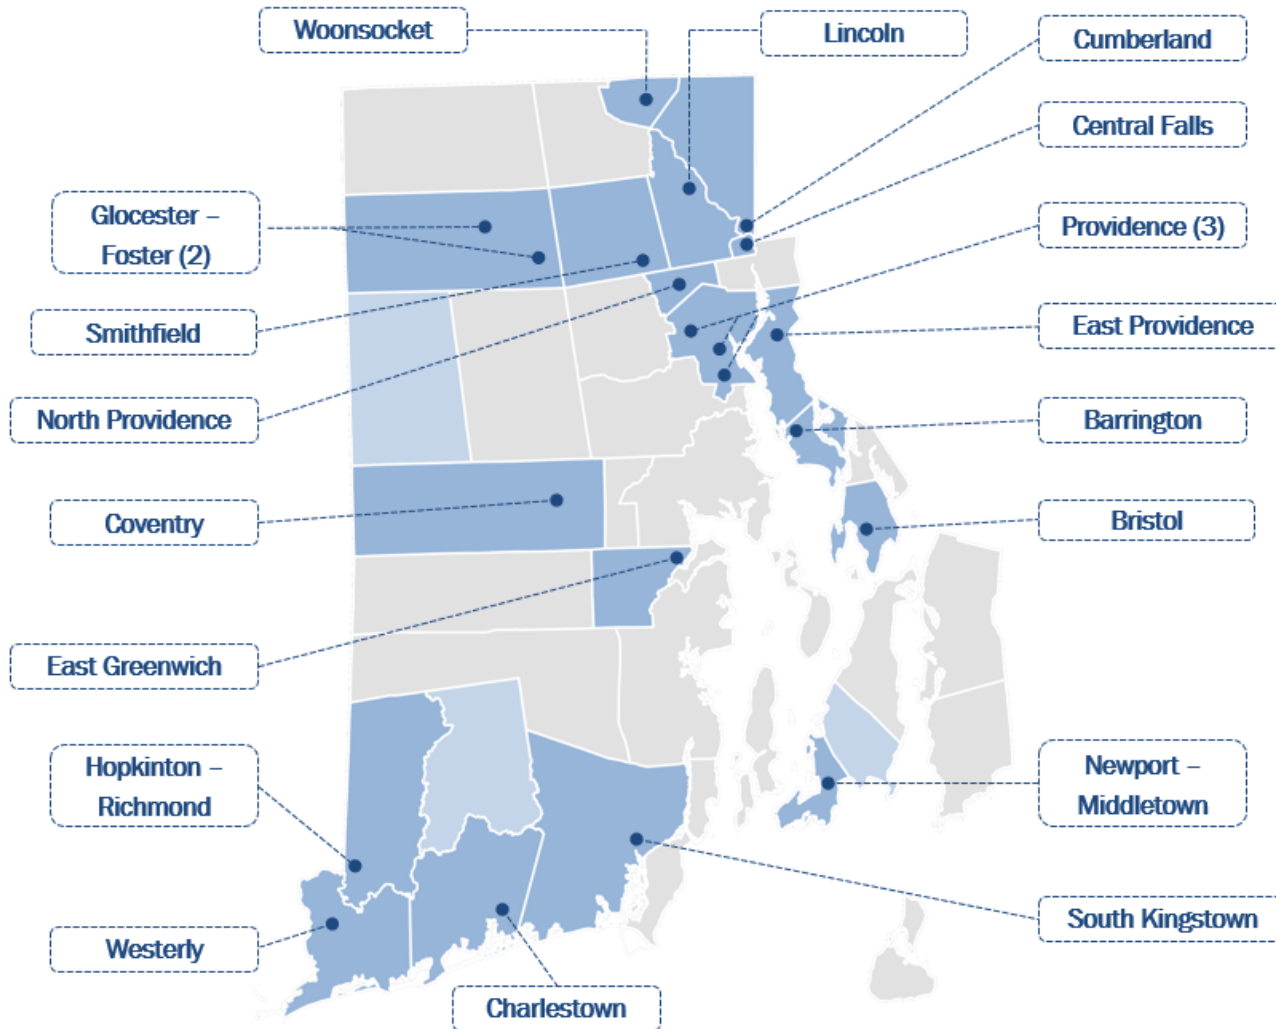

- Current Amount Subawarded: **\$82,220,128**
- Eighteen municipalities are building 21 Community Learning Centers across the State of Rhode Island
- Six neighboring municipalities are partnering to build four shared projects:
 - Gloucester – Foster: Two CLC projects
 - Hopkinton – Richmond: One CLC project
 - Newport – Middletown: One CLC project

Municipal Allocation of Capital Project Funds


Data as of FY2026 Q4

Municipality	Grant Award Amount	% of Total Grant Funds
Barrington	\$1,686,732	2.1%
Bristol	\$1,971,967	2.4%
Central Falls	\$8,985,198	10.9%
Charlestown	\$673,368	0.8%
Coventry	\$4,959,565	6.0%
Cumberland	\$3,118,159	3.8%
East Greenwich	\$1,596,800	1.9%
East Providence	\$10,493,659	12.8%
Glocester – Foster ^	\$1,030,247	1.3%
Hopkinton – Richmond	\$2,666,514	3.2%
Lincoln	\$2,000,000	2.4%
Newport – Middletown	\$7,527,554	9.2%
North Providence	\$2,860,894	3.5%
Providence ^	\$16,200,000	19.7%
Smithfield	\$2,592,961	3.2%
South Kingstown	\$2,893,891	3.5%
Westerly	\$3,819,120	4.6%
Woonsocket	\$7,143,500	8.7%
TOTAL	\$82,220,129	100%

^ Municipalities with more than one Community Learning Center project.

Award by Project

Data as of FY2026 Q4

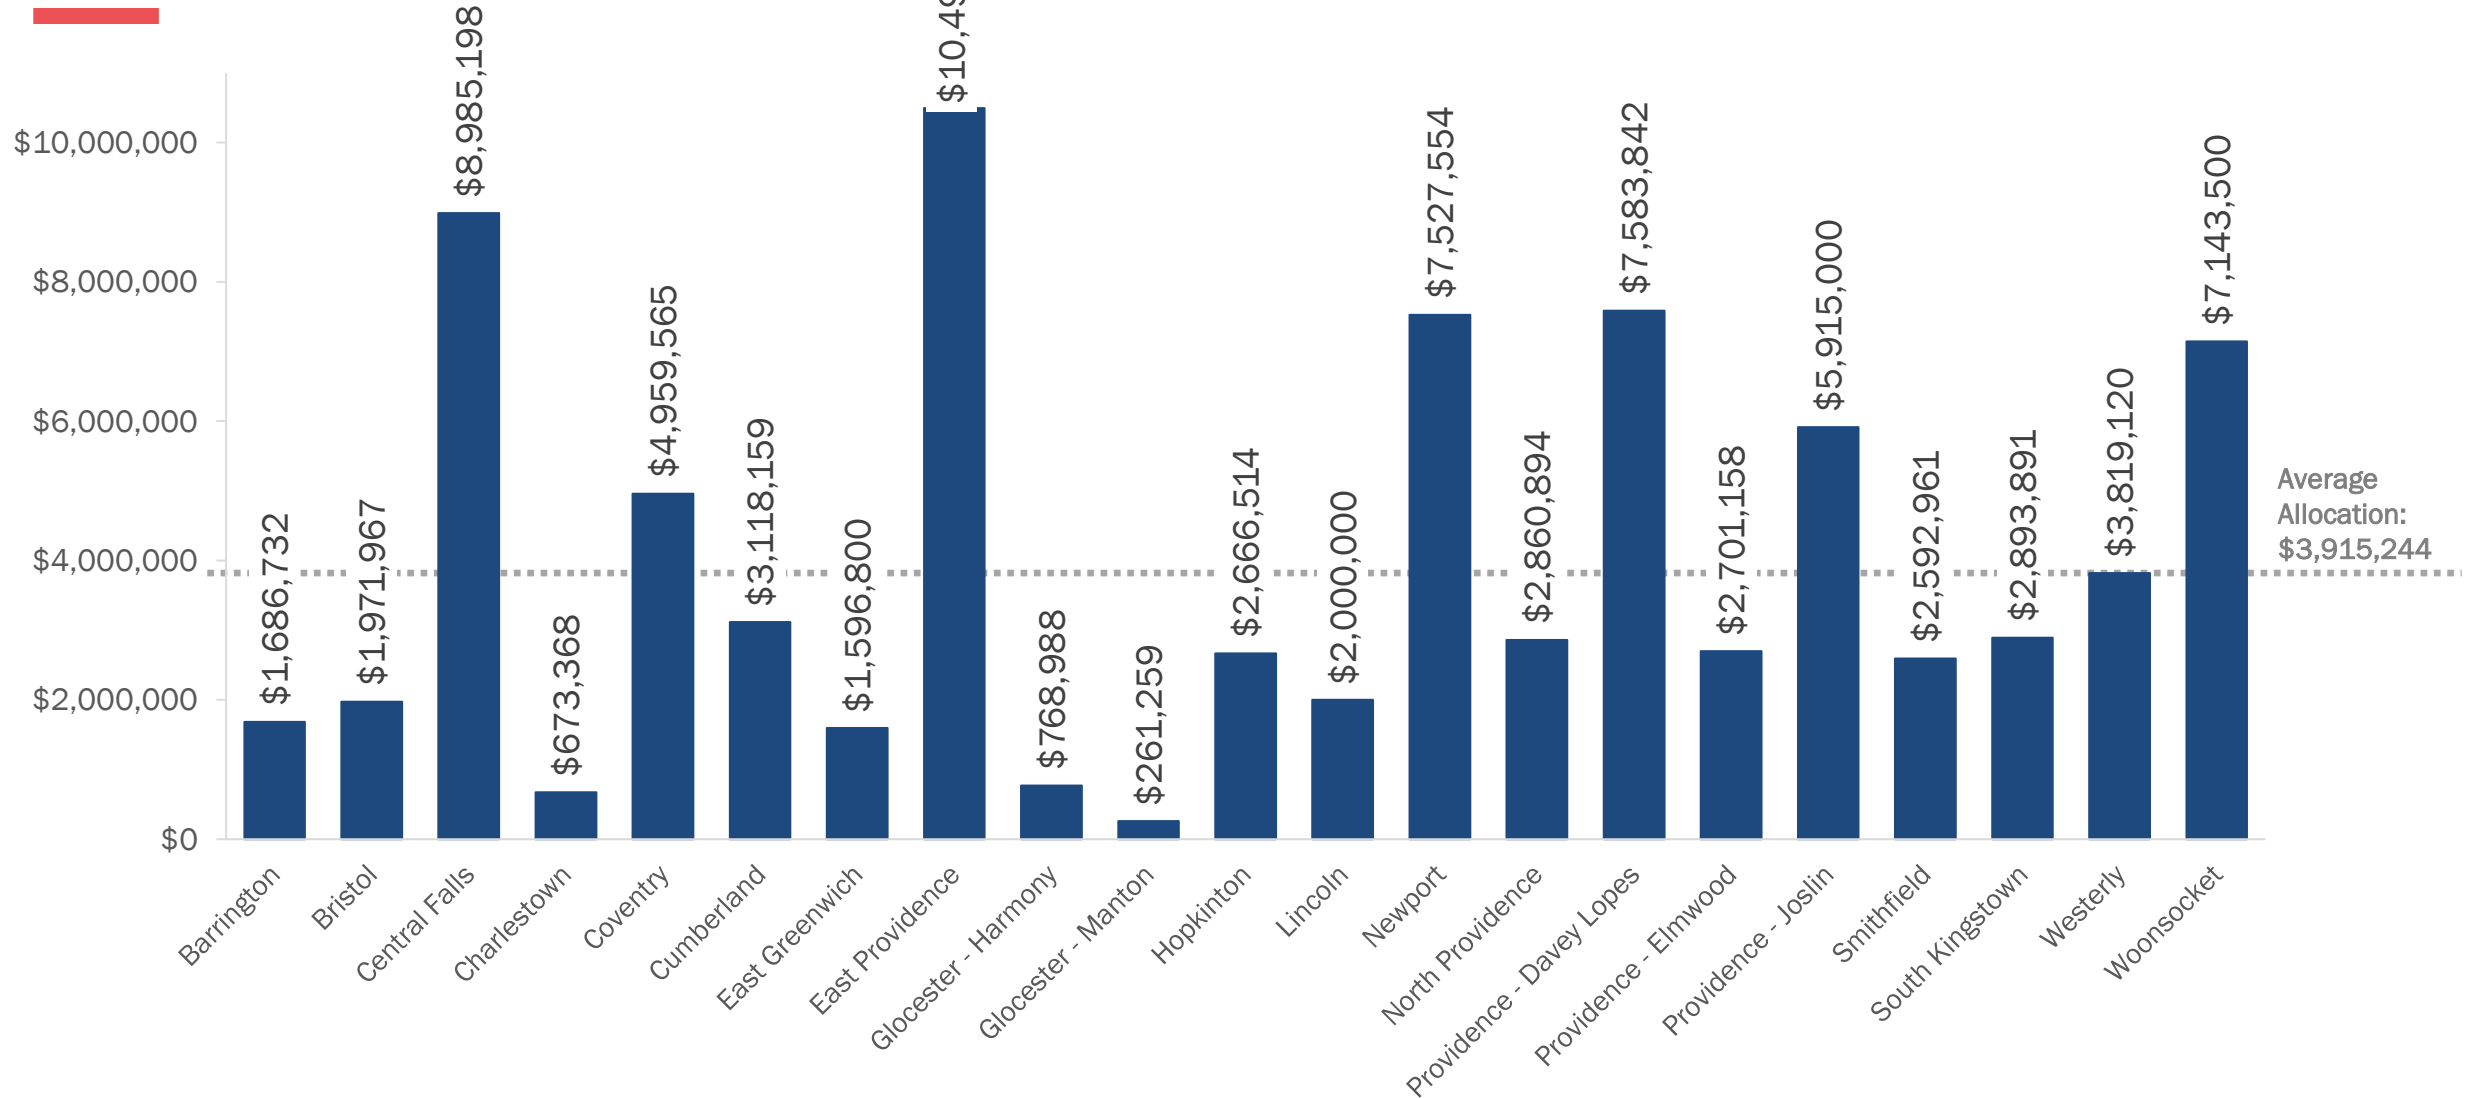

Project Scopes and Timelines

Data as of FY2026 Q4

Green indicates project has completed construction

Purple indicates project has reached substantial completion per U.S. Treasury

Municipality	Project	Square Footage	Construction Start	Construction End	Start of Operations
Barrington	Bay Spring Community Learning Center	2,367	06/23/2025	07/17/2026	09/01/2026
Bristol	Rogers Free Library Facility Improvements	25,000	10/15/2025	07/10/2026	07/21/2026
Central Falls	El Centro	19,500	08/11/2025	09/18/2026	10/31/2026
Charlestown	Cross Mills Public Library	2,450	01/05/2026	07/15/2026	07/15/2026
Coventry	Coventry Community Learning Center	38,500	08/17/2024	06/15/2026	07/13/2026
Cumberland	Amaral Building And Heritage Park	9,302	09/20/2024	10/31/2026	11/30/2026
East Greenwich	Swift Community Center †	2,051	04/15/2025	09/01/2026	10/01/2026
East Providence	East Providence Community Center †	9,803	06/06/2025	10/31/2026	10/31/2026
Glocester	Harmony Library †	1,080	12/08/2025	07/31/2026	09/08/2026
Glocester	Manton Library	1,320	03/03/2025	12/31/2025	02/02/2026
Hopkinton	Hopkinton Regional Community Center	2,750	01/06/2025	02/09/2026	03/07/2026

† Indicates project is new construction. All other projects are renovations of existing capital assets.

Project Scopes and Timelines

Data as of FY2026 Q4

Green indicates project has completed construction

Purple indicates project has reached substantial completion per U.S. Treasury

Municipality	Project	Square Footage	Construction Start	Construction End	Start of Operations
Lincoln	Lincoln Learning Center †	2,600	03/07/2025	05/01/2026	08/31/2026
Newport	Florence Gray Center	15,700	09/03/2024	08/31/2026	11/15/2026
North Providence	North Providence Community Center	8,893	06/16/2025	10/31/2026	04/15/2026
Providence	Davey Lopes Recreation Center	9,000	09/29/2025	08/31/2026	09/17/2026
Providence	Elmwood Community Center	14,000	10/02/2023	12/31/2025	03/02/2026
Providence	Joslin Recreation Center	12,830	09/04/2025	10/20/2026	12/21/2026
Smithfield	East Smithfield Neighborhood Center	6,435	05/01/2022	03/31/2026	04/15/2026
South Kingstown	Peace Dale Library	3,867	09/29/2025	07/31/2026	09/07/2026
Westerly	Tower Street Community Center †	8,000	10/27/2025	10/15/2026	11/15/2026
Woonsocket	Community Learning Center At Cass Park †	14,000	05/21/2024	10/31/2026	12/31/2026

† Indicates project is new construction. All other projects are renovations of existing capital assets.

Budgets & Expenditures

Data as of FY2026 Q4

Green indicates project has completed construction

Purple indicates project has reached substantial completion per U.S. Treasury

Municipality	Project	Total Project Cost	CPF Award	Reported Expenses	CPF Funds Transferred	CPF Funds Remaining
Barrington	Bay Spring Community Learning Center	\$1,686,732	\$1,686,732	\$1,438,399	\$899,265	\$787,467
Bristol	Rogers Free Library Facility Improvements	\$2,075,900	\$1,971,967	\$1,729,337	\$1,691,626	\$280,341
Central Falls	El Centro	\$13,064,698	\$8,985,198	\$5,217,628	\$5,127,367	\$3,857,831
Charlestown	Cross Mills Public Library	\$673,368	\$673,368	\$463,952	\$435,000	\$238,368
Coventry	Coventry Community Learning Center	\$5,535,006	\$4,959,565	\$4,959,565	\$4,136,121	\$823,444
Cumberland	Amaral Building And Heritage Park	\$4,118,159	\$3,118,159	\$3,089,990	\$2,692,530	\$425,630
East Greenwich	Swift Community Center †	\$1,596,800	\$1,596,800	\$773,755	\$978,795	\$618,005
East Providence	East Providence Community Center †	\$10,493,659	\$10,493,659	\$6,721,019	\$4,681,777	\$5,811,882
Glocester	Harmony Library †	\$768,988	\$768,988	\$436,404	\$300,000	\$468,988
Glocester	Manton Library	\$261,259	\$261,259	\$261,259	\$261,259	\$0
Hopkinton	Hopkinton Regional Community Center	\$2,666,514	\$2,666,514	\$2,666,514	\$2,665,834	\$680

† Indicates project is new construction. All other projects are renovations of existing capital assets.

Budgets & Expenditures

Data as of FY2026 Q4

Green indicates project has completed construction


Purple indicates project has reached substantial completion per U.S. Treasury

Municipality	Project	Total Project Cost	CPF Awarded	Reported Expenses	CPF Funds Transferred	CPF Funds Remaining
Lincoln	Lincoln Learning Center †	\$2,000,000	\$2,000,000	\$1,553,287	\$1,480,000	\$520,000
Newport	Florence Gray Center	\$7,527,554	\$7,527,554	\$4,352,521	\$3,252,559	\$4,274,995
North Providence	North Providence Community Center	\$3,160,894	\$2,860,894	\$1,538,963	\$1,482,306	\$1,378,588
Providence	Davey Lopes Recreation Center	\$7,583,842	\$7,583,842	\$4,124,533	\$4,124,533	\$3,459,309
Providence	Elmwood Community Center	\$2,701,158	\$2,701,158	\$2,523,398	\$2,513,778	\$187,380
Providence	Joslin Recreation Center	\$5,915,000	\$5,915,000	\$2,553,391	\$2,580,046	\$3,334,954
Smithfield	East Smithfield Neighborhood Center	\$2,952,479	\$2,592,961	\$2,592,961	\$2,291,845	\$301,116
South Kingstown	Peace Dale Library	\$3,593,891	\$2,893,891	\$1,442,573	\$1,047,601	\$1,846,290
Westerly	Tower Street Community Center †	\$7,031,200	\$3,819,120	\$2,969,930	\$3,084,233	\$734,887
Woonsocket	Community Learning Center At Cass Park †	\$7,143,500	\$7,143,500	\$1,659,434	\$1,032,035	\$6,111,465
TOTAL		\$92,550,601	\$82,220,129	\$53,068,813	\$46,758,510	\$35,461,619

† Indicates project is new construction. All other projects are renovations of existing capital assets.


Project Transfers

Data as of FY2026 Q4

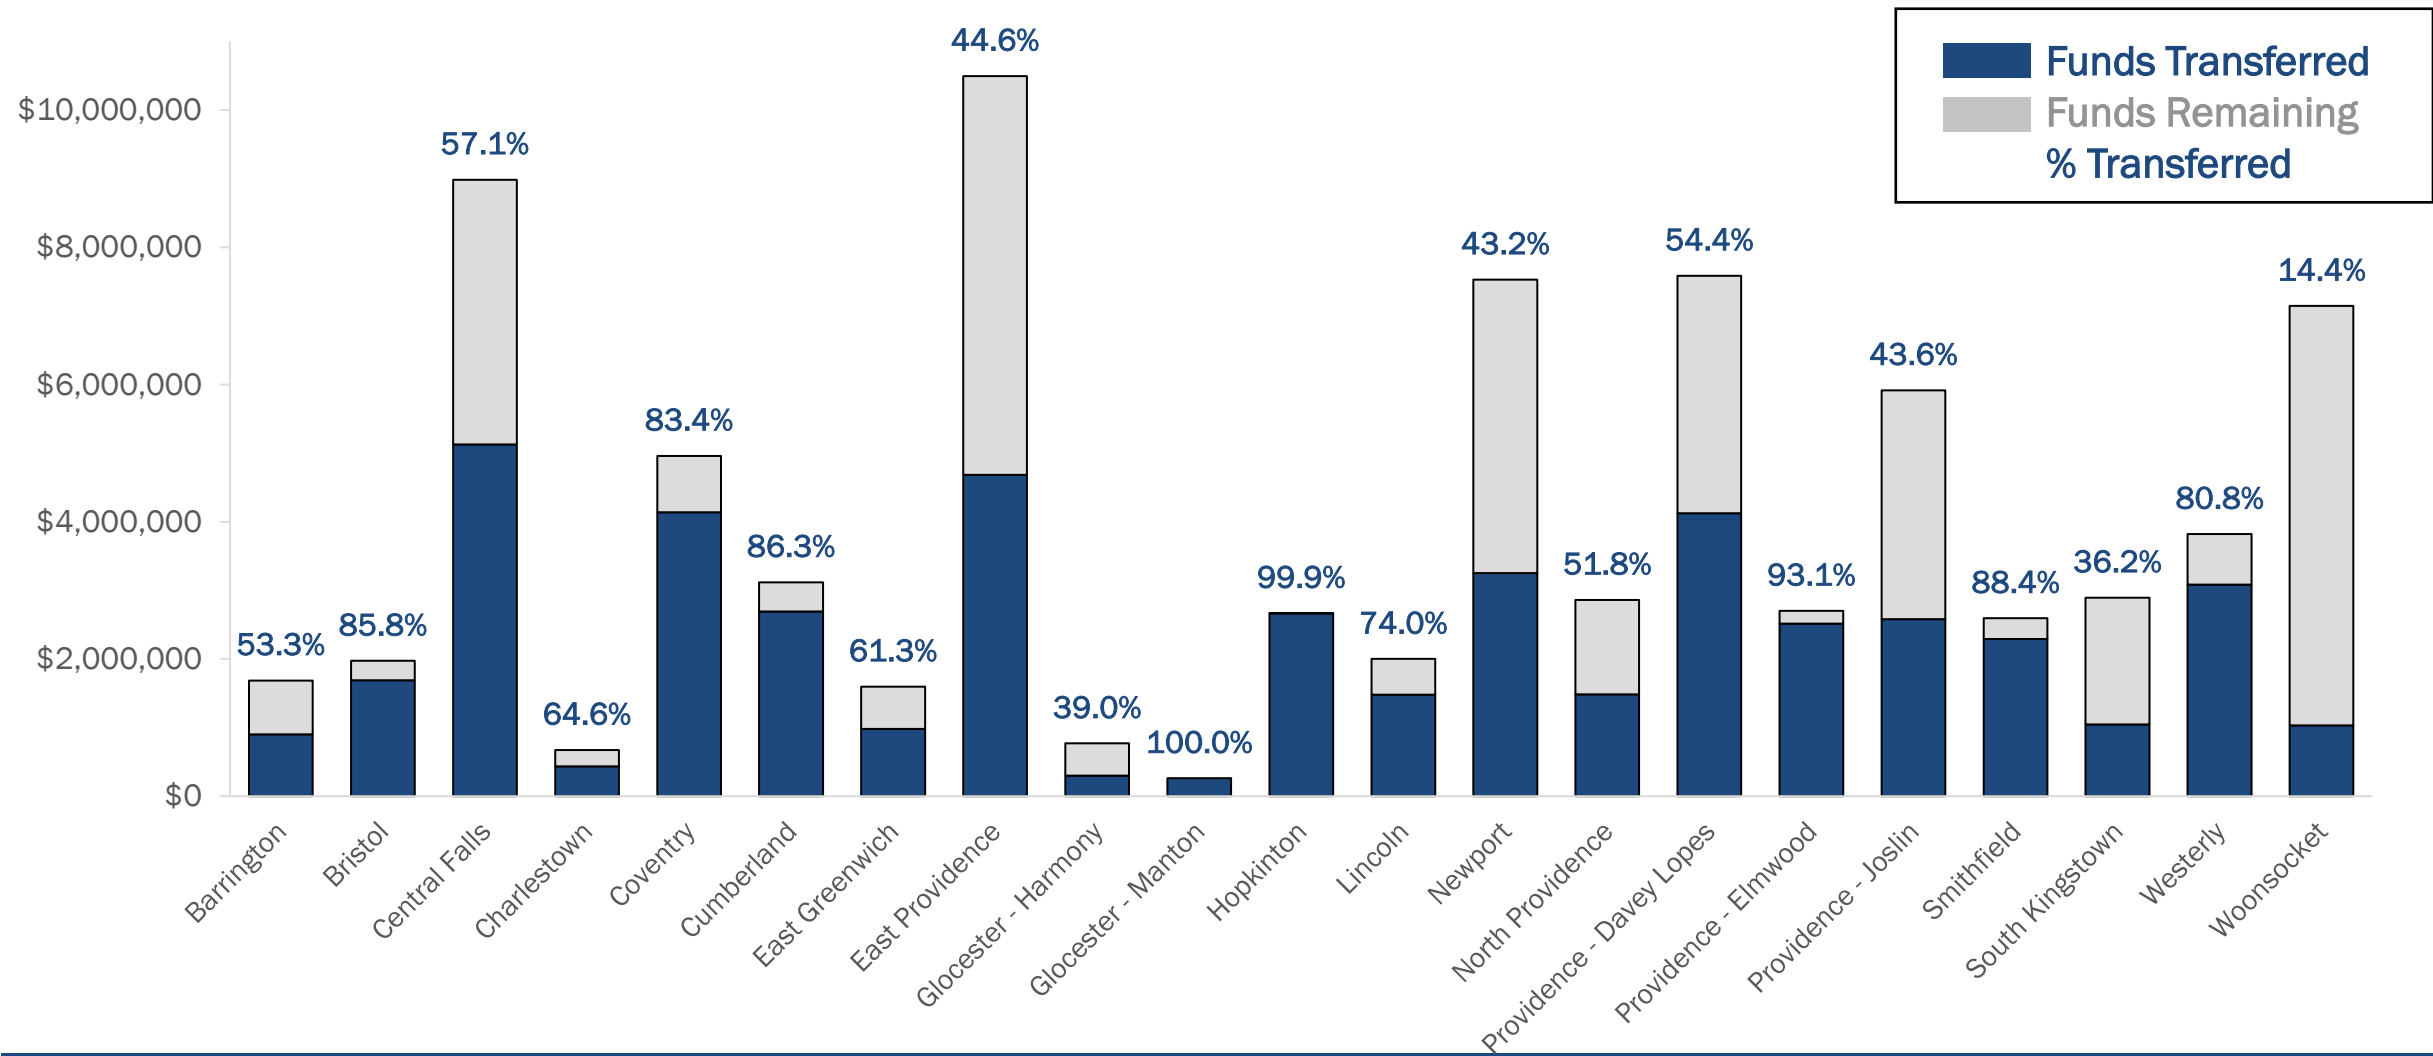

CLC Monthly Financials


Data as of FY2026 Q4

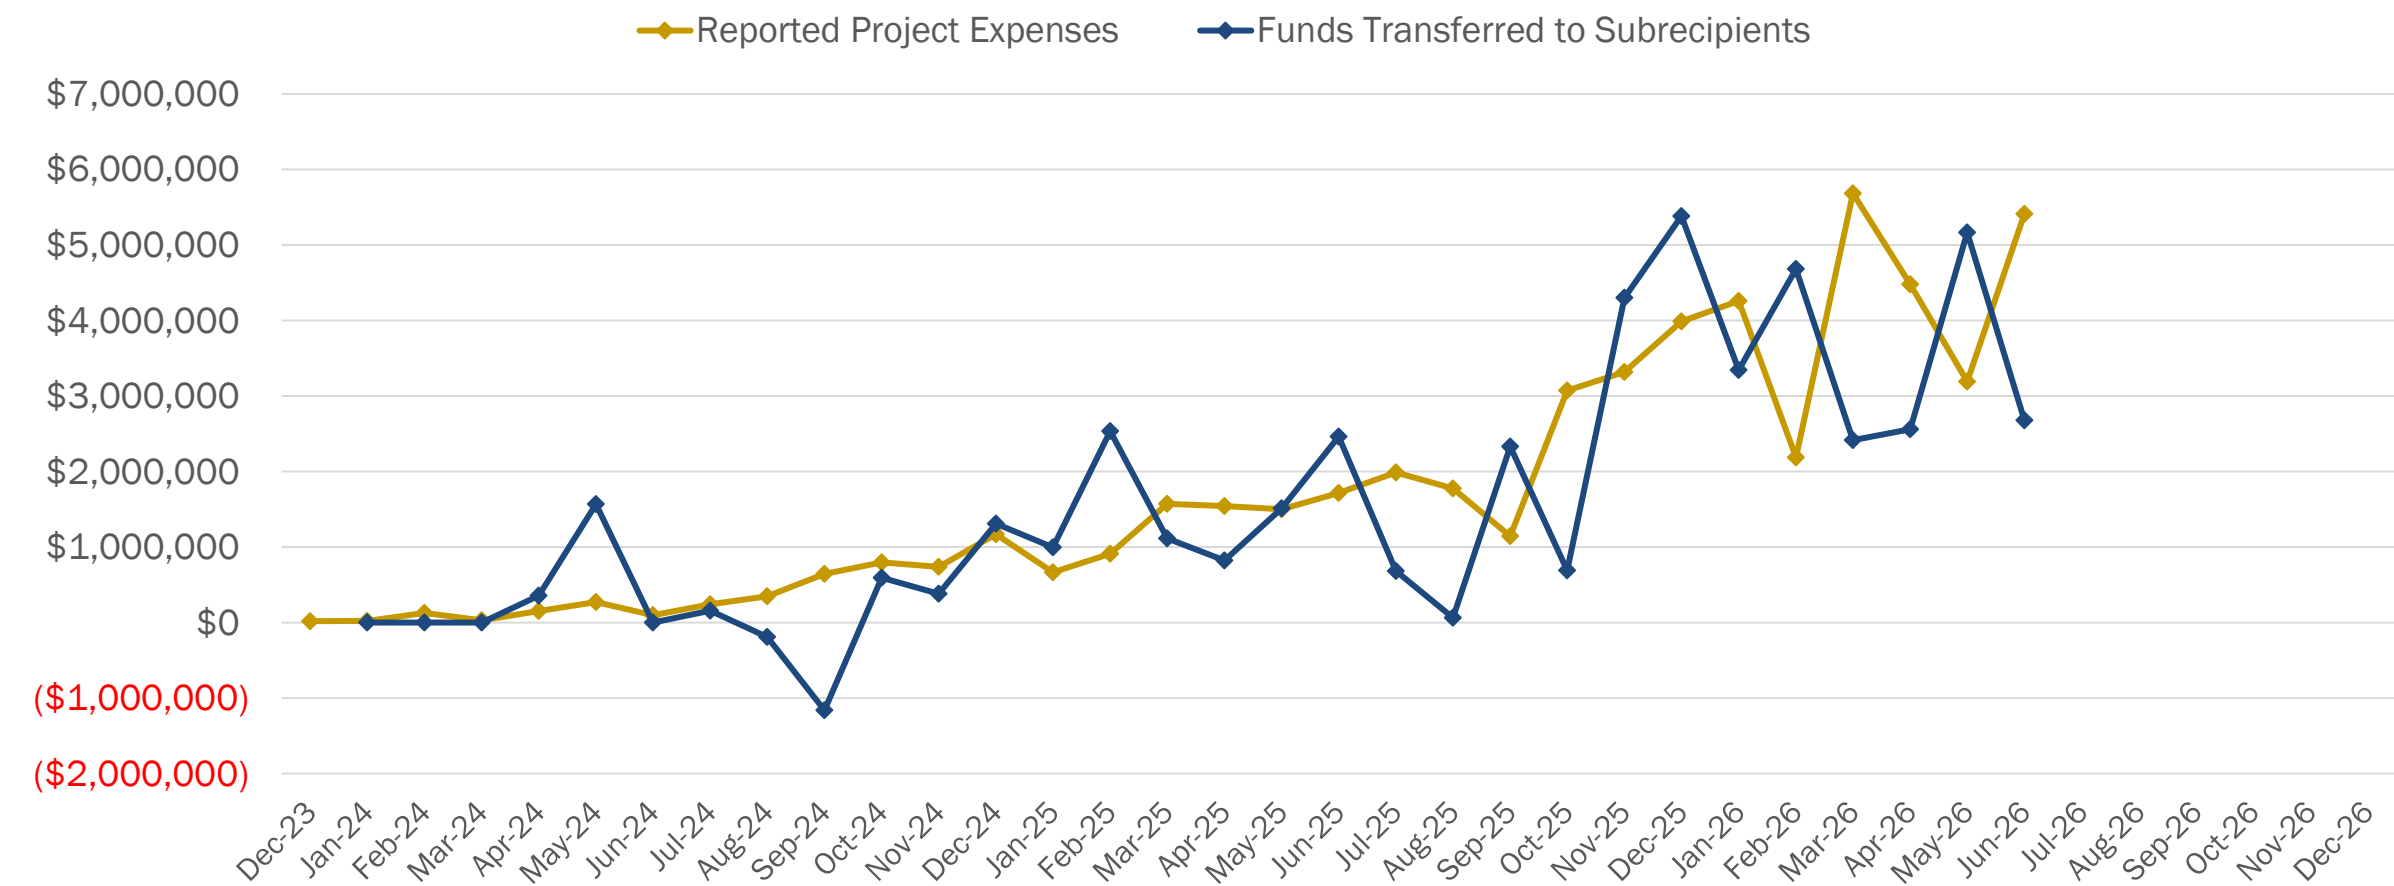

* In August & September 2024, PRO reclaimed funds previously distributed to subrecipients to comply with the Cash Management Improvement Act (CMIA). Four projects were impacted. All projects have since complied with CMIA and continue to draw down funds from PRO.

CLC Cumulative Financials

Data as of FY2026 Q4

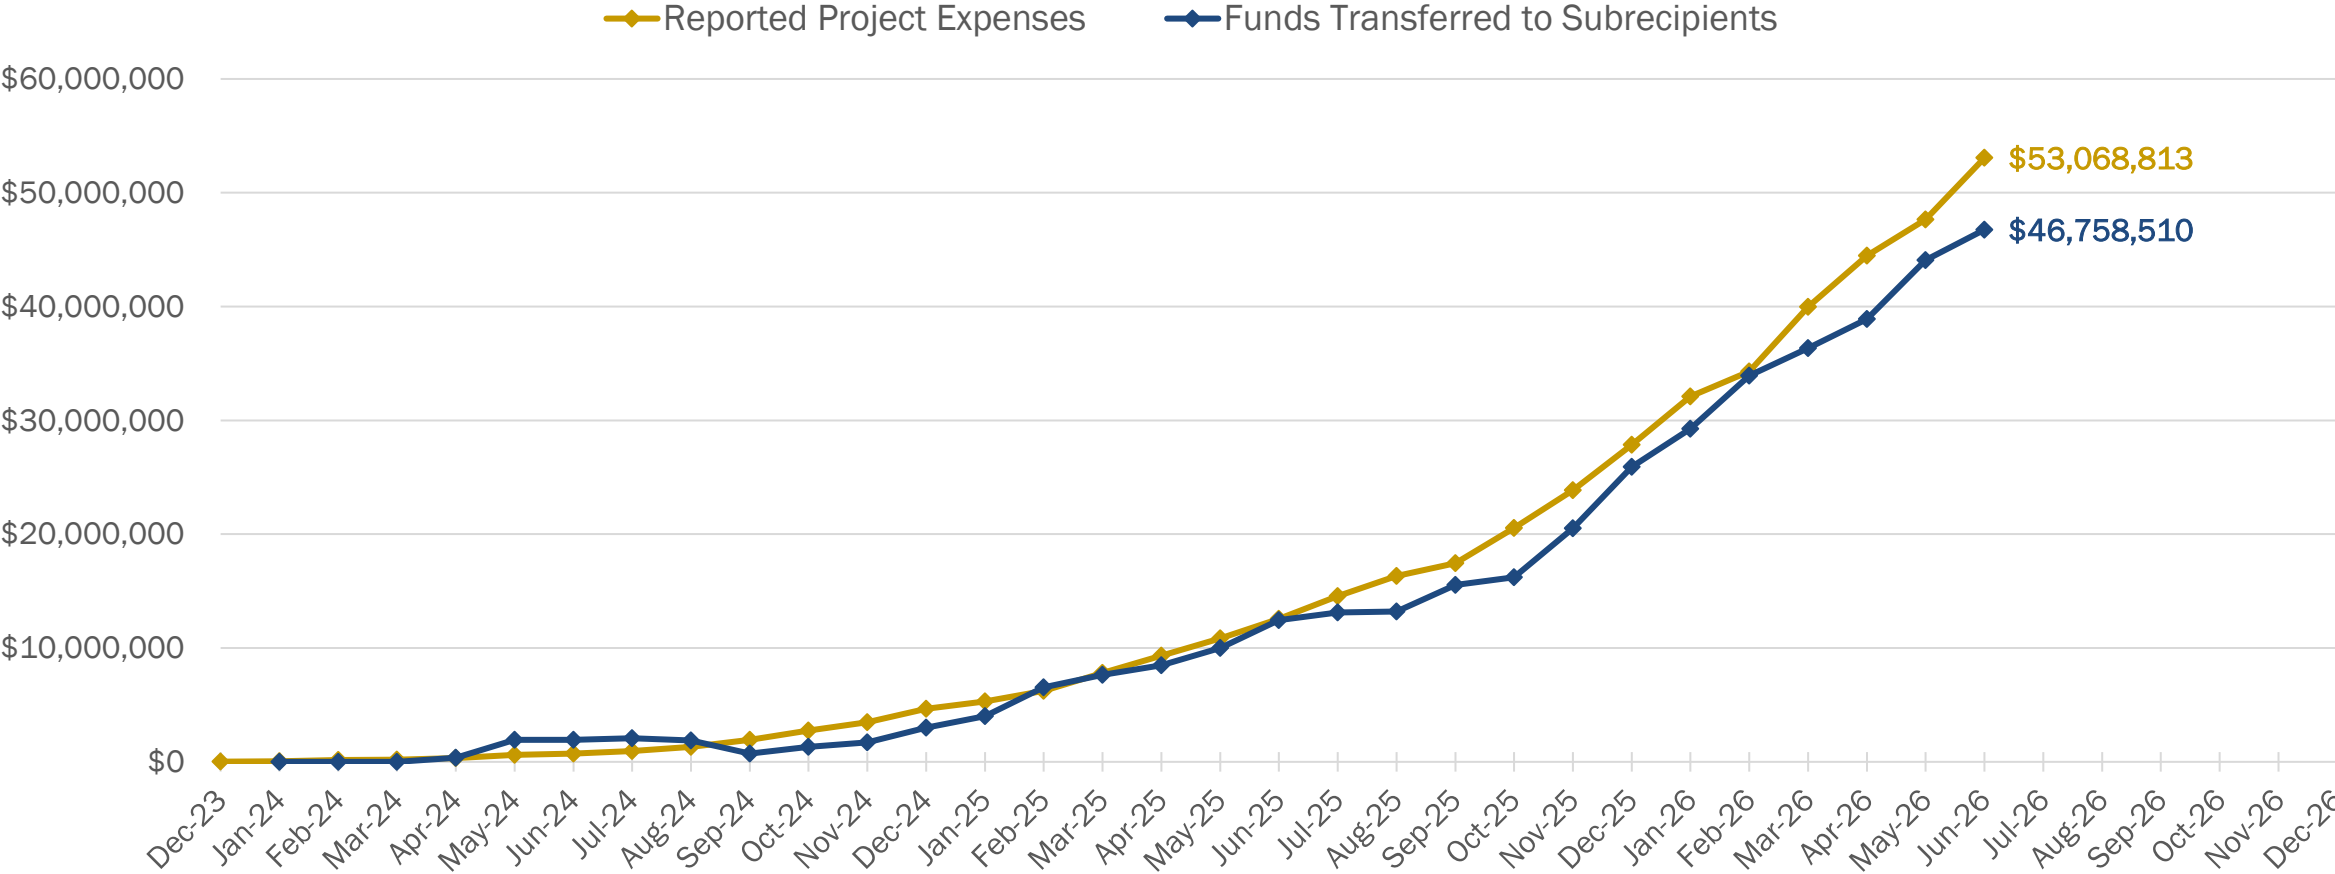


* In August & September 2024, PRO reclaimed funds previously distributed to subrecipients to comply with the Cash Management Improvement Act (CMIA). Four projects were impacted. All projects have since complied with CMIA and continue to draw down funds from PRO.

CLC Program Summary


Data as of FY2026 Q4

New Construction
Renovations


CLCs by Construction Type

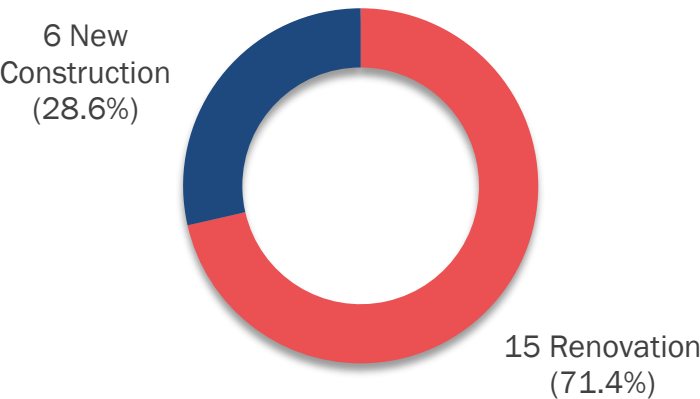


CLCs by Total Project Cost

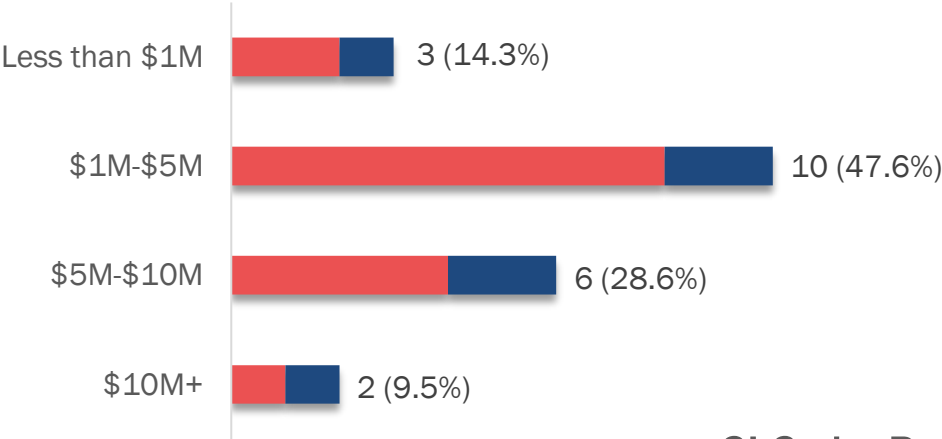

CLCs by Project Square Footage

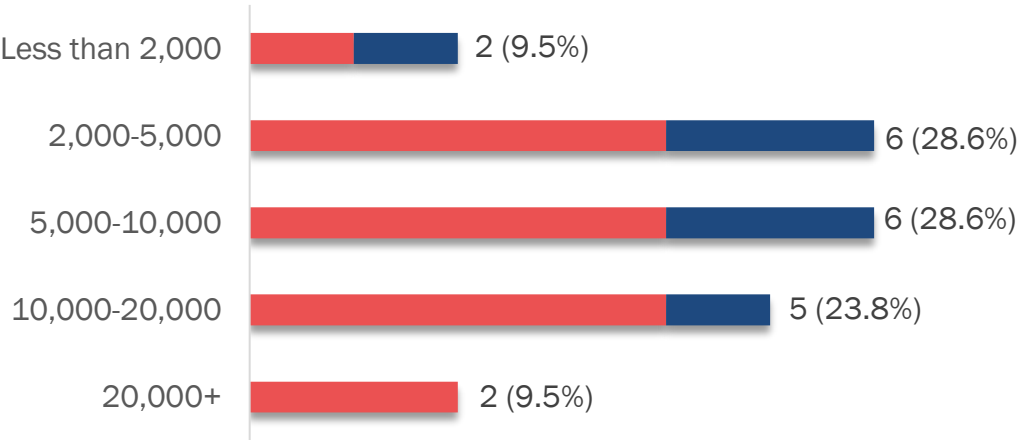

CLCs by Funding Mix

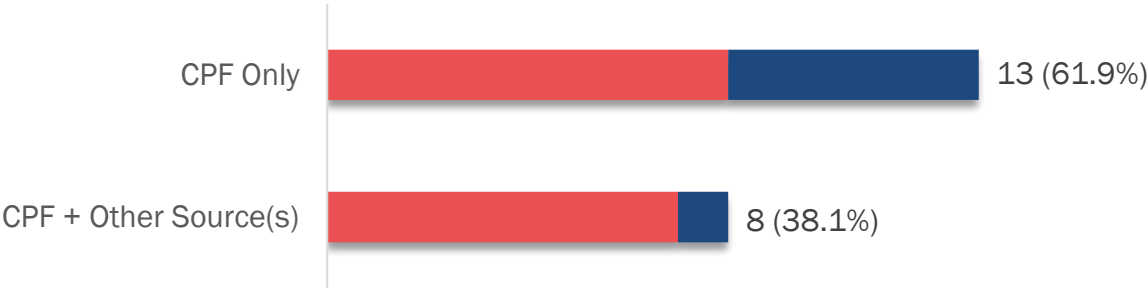



Community Learning Center Municipal Grant

Round 1 Project Update

As of June 30, 2026

**RHODE
ISLAND**

Project Status:
Substantial Completion

As of June 30, 2026

**RHODE
ISLAND**

Manton Library

Glocester
1137 Putnam Pike

CPF award : **\$ 261,259**

Project is 100% funded through CPF



▲ Exterior of the existing building from Putnam Pike

Project Size: **1,320 sf** Asset Type: **Library**

Project Type: **Renovation** Asset Ownership: **Private**


Project Description:

- Renovation of existing community room and three small spaces for moisture remediation and ADA compliance.
- Upgrades to an existing conference room to create three private rooms each one dedicated to telehealth, employment tasks, and educational online classes.


0 Classroom **2** Computer Lab **1** Multipurpose **1** Telemedicine **1** 'Other' Assets

▼ CLC space renovation is complete. Usage of the space has begun.



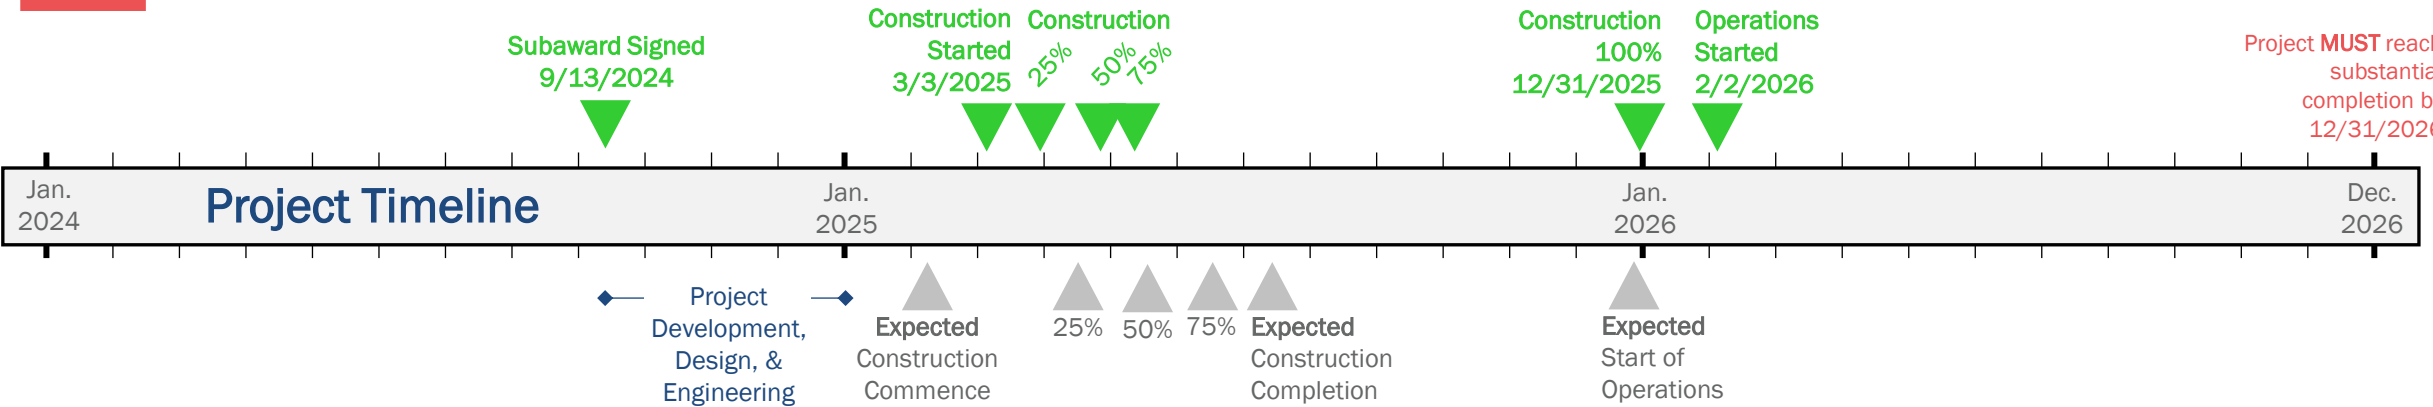


CPF Project Costs

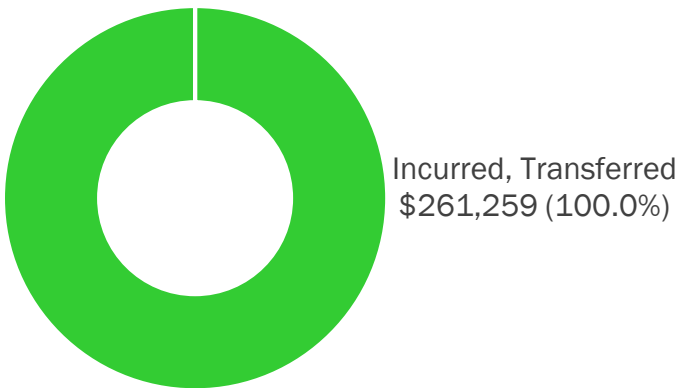

Incurred: Project expenses that have been reported to PRO.

Transferred: CPF funds transferred to subrecipients. Transfers are initiated by subrecipients.

Project Expenses: Planned v. Actual

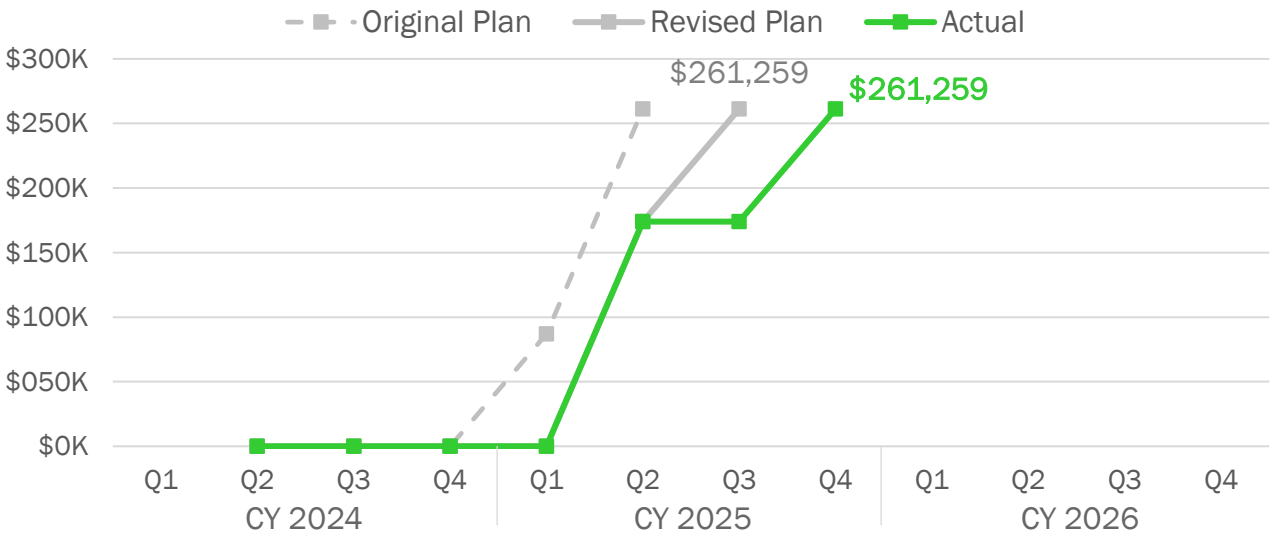

Project Status:
Construction Complete

As of June 30, 2026

**RHODE
ISLAND**

Coventry Community Learning Center

Coventry
1675 Flat River Road

CPF award : **\$ 4,959,564.96**

Total Project Cost : **\$ 5,535,005**

Project is fully funded through CPF, 90%, and town resources 10%



▲ Exterior of the existing building

Project Size: **38,500 sf** Asset Type: **Community Center**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Complete rehabilitation of about one-third of the existing Town Hall Annex building.
- Project will create ADA compliant indoor and outdoor spaces.
- Renovations will include technology and equipment to enable remote access to work, education, and health monitoring.

8

Classroom

2

Computer Lab

3

Multipurpose


3

Telemedicine

10


'Other' Assets

▼ Construction has completed. Furniture, fixtures and equipment have been installed throughout the renovated space.

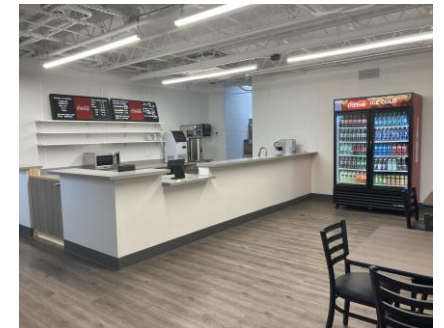


Coventry Community Learning Center

Data as of FY2026 Q4

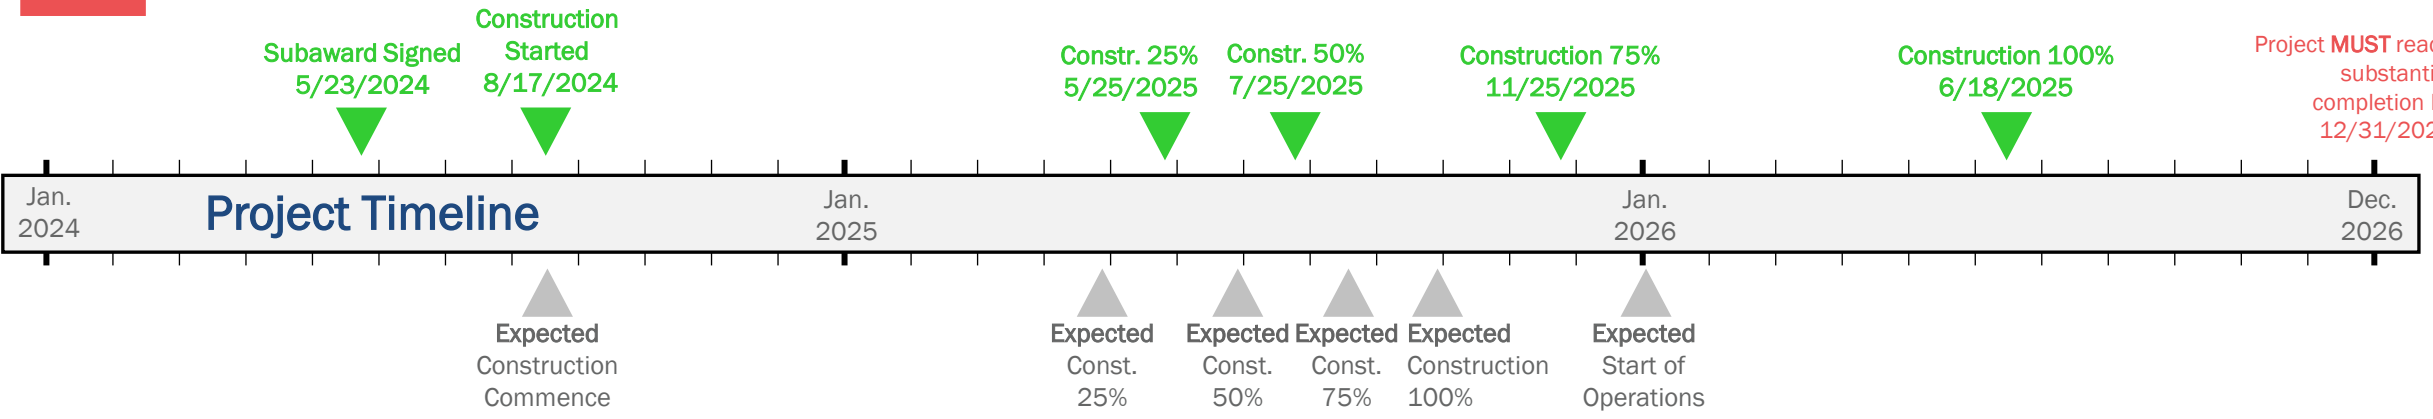


CPF Project Costs

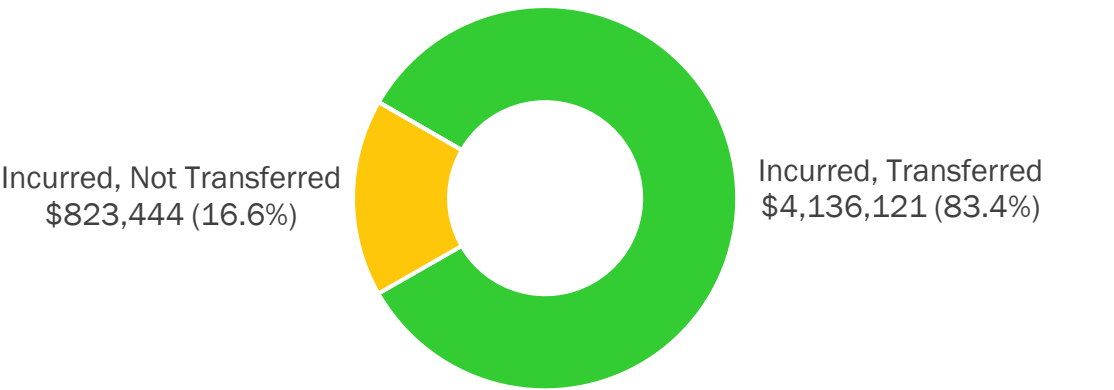

Incurred: Project expenses that have been reported to PRO.

Transferred: CPF funds transferred to subrecipients. Transfers are initiated by subrecipients.

Project Expenses: Planned v. Actual

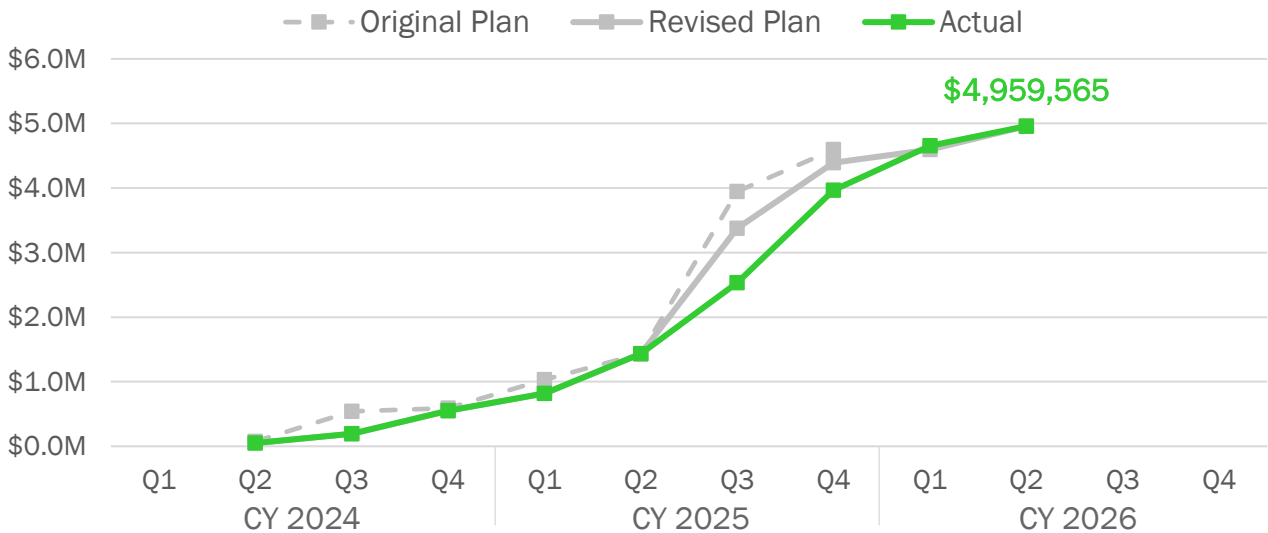

Hopkinton Regional Community Center

Hopkinton
188A Main Street

CPF award : **\$ 2,666,514.04**

Project is 100% funded through CPF



▲ Exterior of the existing building post renovation

Project Size: **2,750 sf** Asset Type: **Community Center**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Full renovation and expansion of Department of Public Works (DPW) storage into ADA compliant community hub.
- New walls, roofing, siding, windows, doors, an accessible lift, mechanical, electrical, plumbing, fire protection, and IT systems.
- Sitework to create new parking lot, new drainage system, and retrofitting the sewage disposal system to current standards.

1

Classroom

0

Computer Lab

4

Multipurpose


1

Telemedicine

4




'Other' Assets

▼ Updated furniture, fixtures and finishes throughout the renovated center

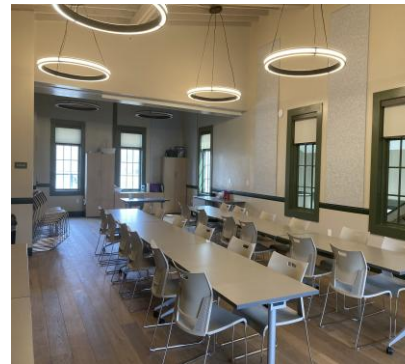

Hopkinton Regional Community Center

Data as of FY2026 Q4

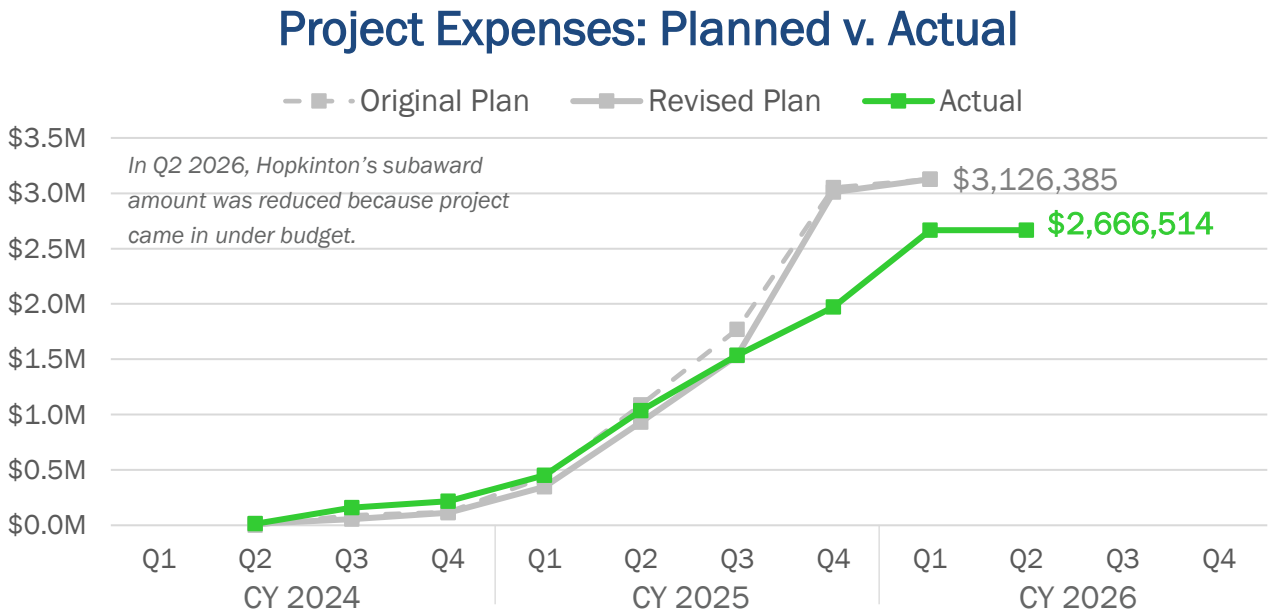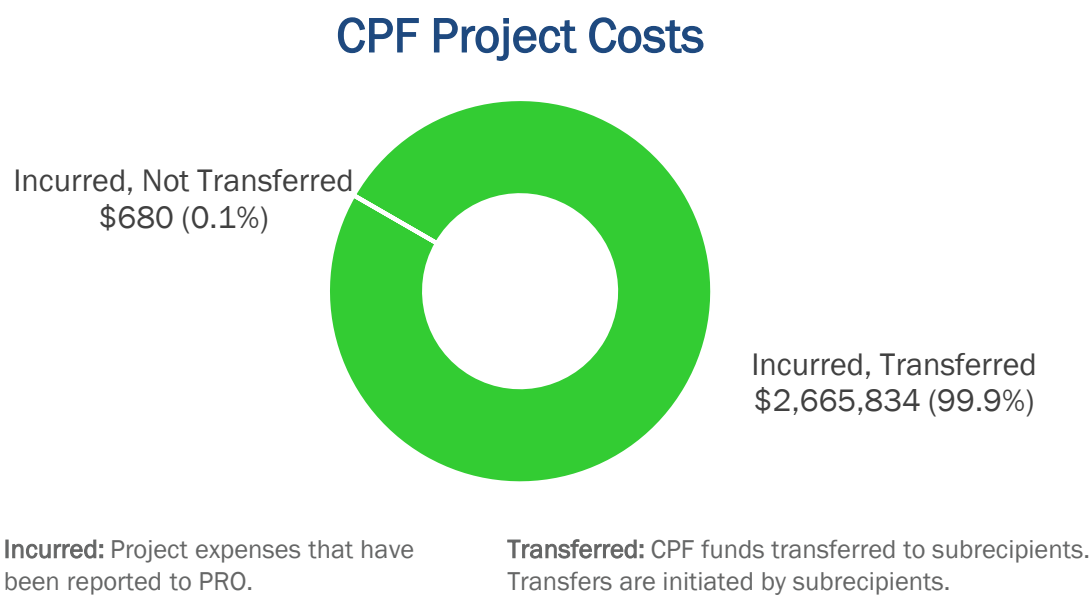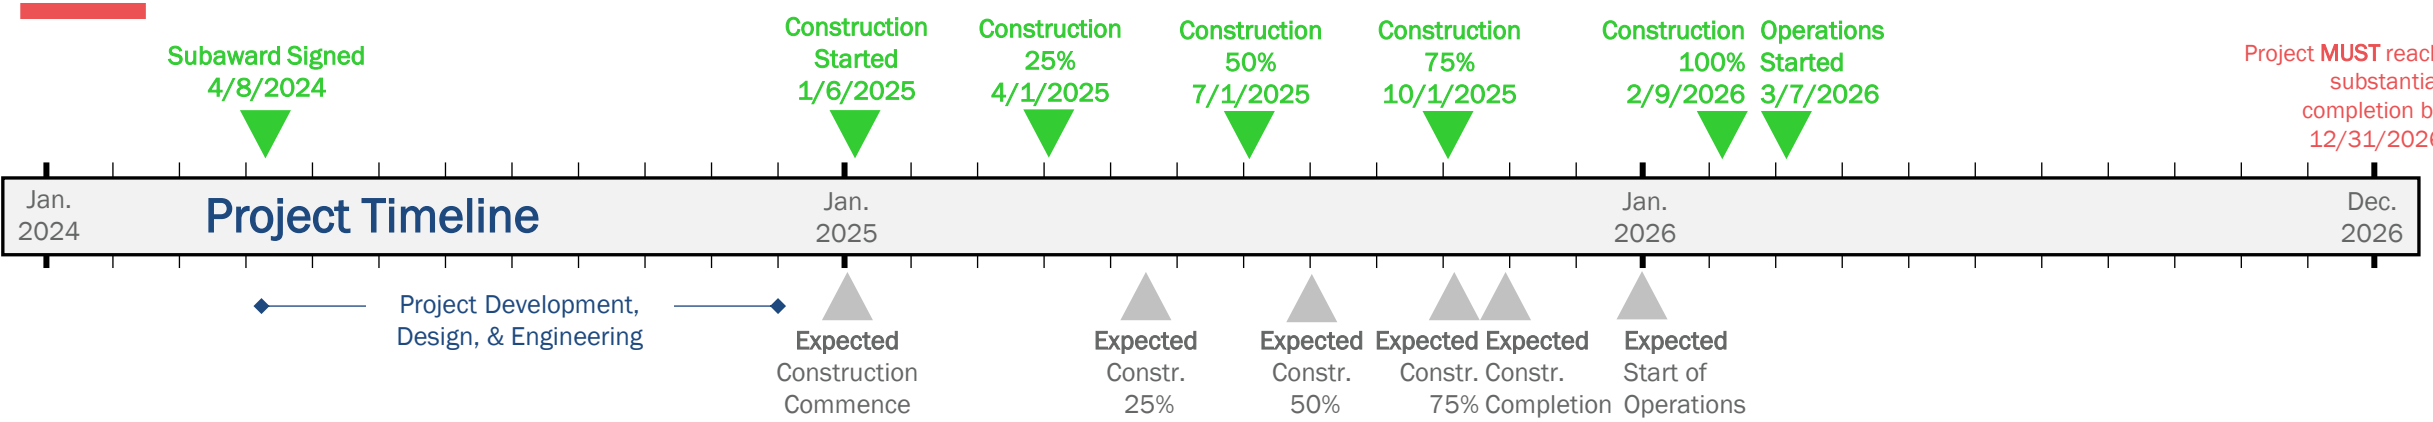

Elmwood Community Center

Providence
75 Atlantic Avenue

CPF award : **\$ 2,701,158**

Project is 100% funded through CPF



▲ Exterior of the existing building

Project Size: **14,000 sf** Asset Type: **Community Center**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Renovation of vacant Elmwood Community Center.
- Mechanical, electrical, plumbing, fire protection, site work, interior fit-out, AV, furniture, fixtures & equipment, access control and security, accessibility, and envelope repairs/upgrades.
- 5 multi-purpose rooms, 1 computer room, 3 private pods, and a large assembly space

0

Classroom

1

Computer Lab

9

Multipurpose

1

Telemedicine

1


'Other' Assets

▼ Renovation complete with updated flooring and furniture, and equipment




Elmwood Community Center

Data as of FY2026 Q4

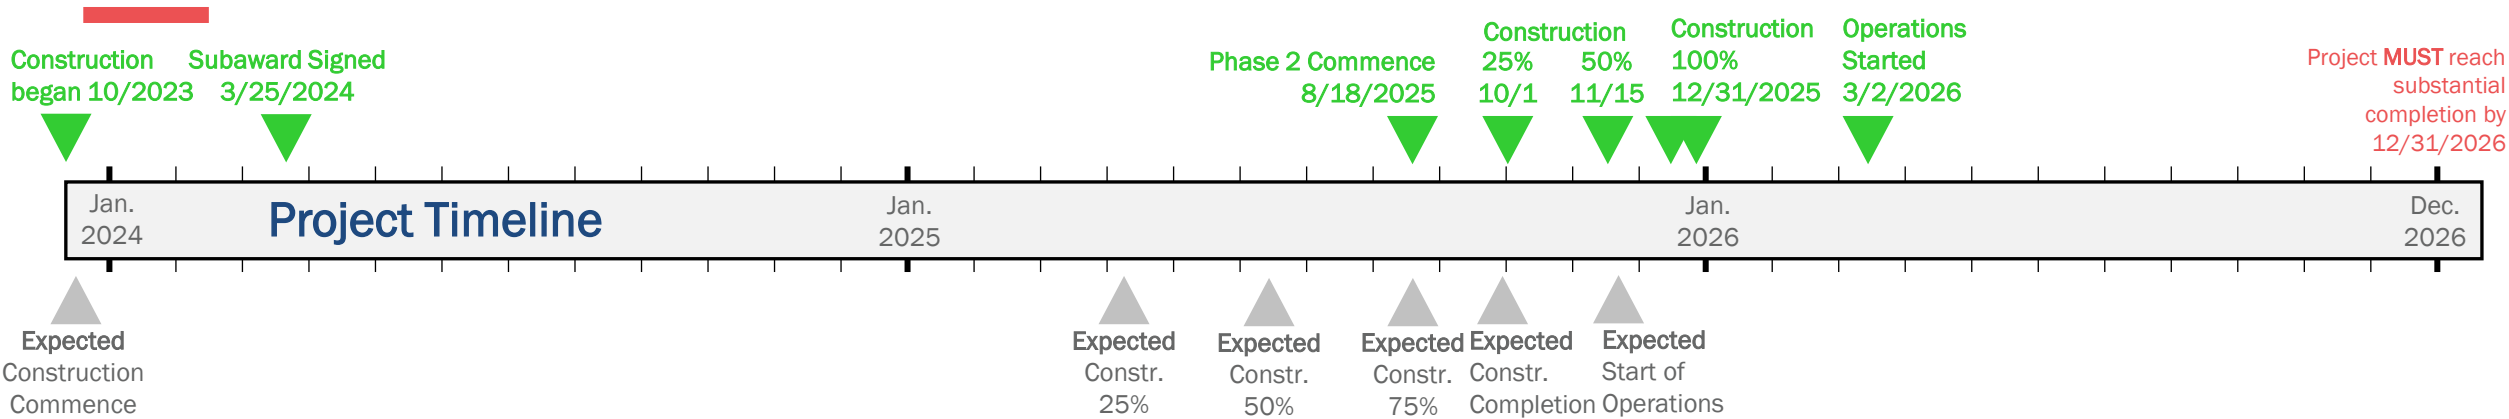


CPF Project Costs

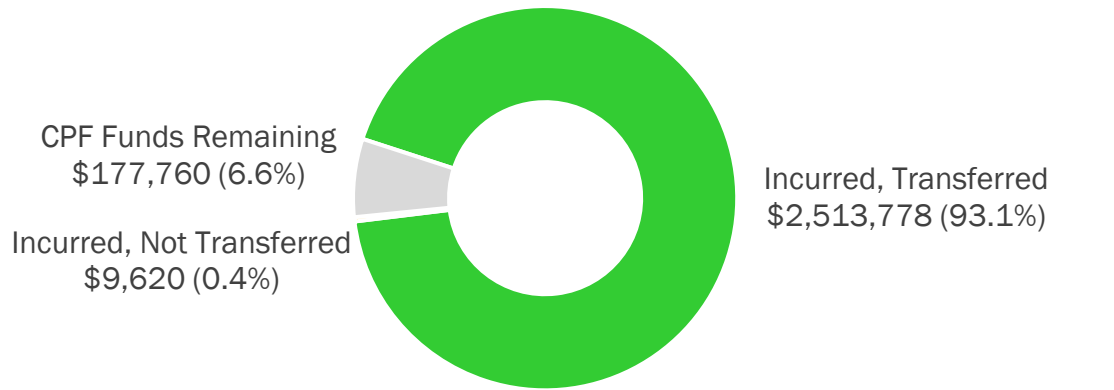

Incurred: Project expenses that have been reported to PRO.

Transferred: CPF funds transferred to subrecipients. Transfers are initiated by subrecipients.

Project Expenses: Planned v. Actual

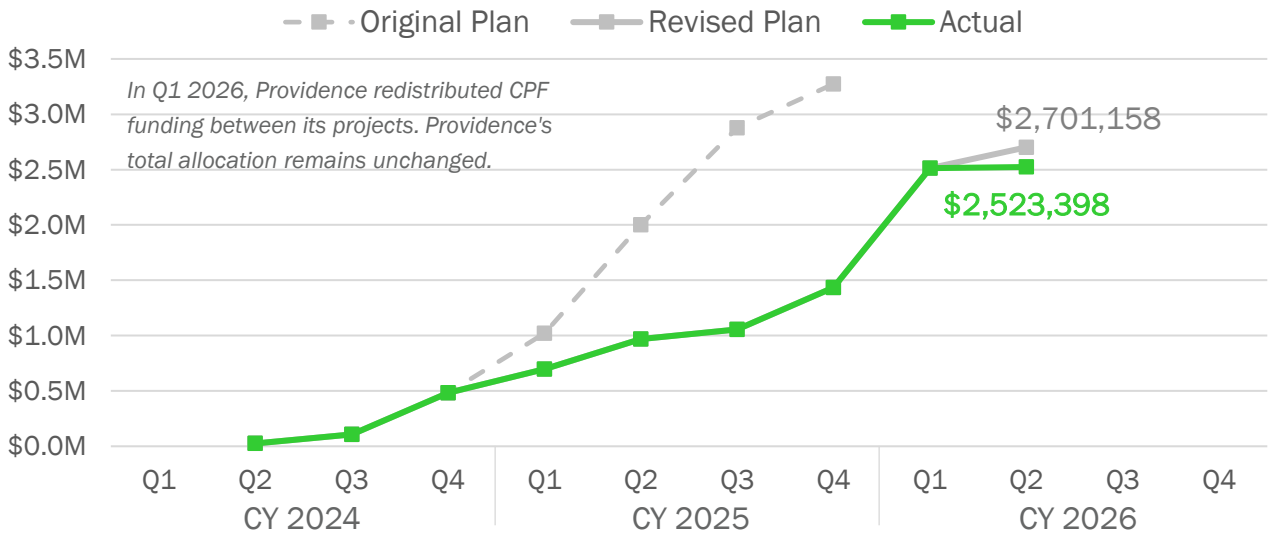

East Smithfield Neighborhood Center

Smithfield
7 Esmond Street

CPF award : **\$ 2,592,961**

Total Project Cost : **\$ 2,952,479**

Project is funded through CPF, 88%, ARPA Local Fiscal Recovery Funds, 9%, and Town Resources, 3%.



▲ Updated exterior of the building from Esmond Street.

Project Size: **6,435 sf** Asset Type: **Community Center**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Restoration of the East Smithfield Neighborhood Center (ESNC) into a multi-generational community learning center
- Structural repairs and historic restoration of the main hall, new roof, mechanical, electrical, plumbing, ADA compliant interiors and high-speed internet
- Private workspaces for tele-work, tele-education and tele-health

0

Classroom

1

Computer Lab

9

Multipurpose

1

Telemedicine

14


'Other' Assets

▼ Interior and exterior work is complete. FF&E has been installed.



East Smithfield Neighborhood Center

Data as of FY2026 Q4

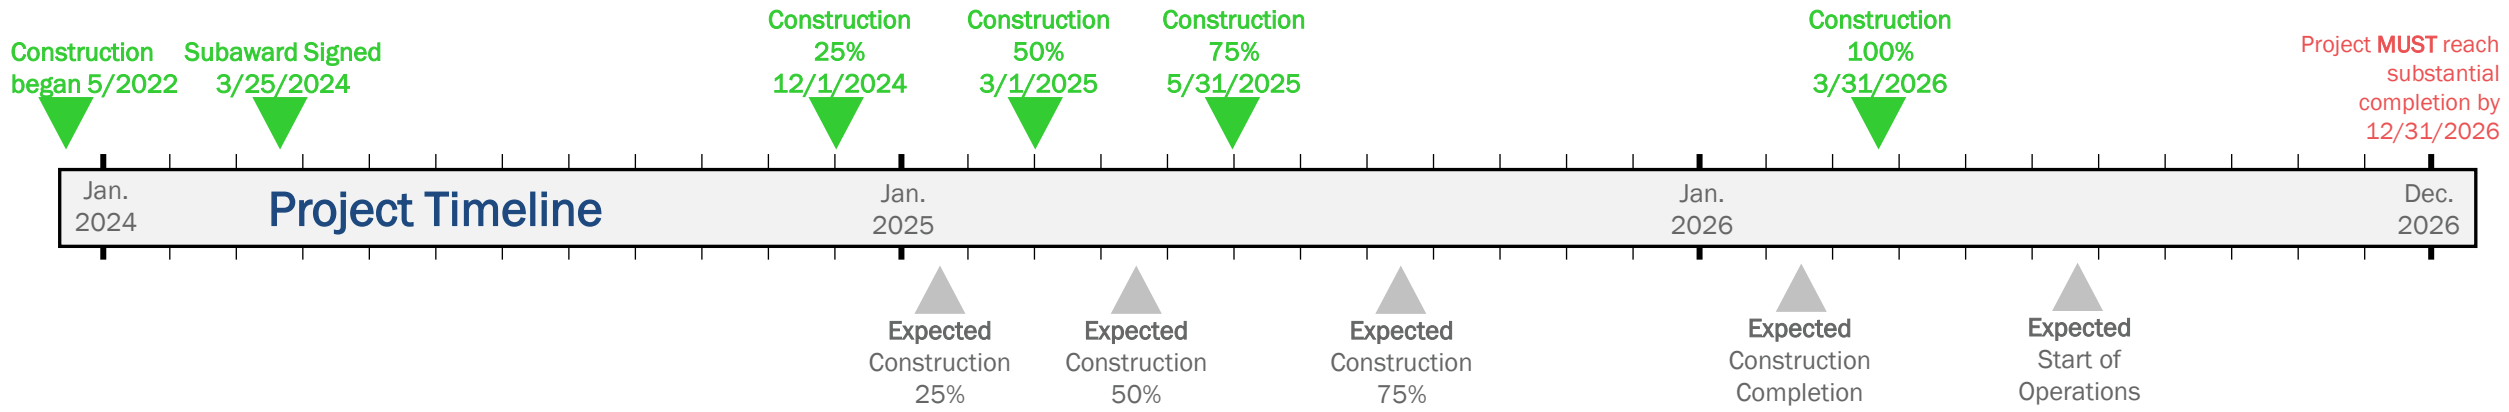


CPF Project Costs



Incurred: Project expenses that have been reported to PRO.

Transferred: CPF funds transferred to subrecipients. Transfers are initiated by subrecipients.

Project Expenses: Planned v. Actual

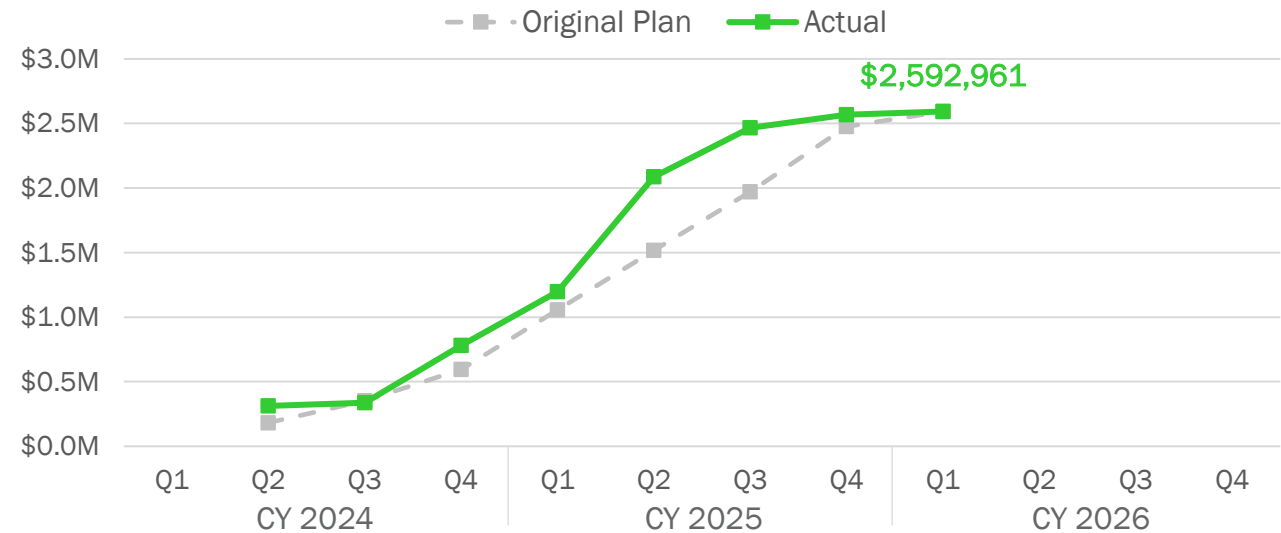

Project Status:
Under Construction

As of June 30, 2026

**RHODE
ISLAND**

Bay Spring Community Center

Barrington
170 Narragansett Avenue

CPF award : **\$ 1,686,732**

Project is 100% funded through CPF



▲ Rendering of the Bay Springs Community Center

Project Size: **2,367 sf** Asset Type: **Community Center**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Renovation of the first floor – garage bay conversion.
- Ramp construction to meet ADA accessibility requirements.
- Plumbing, electrical, heating and cooling upgrades; structural reinforcement, new lighting, etc.
- Spaces: meeting room, reception area, and three “office pods”.

0

Classroom

2

Computer Lab

1

Multipurpose

1

Telemedicine

3

‘Other’ Assets

▼ Renovated exterior of the community center




▼ Renovated garage bay




Bay Spring Community Center

Data as of FY2026 Q4

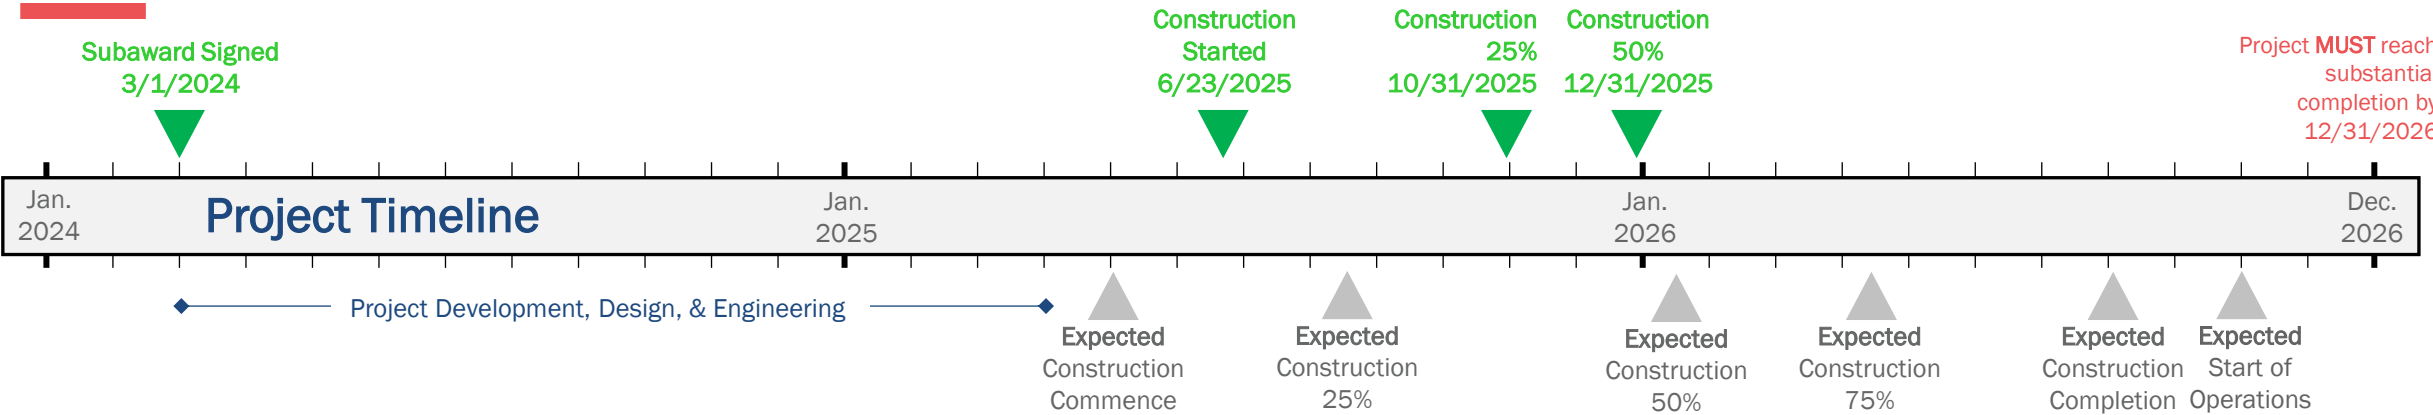


CPF Project Costs

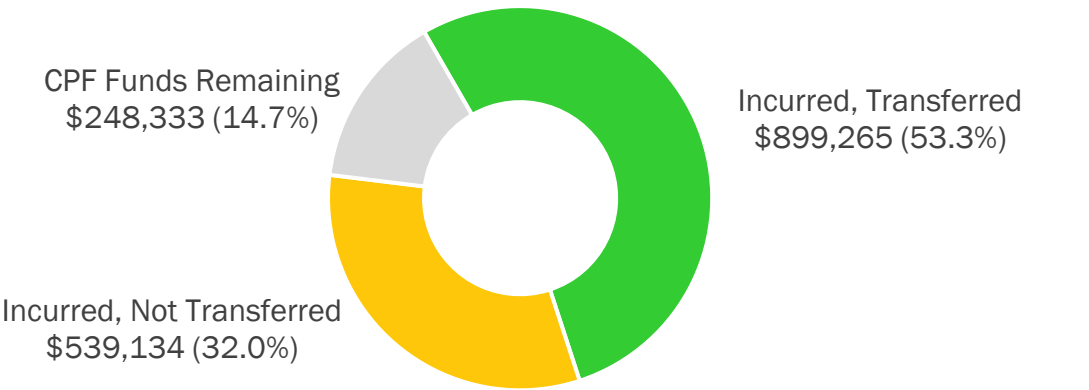

Incurred: Project expenses that have been reported to PRO.

Transferred: CPF funds transferred to subrecipients. Transfers are initiated by subrecipients.

Project Expenses: Planned v. Actual

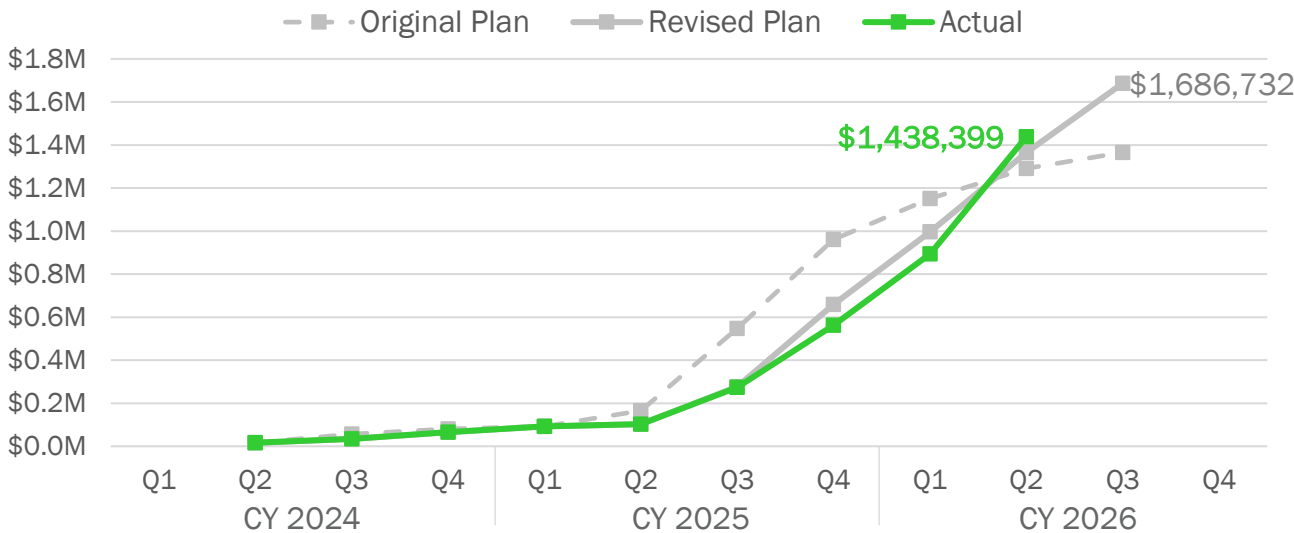

Rogers Free Library

Bristol
525 Hope Street

CPF award : **\$ 1,971,967**

Total Project Cost : **\$ 2,075,900**

Project is funded through CPF, 95%, and a private donation, 5%



▲ Exterior of the library from Hope Street

Project Size: **25,000 sf** Asset Type: **Library**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Partial interior renovation of the Rogers Free Library (1,200 sf).
- New Makerspace and five private spaces with ethernet wiring and computer access for telehealth & private work.
- Building-wide improvements: carpeting, HVAC, security systems, and general repairs.


0 Classroom **0** Computer Lab **5** Multipurpose **2** Telemedicine **0** 'Other' Assets

▼ Renovation of the Library mezzanine, quiet rooms and maker space has been completed




Rogers Free Library


Data as of FY2026 Q4

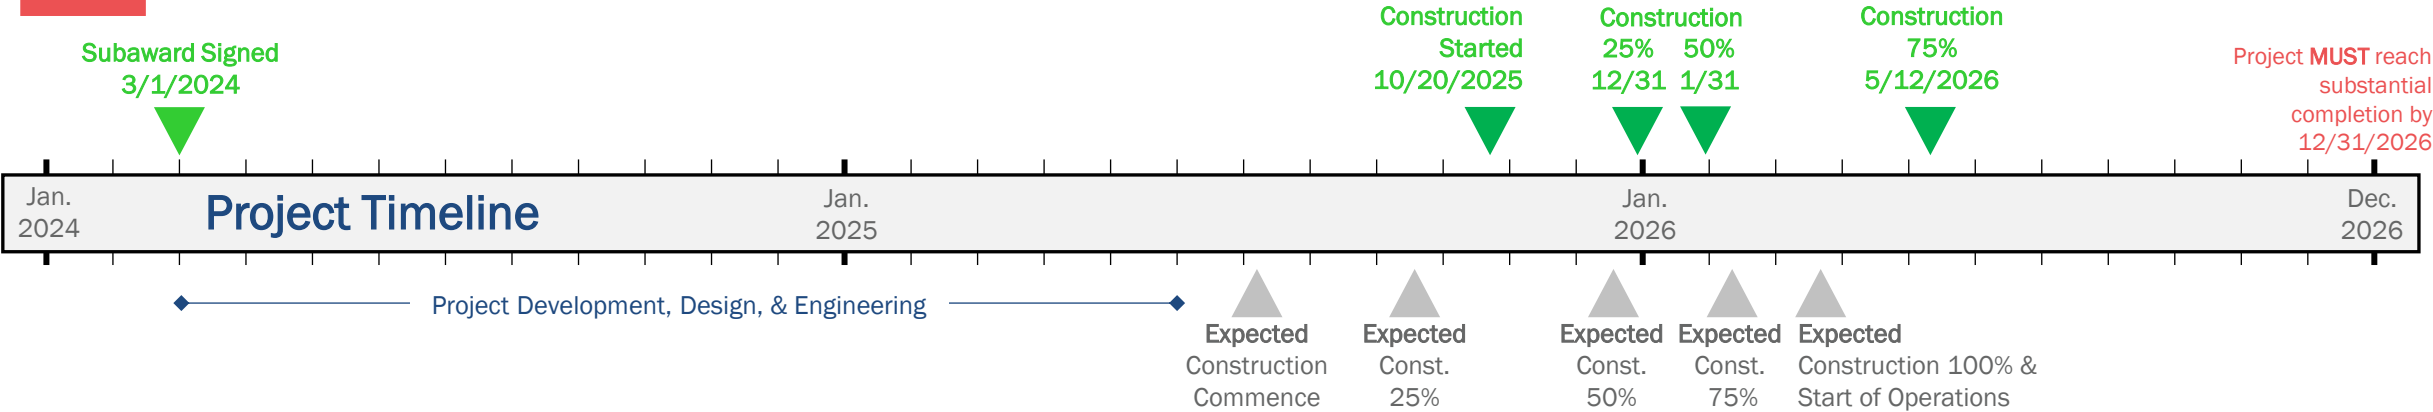

CPF Project Costs

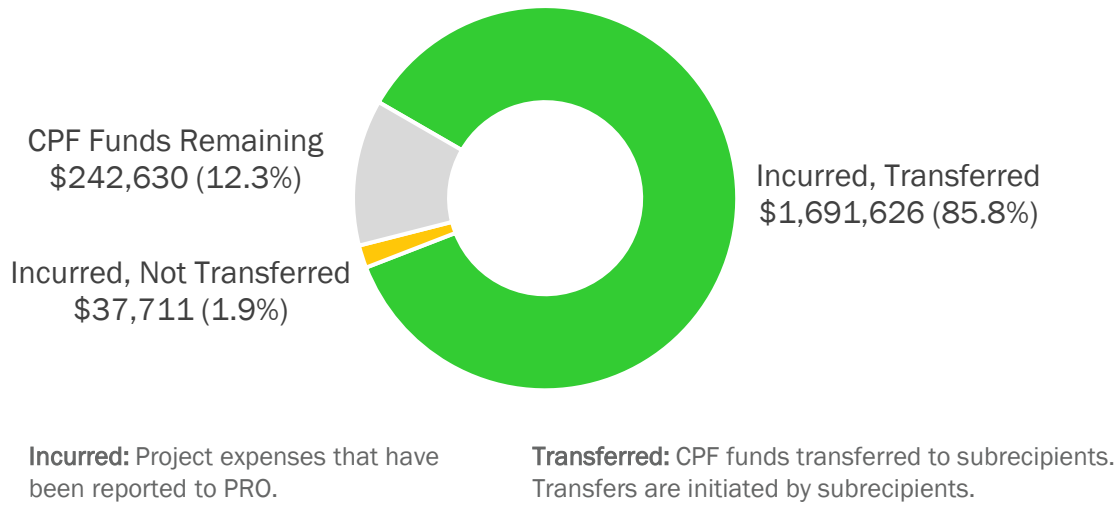

Project Expenses: Planned v. Actual

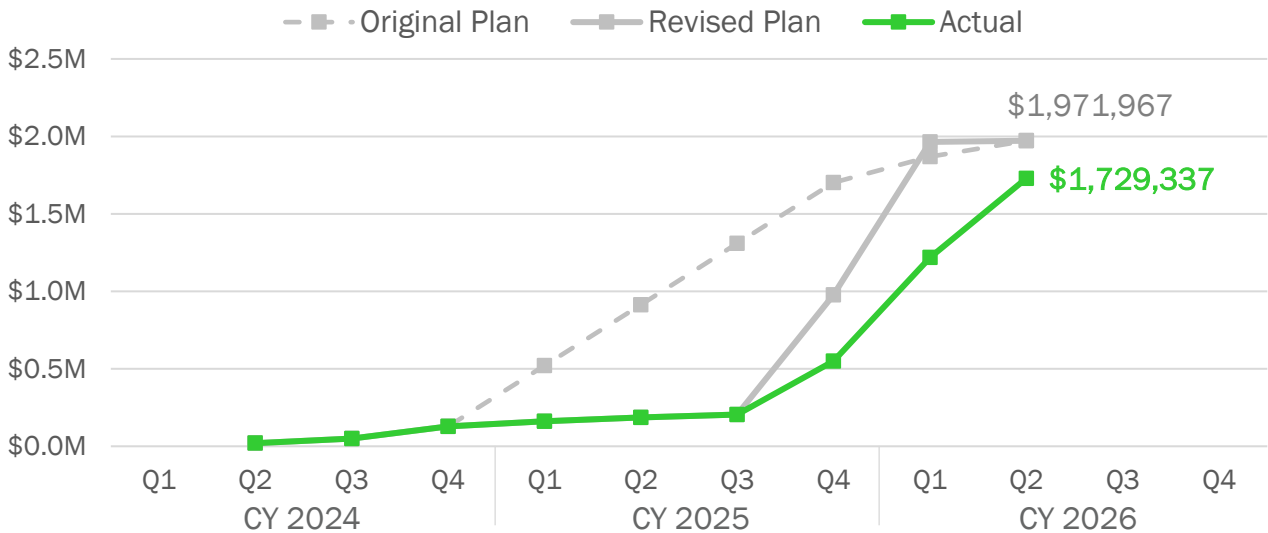

El Centro

Central Falls
702 Broad Street

CPF award : **\$ 8,985,198**

Total Project Cost : **\$ 13,064,698**

Project is funded through CPF, 69%, and other federal funding sources and private donations, 31%



▲ Rendering of the updated building exterior from Broad Street

Project Size: **19,500 sf** Asset Type: **Community Center**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Early 1900s historic building will be gutted and re-built, while keeping the shell and historical attributes.
- Major work includes new roof, façade restoration, replacement of windows, flooring, new elevator, mechanical, electrical, plumbing, and fire protection systems.

2

Classroom

8

Computer Lab

1

Multipurpose

3

Telemedicine


1




'Other' Assets

▼ Interior repairs continue on all floors of the building.



▼ Rear addition

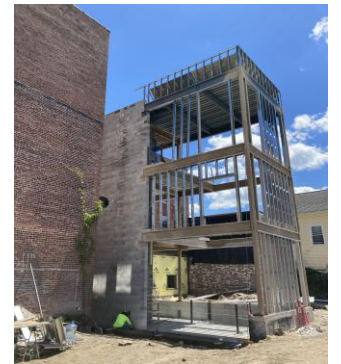

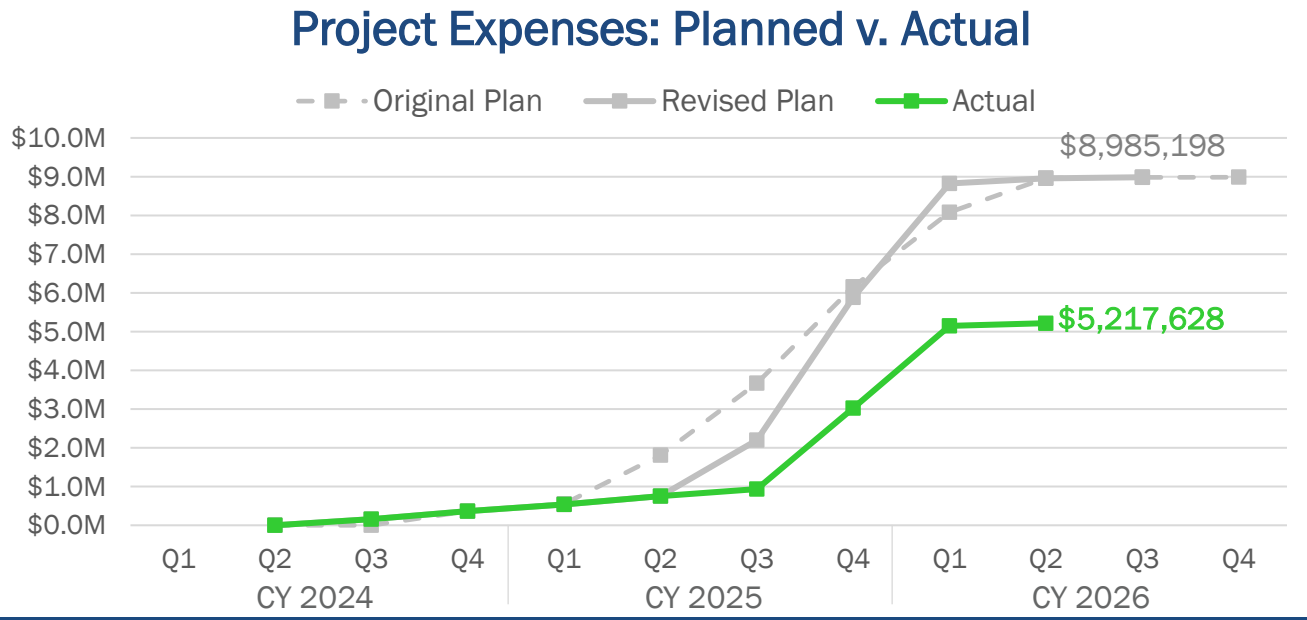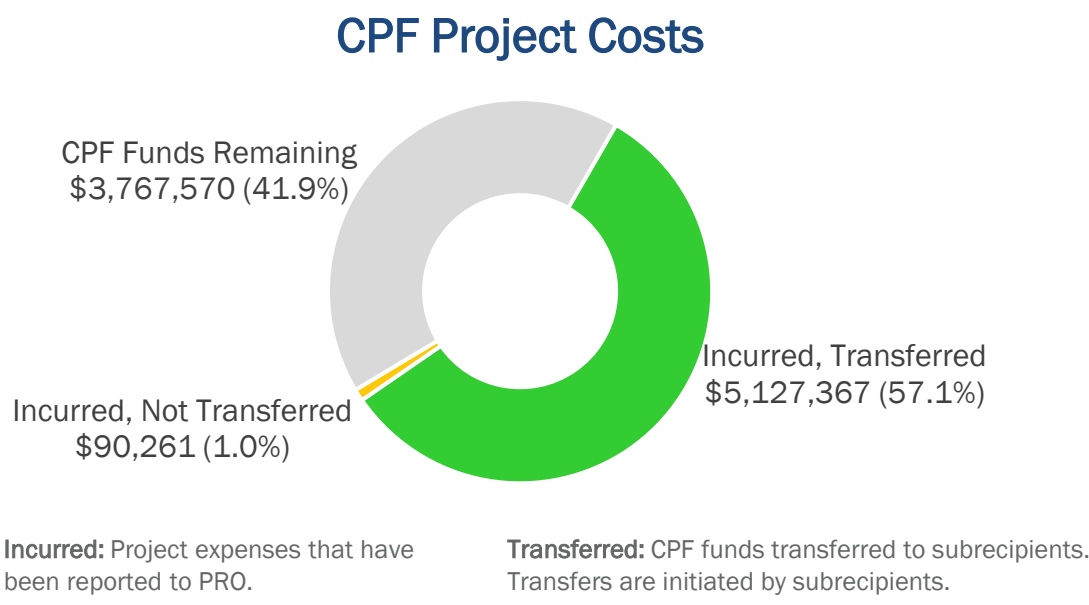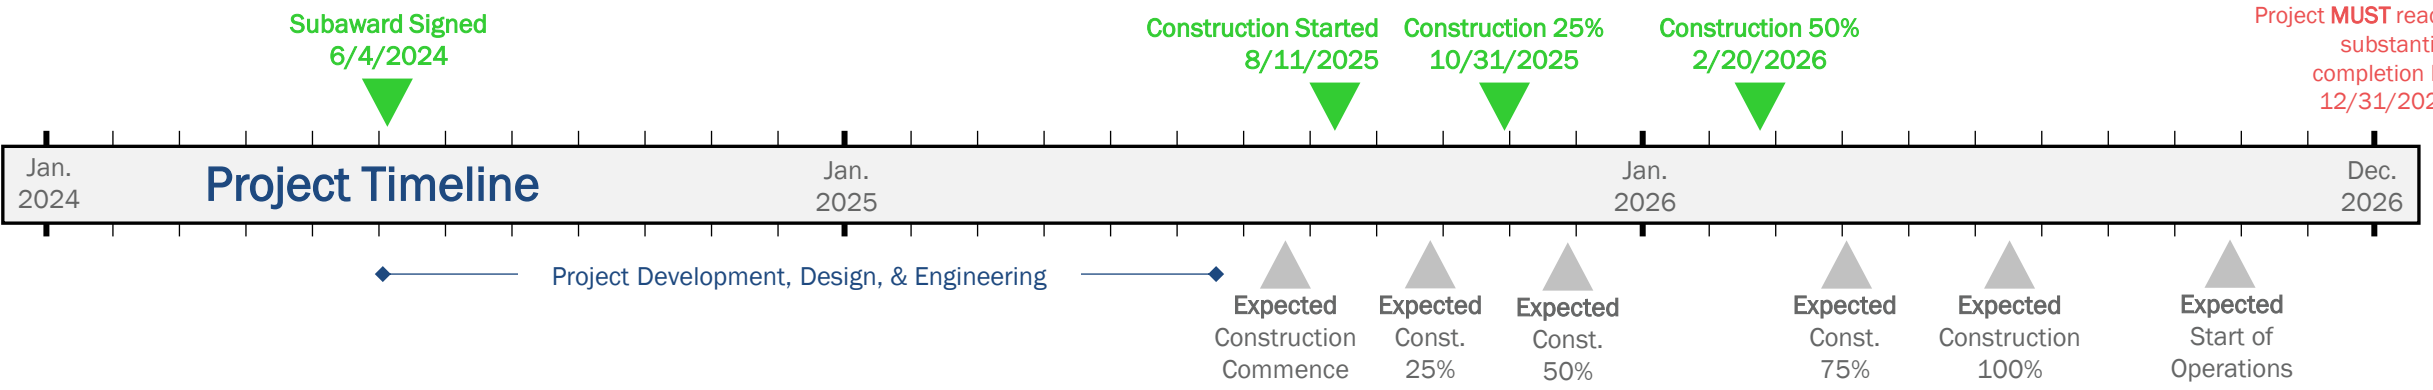

Cross Mills Public Library

Charlestown
4417 Old Post Road

CPF award : **\$ 673,368**

Project is 100% funded through CPF



▲ Exterior of the library from the parking lot

Project Size: **2,450 sf** Asset Type: **Library**

Project Type: **Renovation** Asset Ownership: **Non-Profit**

Project Description:

- Interior renovations throughout the 1st floor, basement and conveying systems include flooring, finishes, and furnishing.
- Creation of new private meeting spaces with acoustic and technological provisions to allow remote access to work, education, and health monitoring activities.

0

Classroom

0

Computer Lab

2

Multipurpose

1

Telemedicine

2

'Other' Assets

▼ Newly created private space in basement




▼ New privacy glass for large meeting space




Cross Mills Public Library

Data as of FY2026 Q4

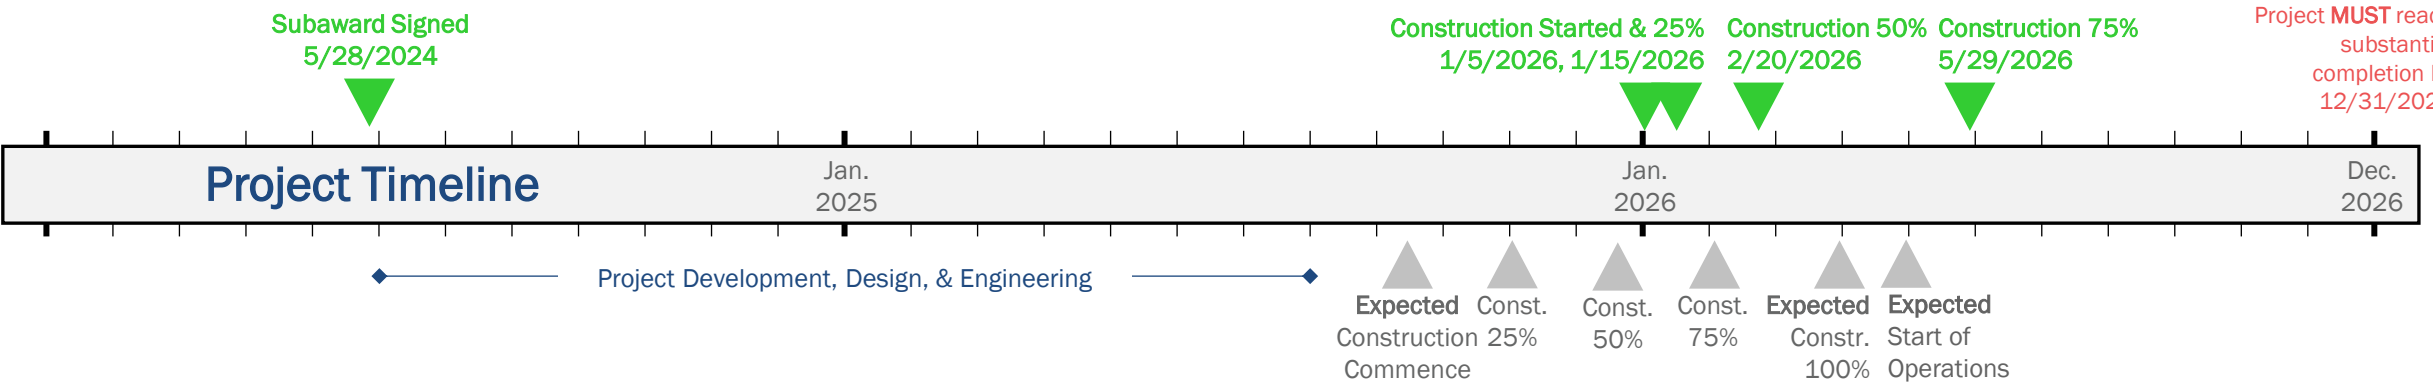


CPF Project Costs

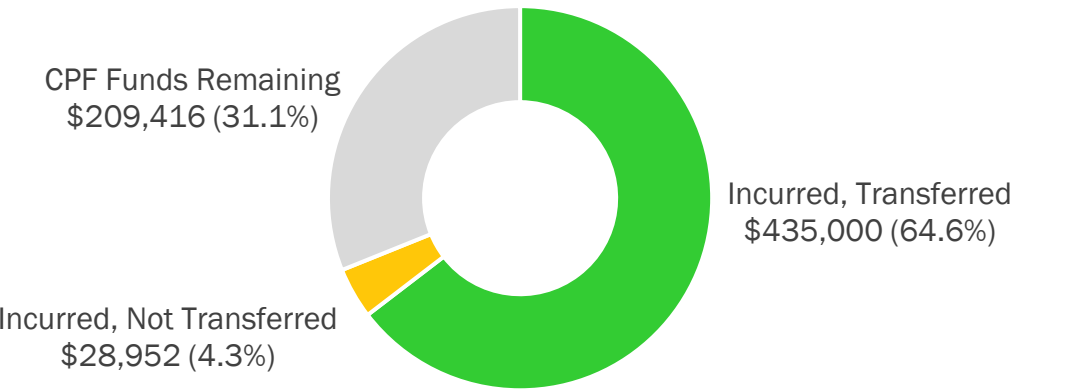

Incurred: Project expenses that have been reported to PRO. **Transferred:** CPF funds transferred to subrecipients. Transfers are initiated by subrecipients.

Project Expenses: Planned v. Actual

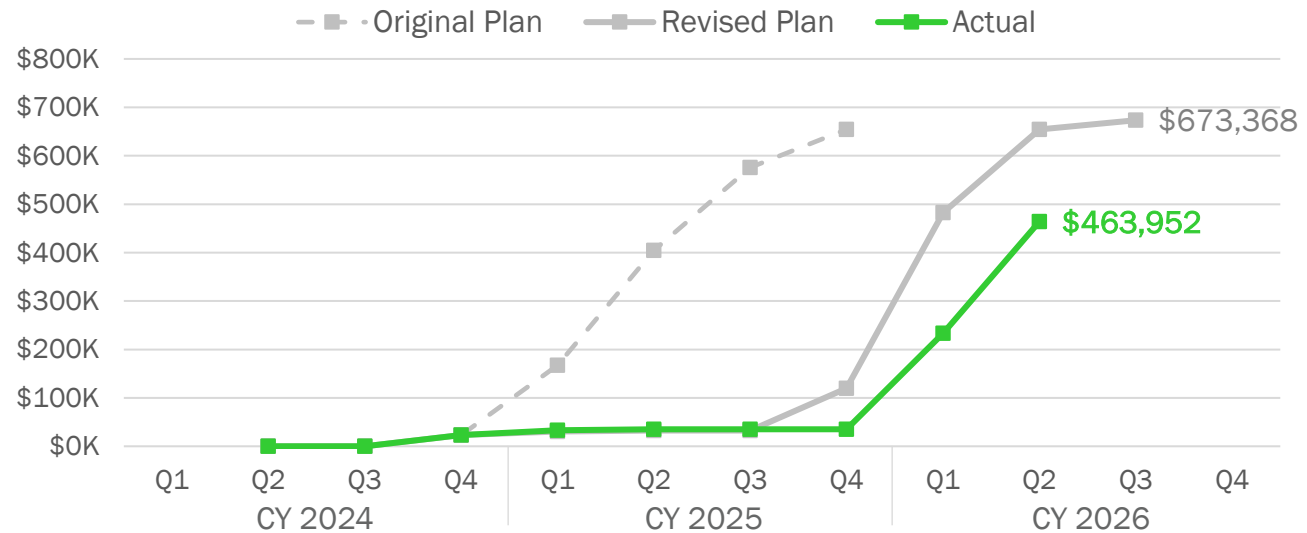

Wellness Hub at Amaral Building & Heritage Park

Cumberland
16 Mill Street

CPF award : \$ 3,118,159

Total Project Cost : \$ 4,118,159

Project is fully funded through CPF, 76%, and a Community Development Block Grant, 24%



▲ Updated exterior façade; front and back of the building

Project Size: 9,302 sf Asset Type: Community Center

Project Type: Renovation Asset Ownership: Municipal

Project Description:

- Adaptive reuse and site development to create ‘Wellness Hub’ that ties together the Amaral Building and Heritage Park.
- This includes an outdoor classroom, flexible learning space in the Amaral Building, a designated telehealth and community paramedicine office.

1

Classroom

1

Computer Lab

2

Multipurpose

1

Telemedicine

7


‘Other’ Assets

▼ Interior finishes and furnishing are complete throughout building.




Wellness Hub at Amaral Building & Heritage Park

Data as of FY2026 Q4

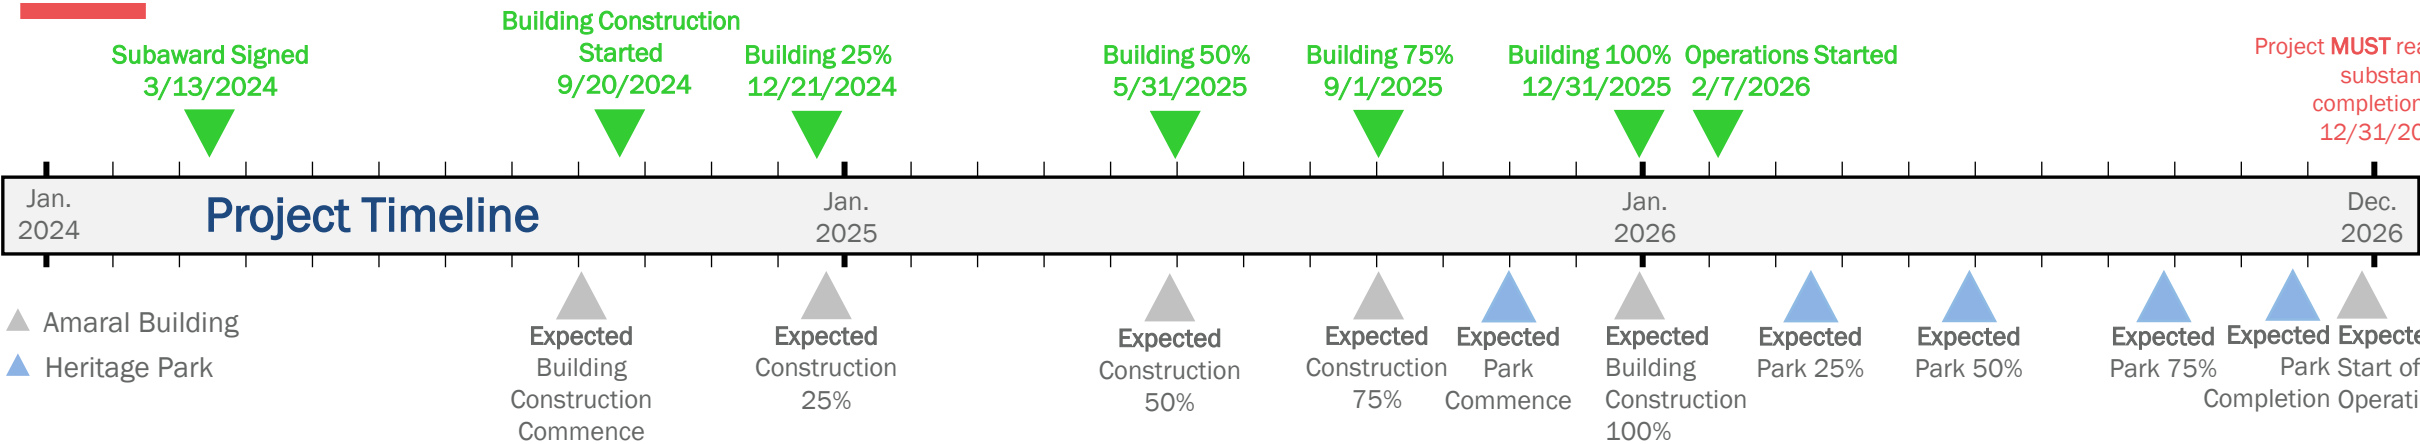


CPF Project Costs

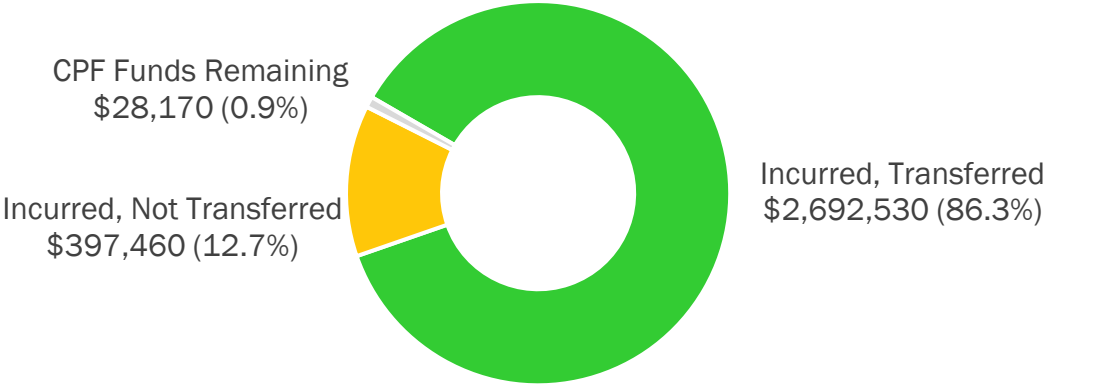

Incurred: Project expenses that have been reported to PRO.

Transferred: CPF funds transferred to subrecipients. Transfers are initiated by subrecipients.

Project Expenses: Planned v. Actual

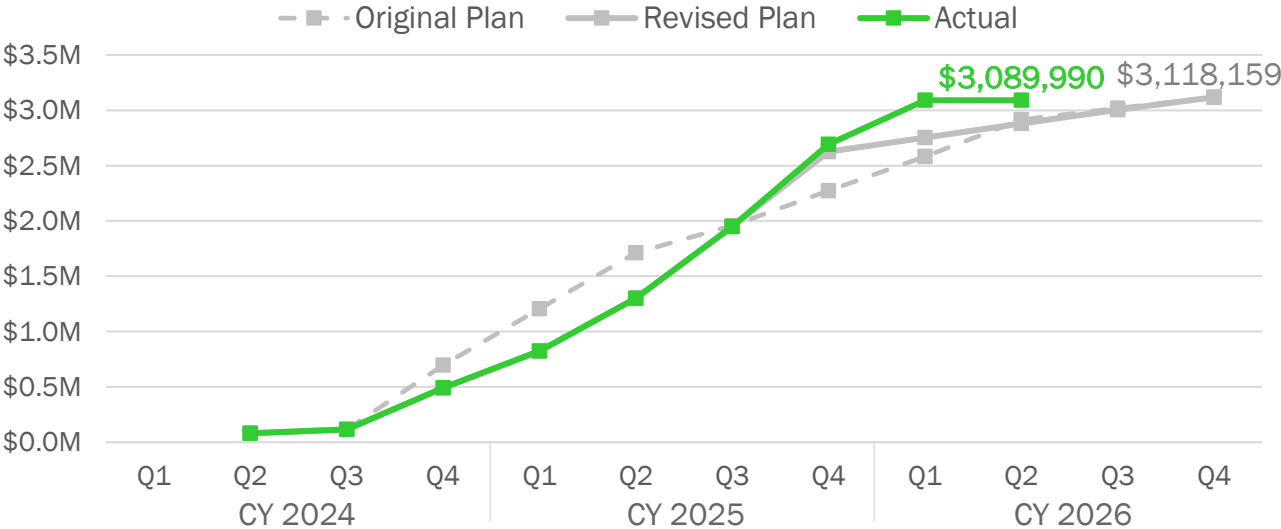

Swift Community Center

East Greenwich
121 Peirce Street

CPF award : **\$ 1,596,800**

Project is 100% funded through CPF



▲ *Rendering of the new addition at Swift Community Center*

Project Size: **2,051 sf** Asset Type: **Community Center**

Project Type: **New Build** Asset Ownership: **Municipal**

Project Description:

- New ~1,400 sf addition to the north of the existing community center, adding two classrooms.
- Renovation of existing space to include a health screening room, additional storage, and hallways to connect to addition.

2

Classroom

1

Computer Lab

1

Multipurpose

1

Telemedicine

1

'Other' Assets

▼ *Exterior masonry & windows are complete*




▼ *Interior framing, mechanical and electrical work is ongoing*




Swift Community Center


Data as of FY2026 Q4

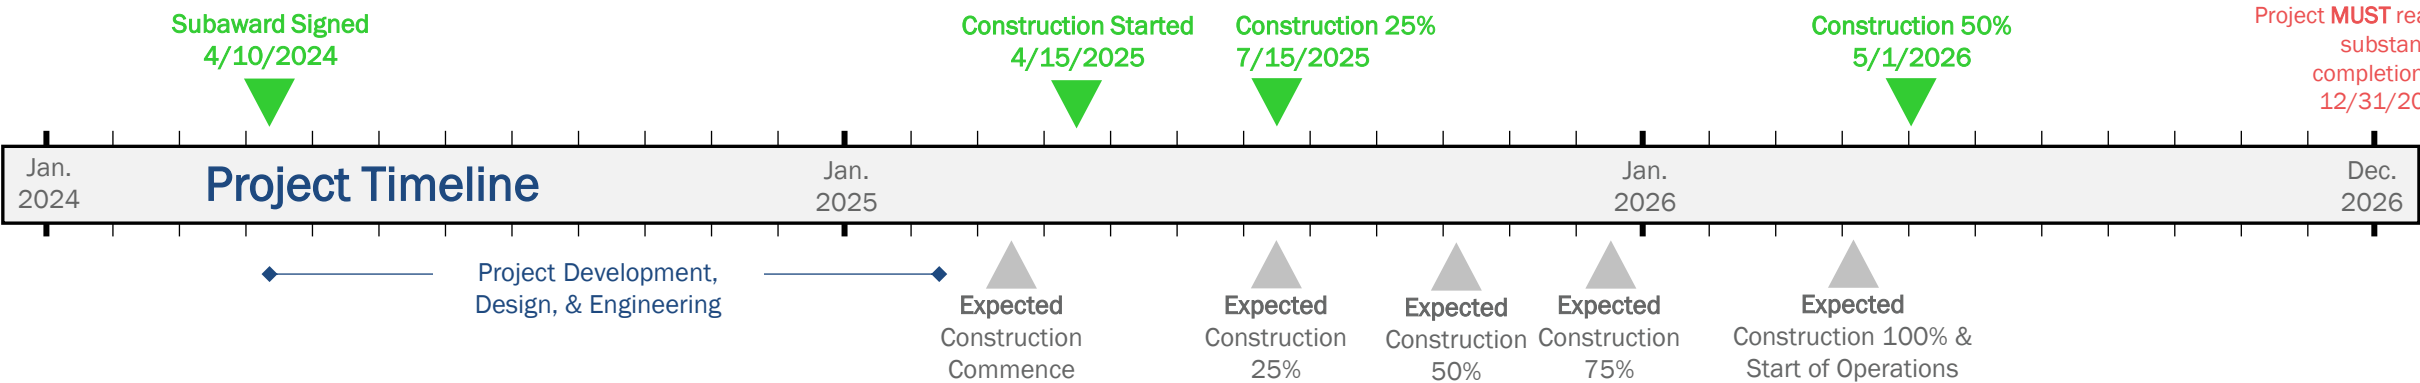

CPF Project Costs

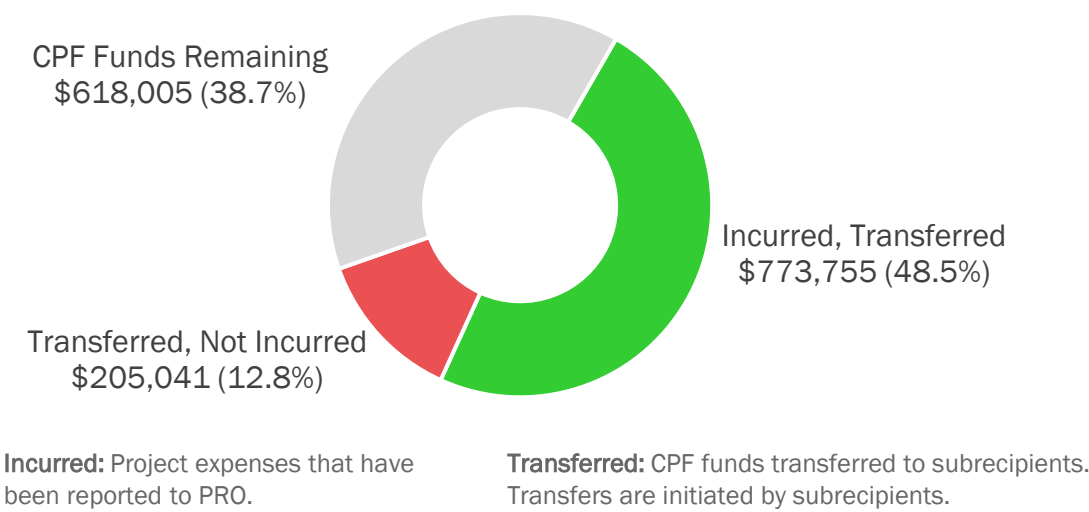

Project Expenses: Planned v. Actual

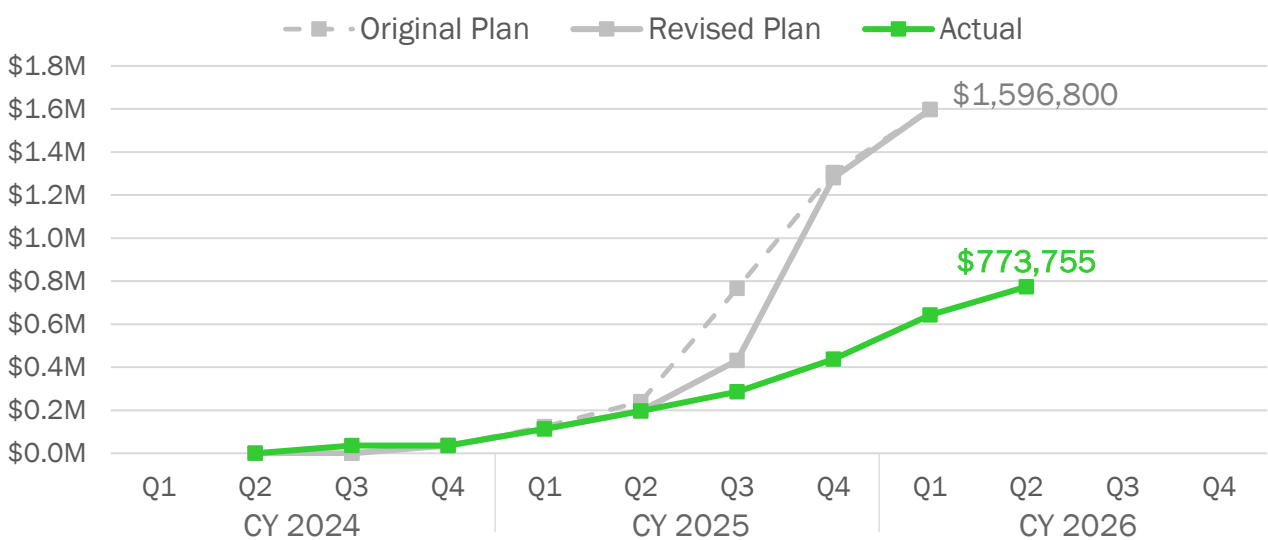

East Providence Community Center

East Providence
610 Waterman Avenue

CPF award : **\$ 10,493,659**

Project is 100% funded through the CPF



▲ New Rendering of the new building exterior

Project Size: **9,803 sf** Asset Type: **Community Center**

Project Type: **New Build** Asset Ownership: **Municipal**

Project Description:

- New construction housing the learning center and recreation center across from high school and adjacent to senior center.
- Pre-engineered metal building; mechanical, electrical, plumbing, fire protection systems, site work, lighting and parking.
- Recreation center constructed through City and Local Fiscal Recovery Funds from ARPA.

0

Classroom

0

Computer Lab

7

Multipurpose

1

Telemedicine

5




'Other' Assets

▼ Steel has been delivered and building erection is ongoing



East Providence Community Center

Data as of FY2026 Q4

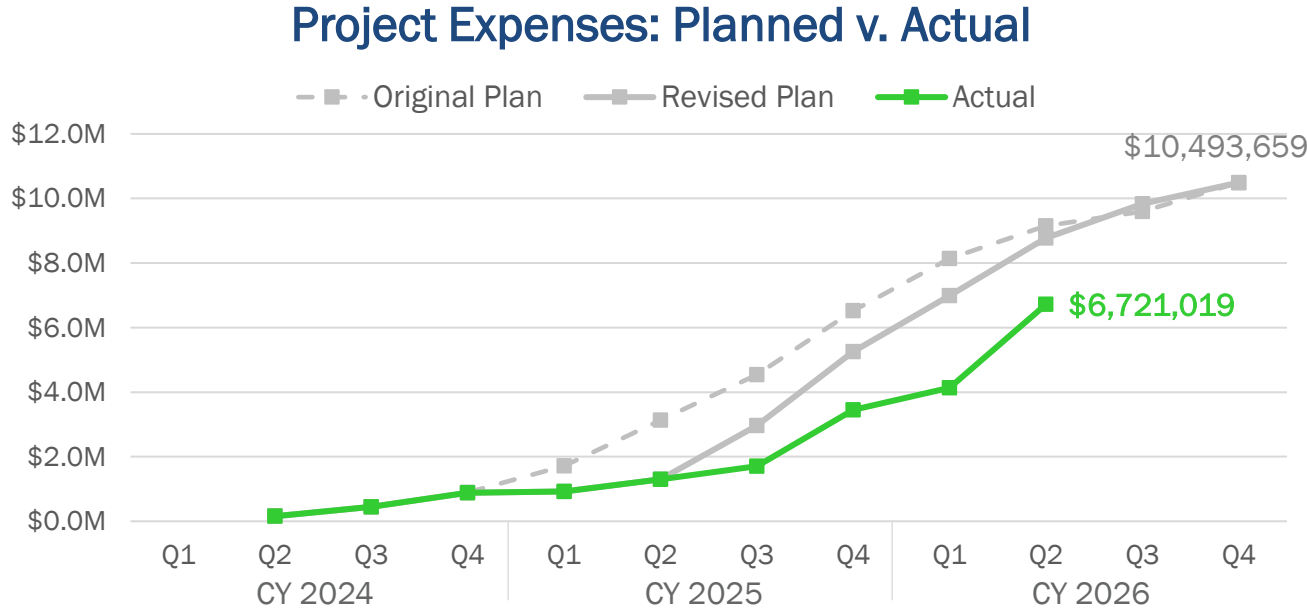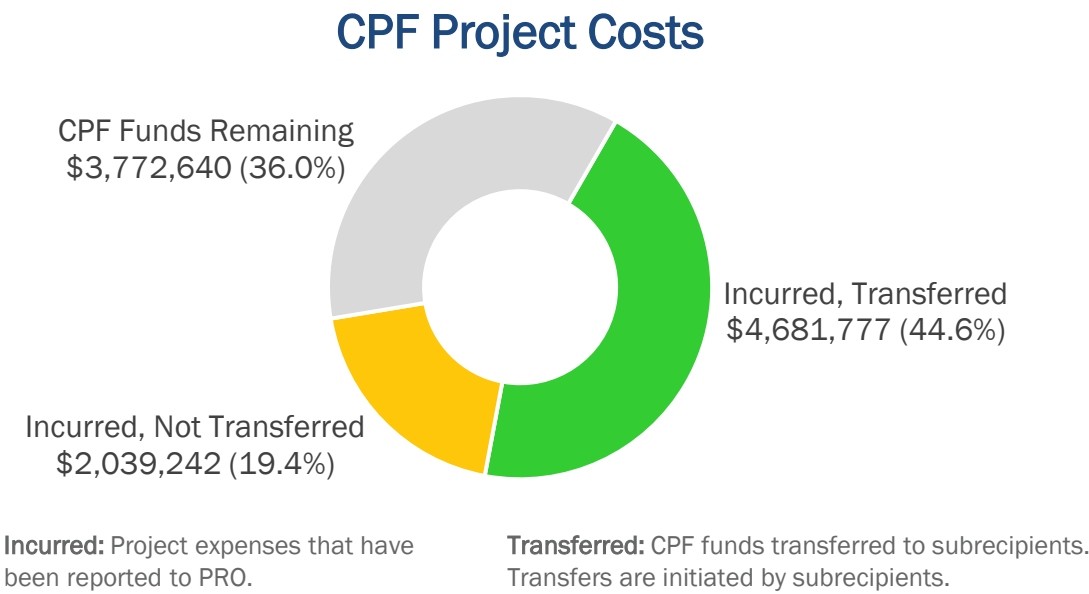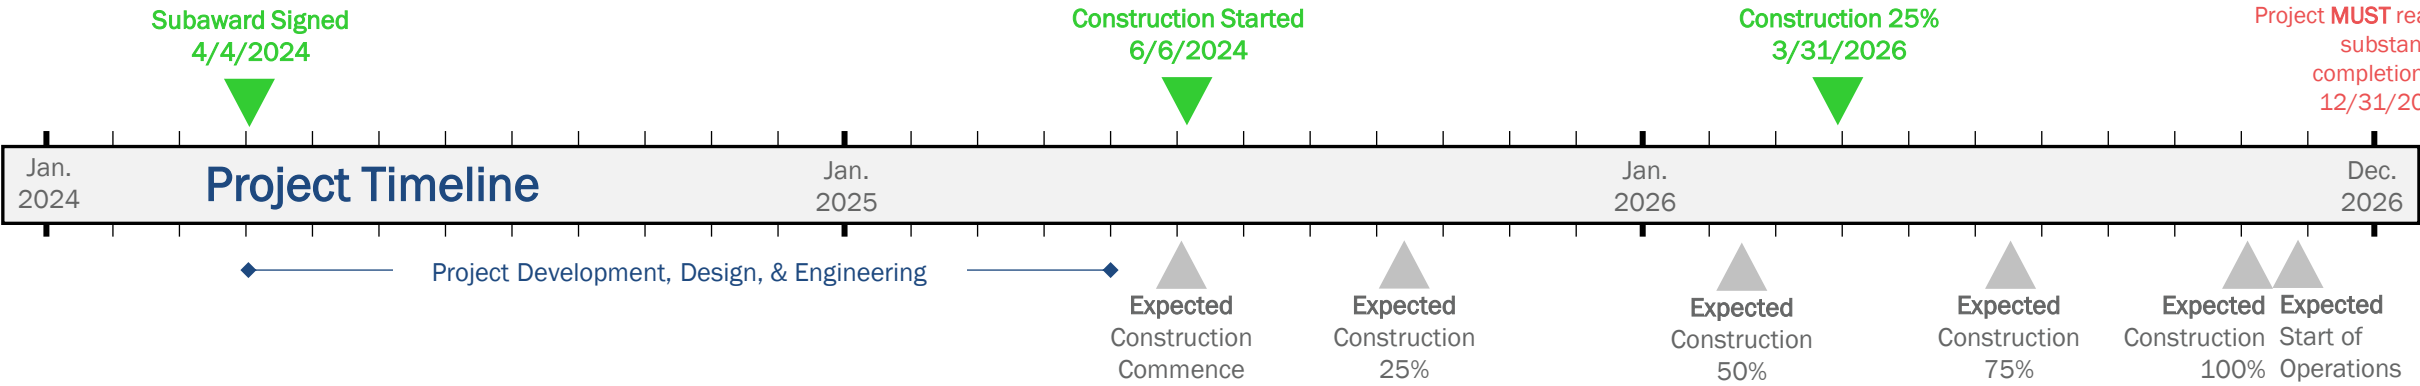

Harmony Library

Glocester
195 Putnam Pike

CPF award : **\$ 768,988**

Project is 100% funded through CPF



▲ Exterior of the existing building from parking lot

Project Size: **1,080 sf**

Asset Type: **Library**

Project Type: **New Build**

Asset Ownership: **Private**

Project Description:

- New 900 sf addition to the existing Harmony library, adding a community room for education and cultural events.
- Renovate existing space to provide dedicated resources for employment, education, and telehealth.

0

Classroom

2

Computer Lab

1

Multipurpose

1

Telemedicine

0

'Other' Assets

▼ Community room addition is ongoing. Vinyl siding has started on part of the new addition.




▼ New private spaces in main library




Harmony Library


Data as of FY2026 Q4

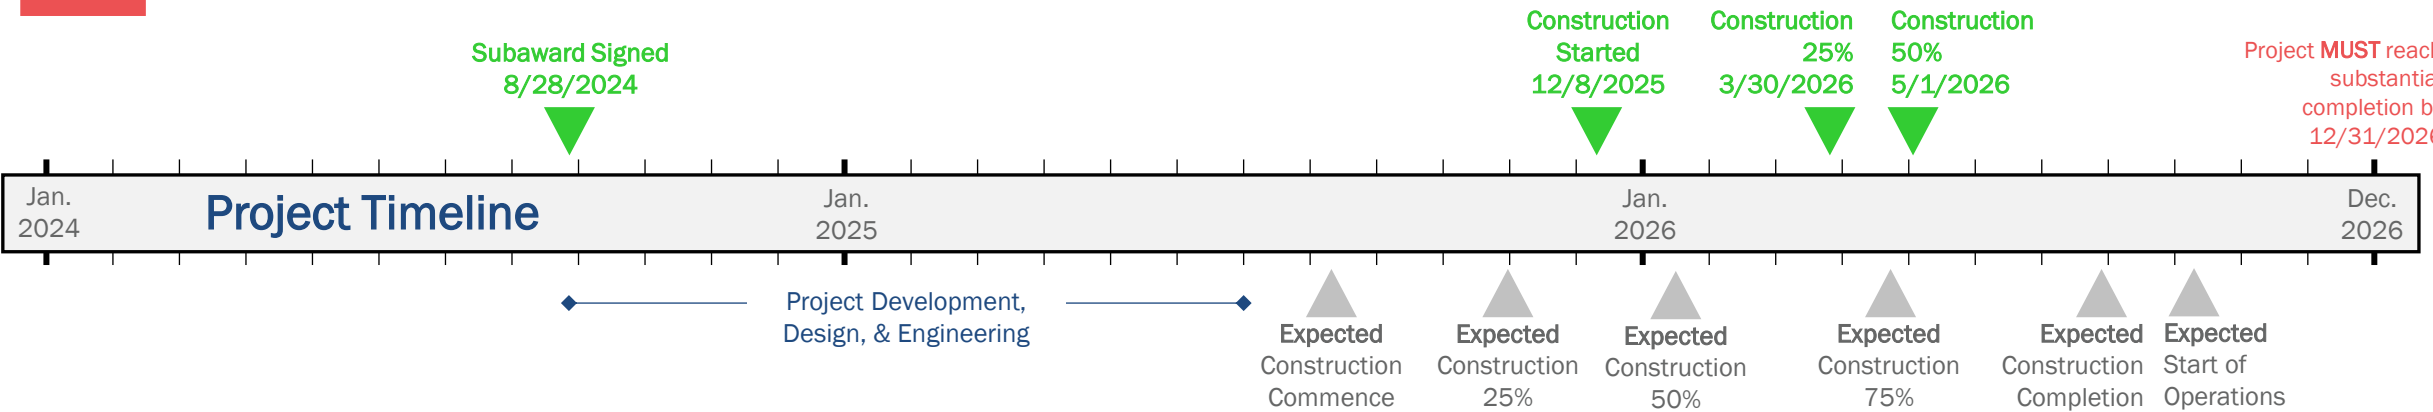

CPF Project Costs

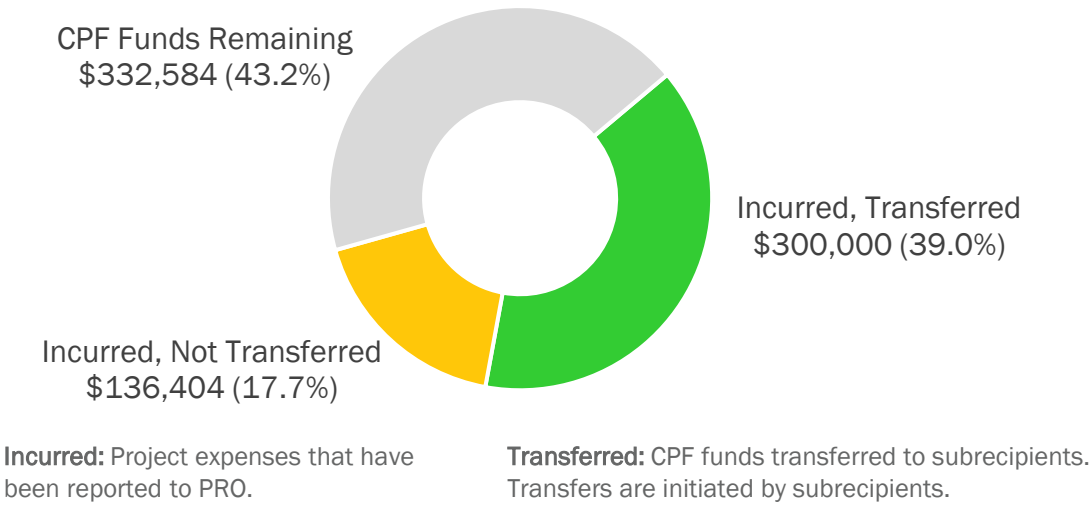

Project Expenses: Planned v. Actual

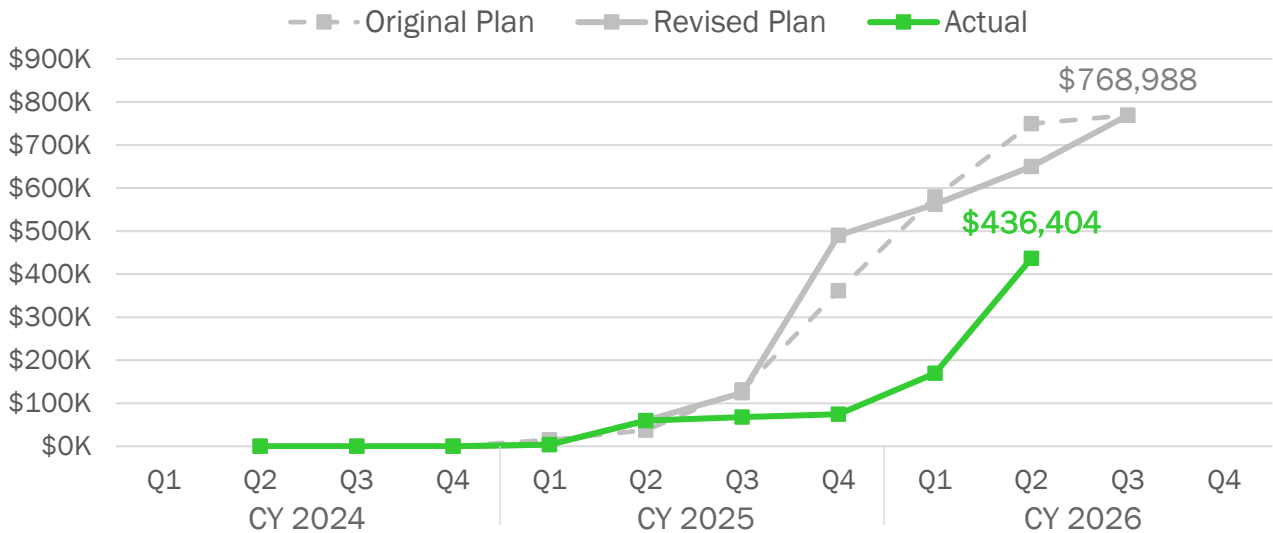

Lincoln Learning Center

Lincoln
98 Old River Road

CPF award : **\$ 2,000,000**

Project is 100% funded through CPF



▲ *Rendering of the new Rescue Center. The Lincoln Learning Center will be housed in the rear brick portion of the building.*

Project Size: **2,600 sf** Asset Type: **Community Center**

Project Type: **New Build** Asset Ownership: **Municipal**

Project Description:

- New construction attached to the Lincoln Central Rescue for administrative and operational efficiency.
- All rooms will have both wireless access and physical data drops. There will be acoustical ceilings with the optimal amount of LED lighting for increased productivity and privacy. All areas will have resilient flooring.

0

Classroom

0

Computer Lab

4

Multipurpose

1

Telemedicine

4

'Other' Assets

▼ *Flooring is being installed in main meeting space.*



▼ *1 of 3 new private spaces being created*






▼ *Exterior brick veneer complete*



Lincoln Learning Center

Data as of FY2026 Q4

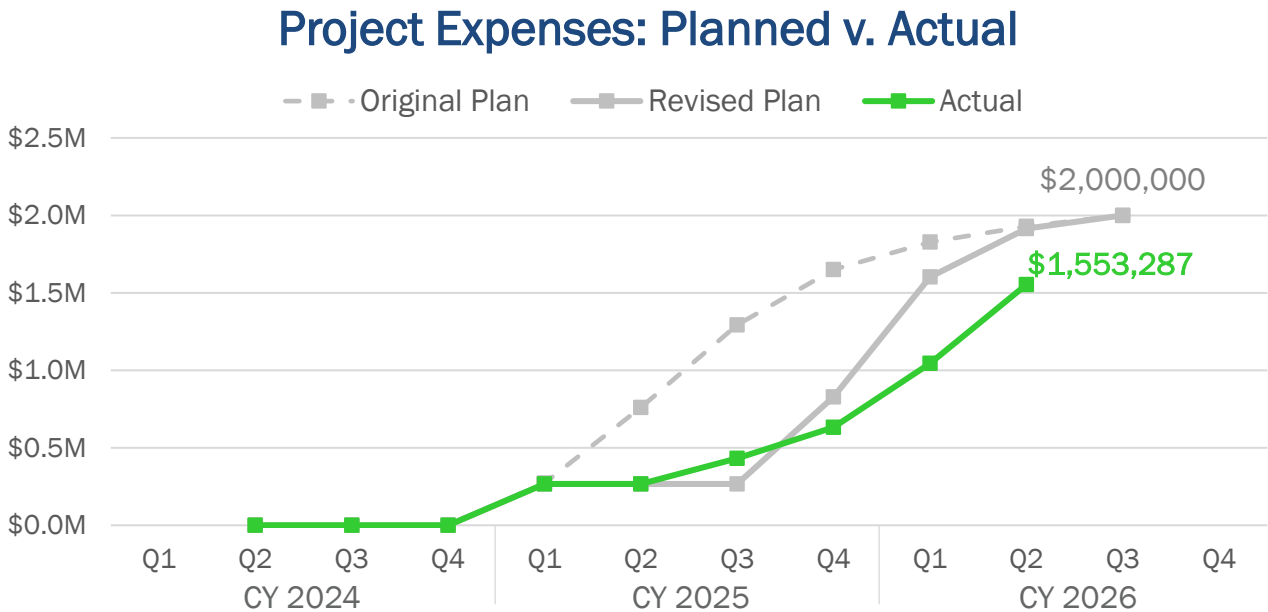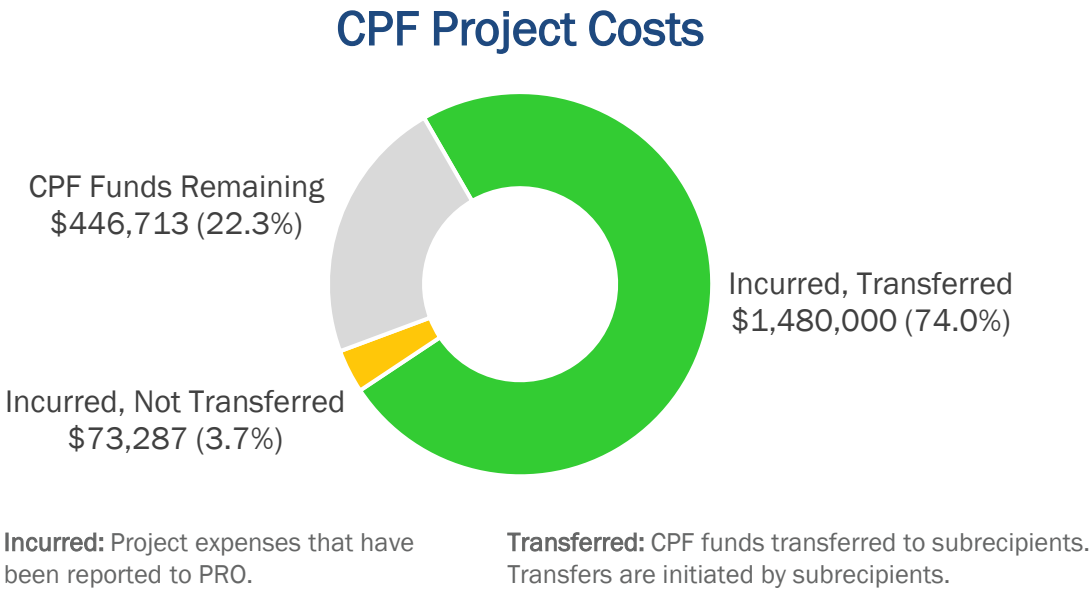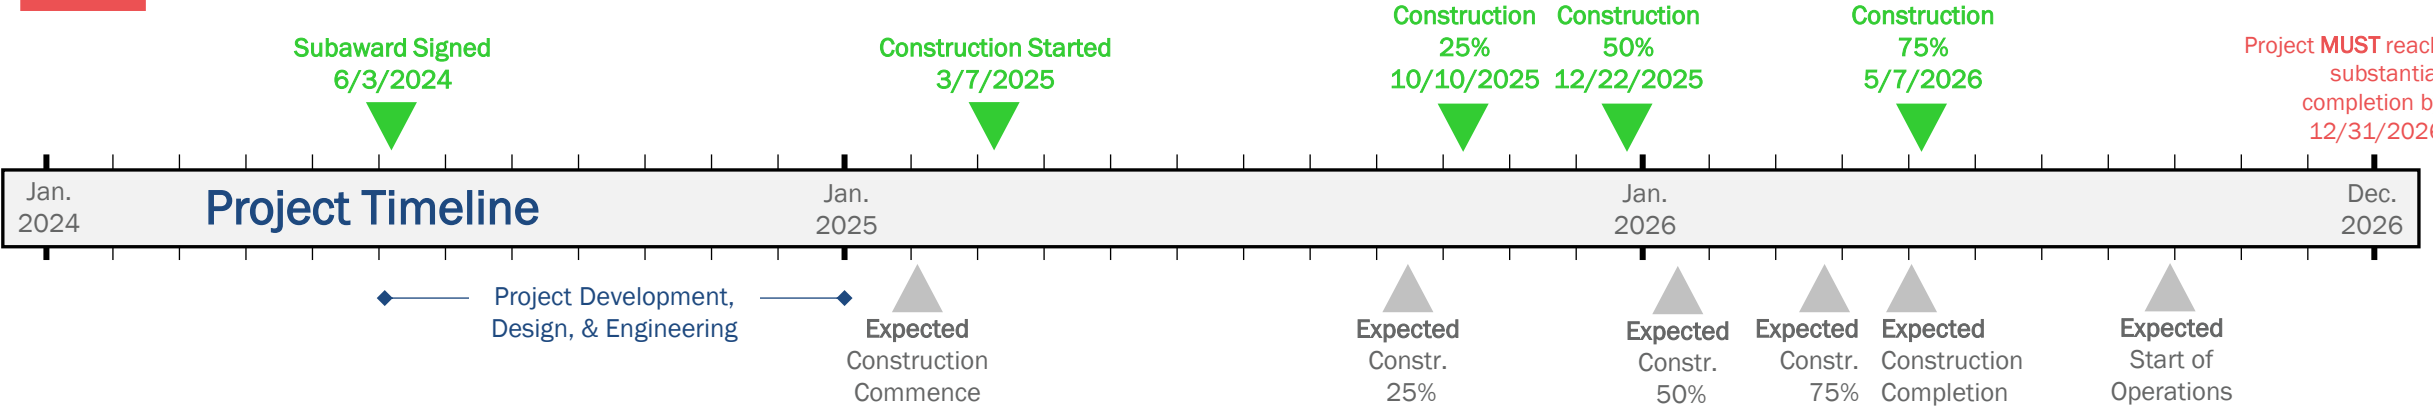

Florence Gray Center

Newport
1 York Street

CPF award : **\$ 7,527,554**

Project is 100% funded through CPF



▲ Exterior of the existing building. The Gallagher Wing is on the left side of the building.

Project Size: **15,700 sf** Project Type: **Renovation**

Asset Type: **Community Center**

Asset Ownership: **State & Quasi-Municipal**

Project Description:

- Major renovations to vacant 2-floor structure (Gallagher Wing) attached to currently operational Florence Gray Center.
- Minor and major upgrades to the interior layout, mechanical, electrical, plumbing, interior finishes, fixtures and equipment.
- A new interior staircase and new corridors for better circulation at the Florence Gray Community Learning Center.

7

Classroom

2

Computer Lab

4

Multipurpose


1

Telemedicine

0


'Other' Assets

A full building rehab is underway with new framing and drywall, mechanical, plumbing, electrical, flooring, etc. throughout the building. Exterior rehab is also underway.

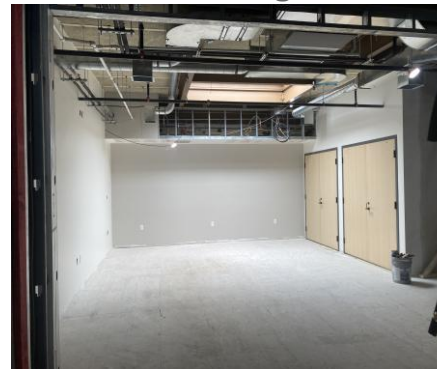


Florence Gray Center


Data as of FY2026 Q4

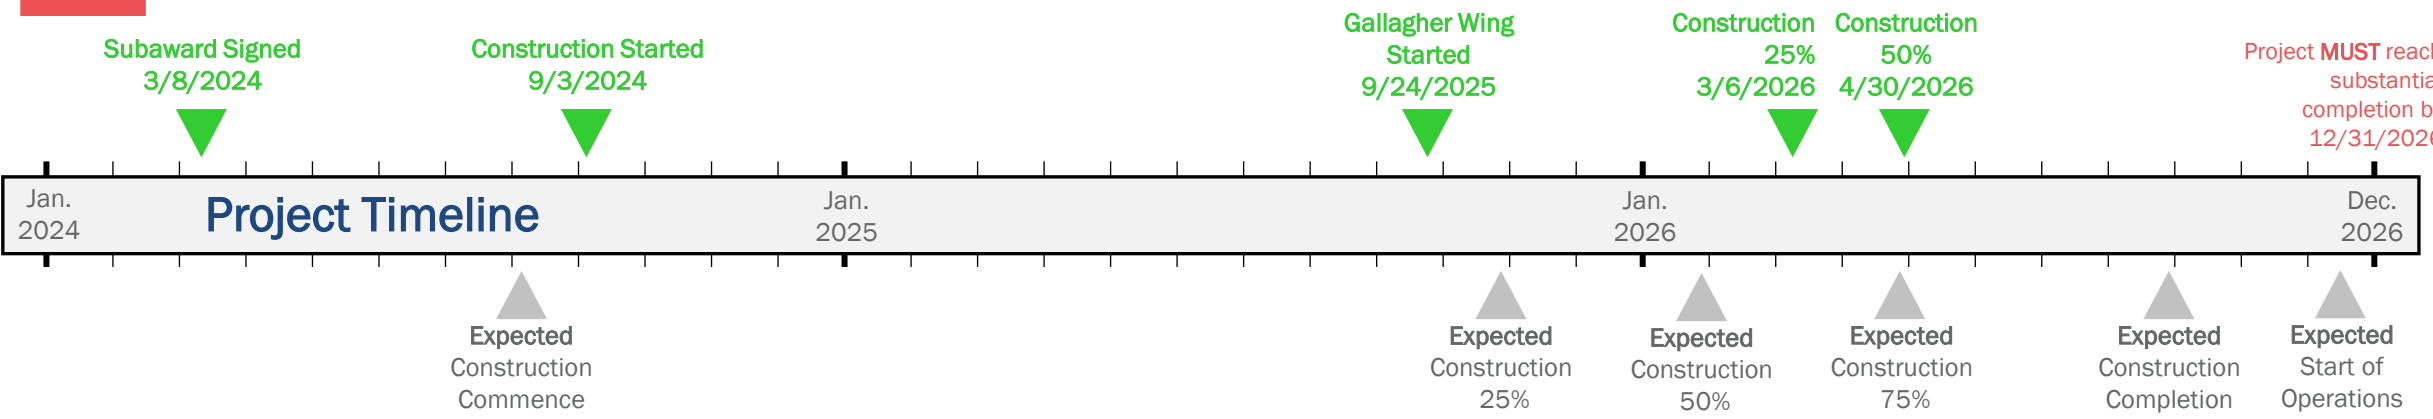

CPF Project Costs

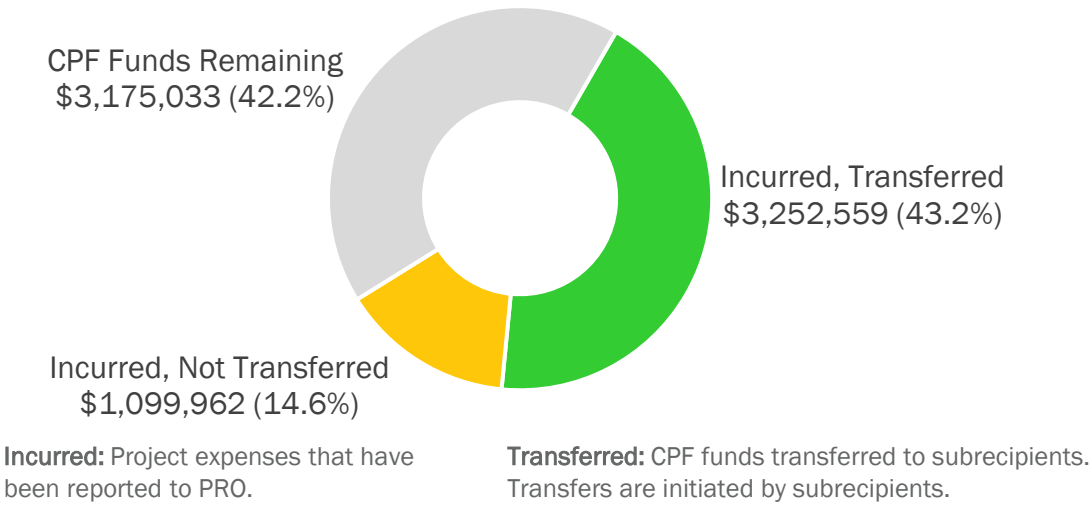

Project Expenses: Planned v. Actual

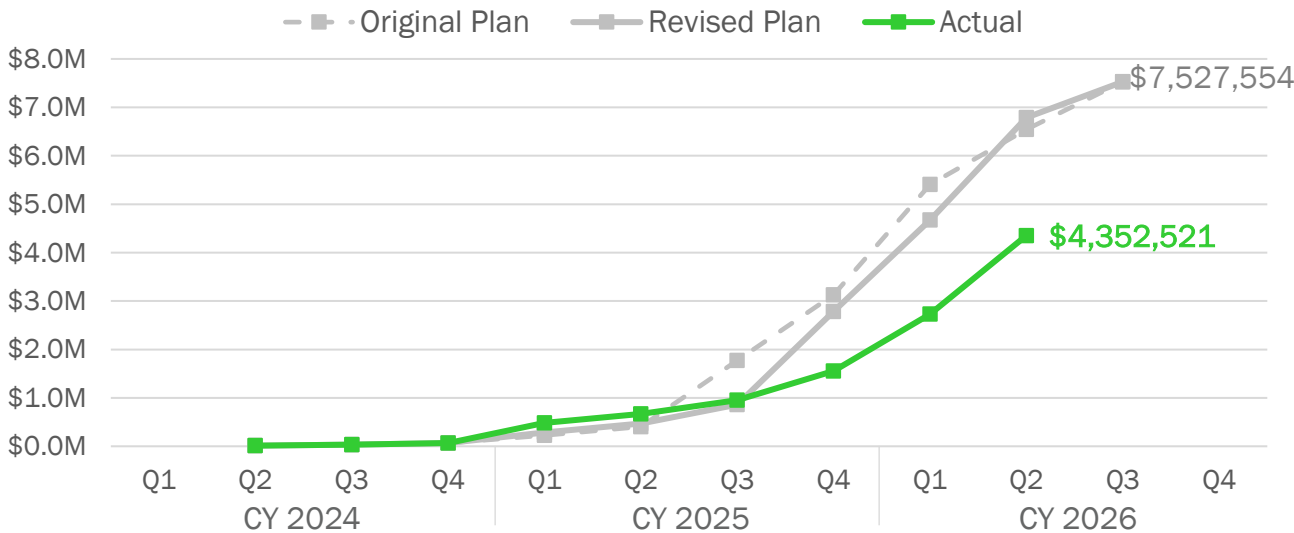

North Providence Community Center

North Providence
1810 Mineral Spring Avenue

CPF award : **\$ 2,860,894**

Project is 100% funded through CPF



▲ Exterior of the existing building

Project Size: **8,893 sf** Asset Type: **Library**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Renovation of the second floor of the library, the outside classroom area and stairwell from the upper parking area.
- Building wide mechanical, electrical, plumbing, fire protection upgrades; new receptacles & data outlets for each computer station, and convenience receptacles per code.
- One new and one renovated ADA compliant restroom

1

Classroom

1

Computer Lab

3

Multipurpose

1

Telemedicine

8


'Other' Assets

▼ The renovation of the exterior classroom space has commenced.




North Providence Community Center


Data as of FY2026 Q4

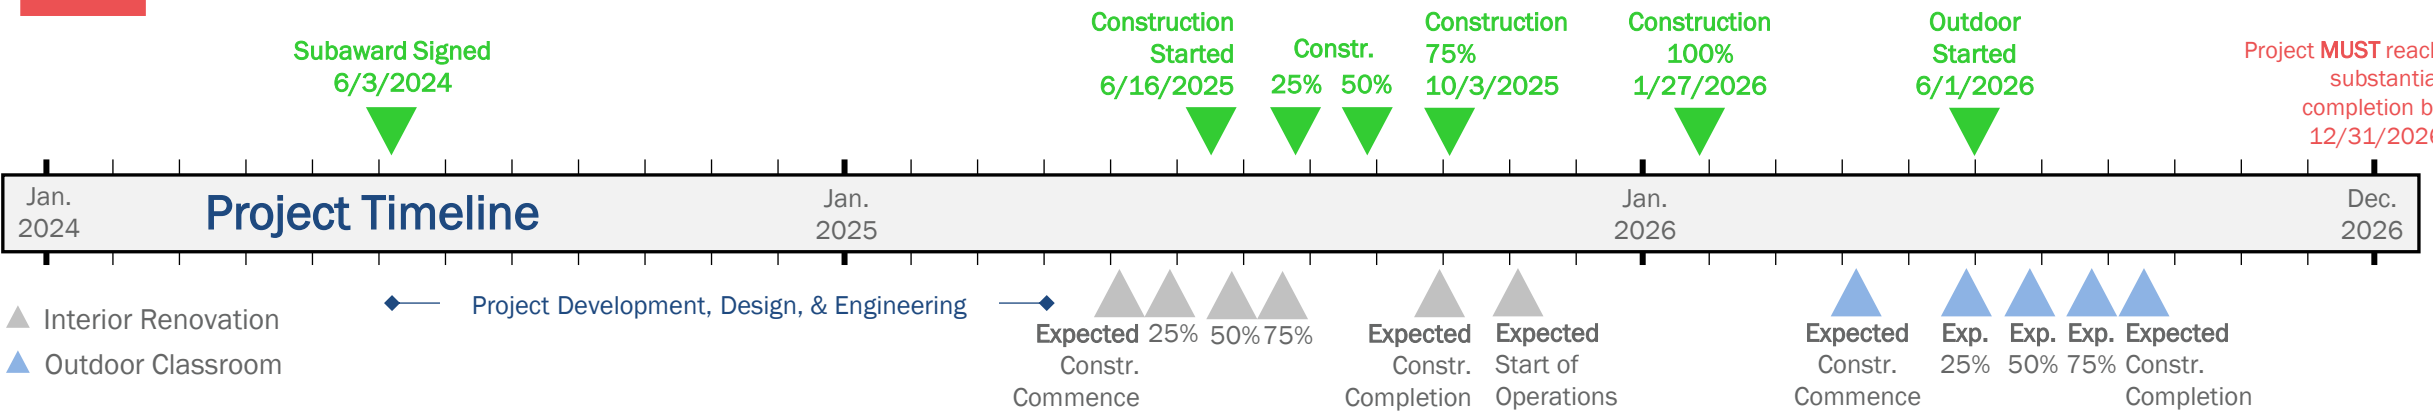

CPF Project Costs

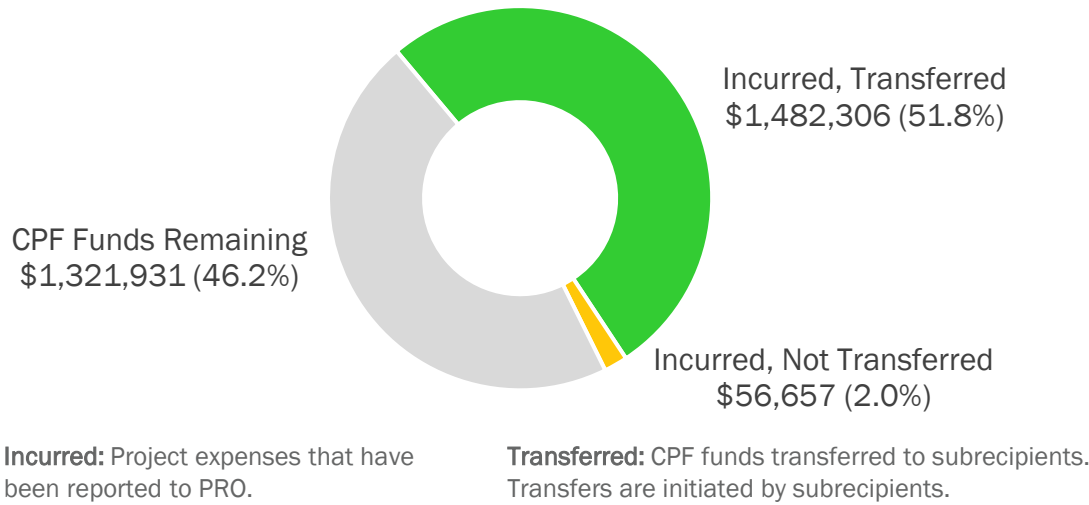

Project Expenses: Planned v. Actual

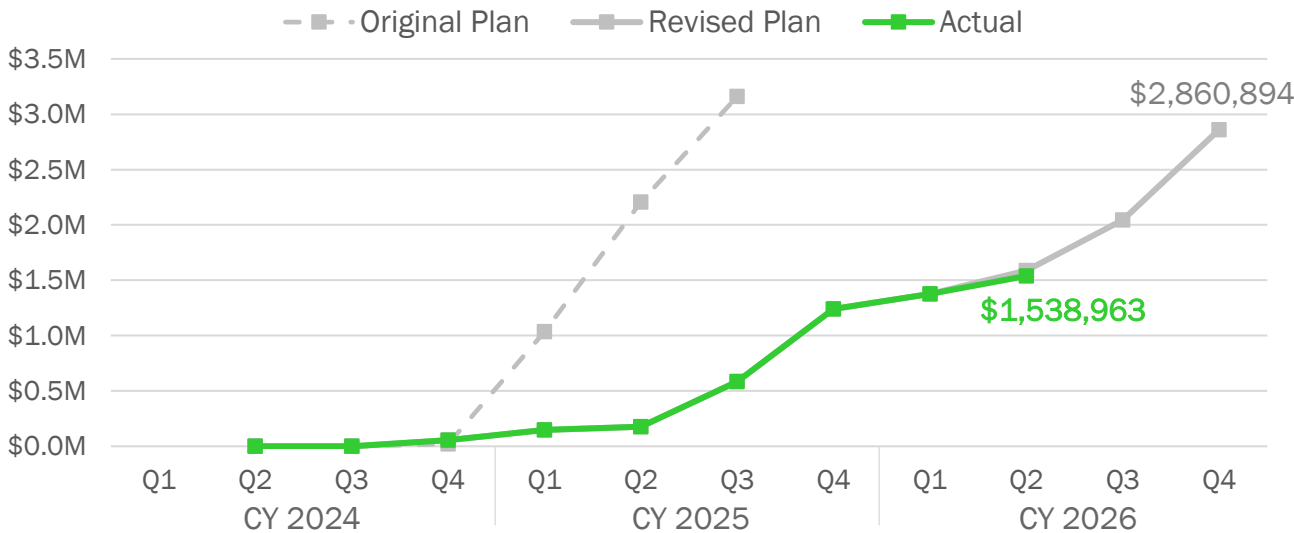

Davey Lopes Recreation Center

Providence
227 Dudley Street

CPF award : **\$ 7,583,842**

Project is 100% funded through CPF



▲ *Rendering of the exterior of the building from Dudley Street*

Project Size: **9,000 sf** Asset Type: **Recreation Center**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Complete renovation of all non-recreational spaces.
- No major structural work – project will include new finishes, fixtures, ADA compliance upgrades, and other repairs to create grant compliant spaces.

0

Classroom

1

Computer Lab

4

Multipurpose


1

Telemedicine

3




'Other' Assets

▼ *Repairs, framing and MEP work occurring throughout center*

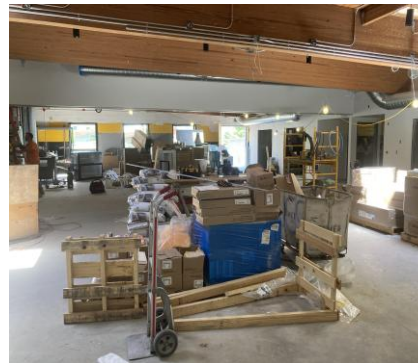

Davey Lopes Recreation Center

Data as of FY2026 Q4

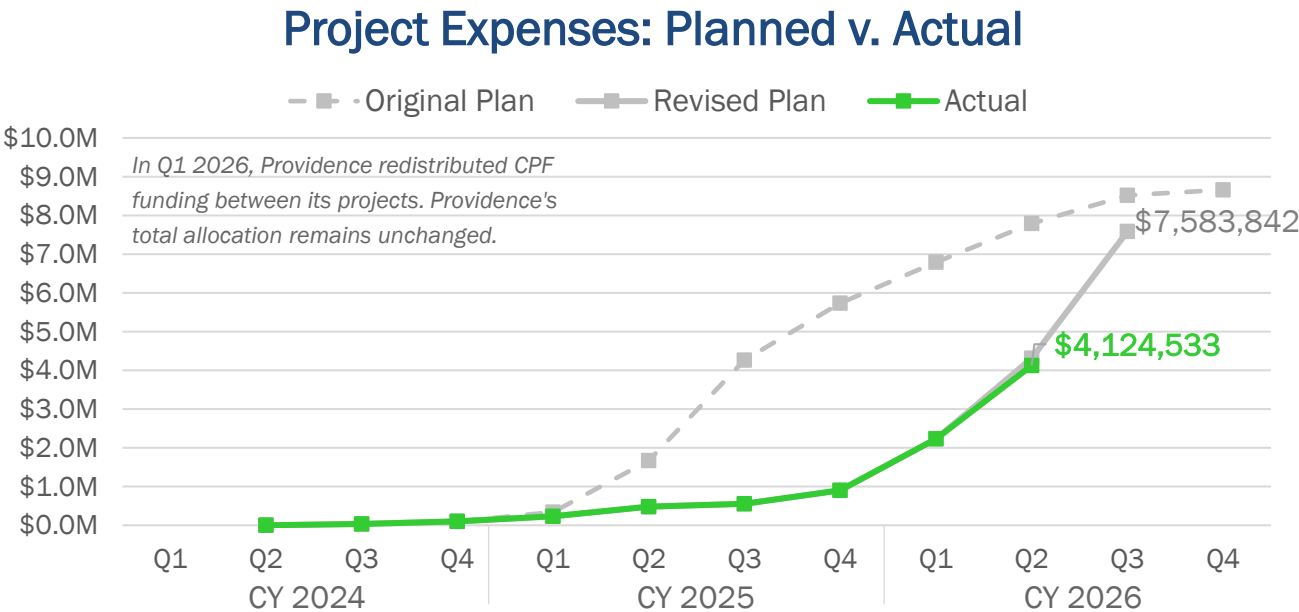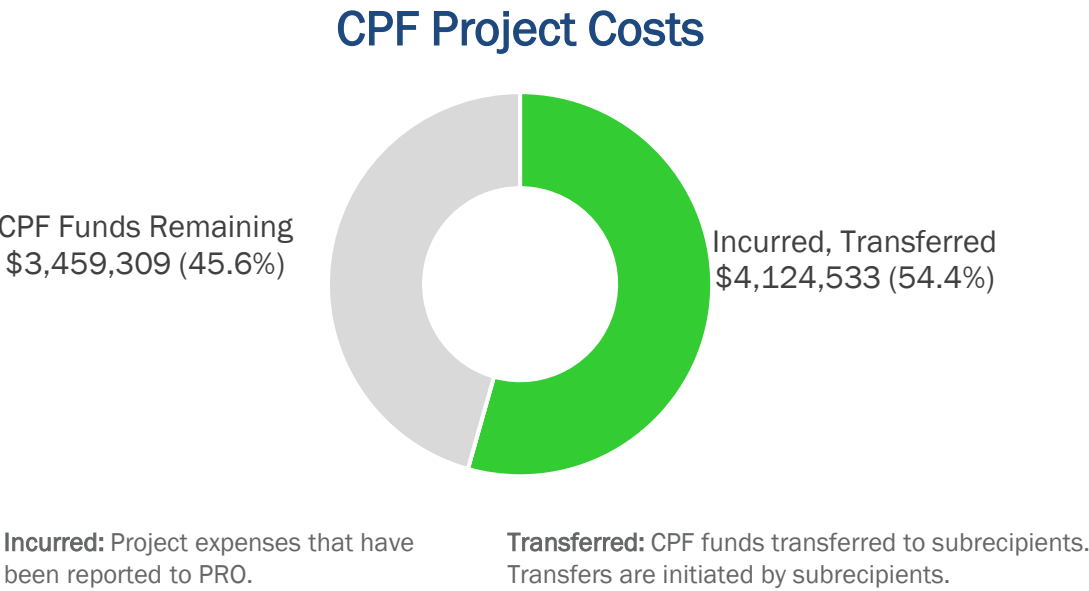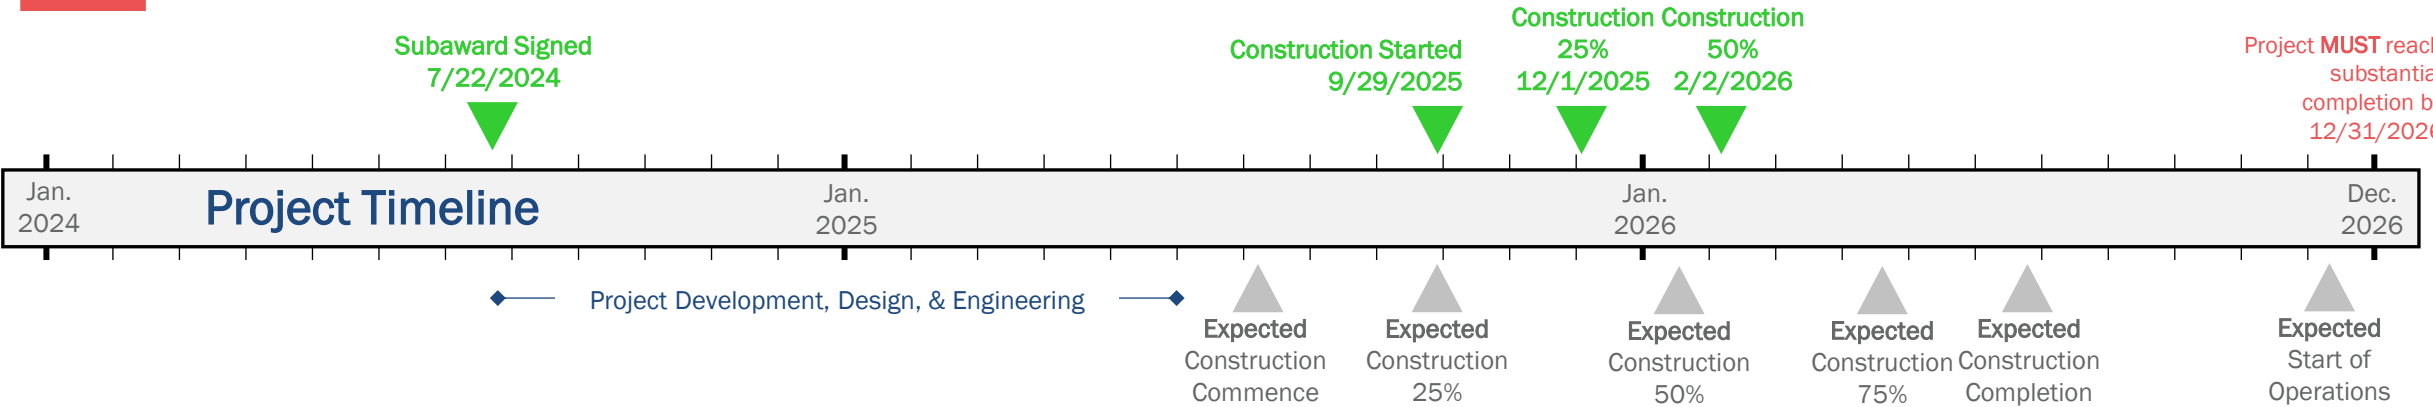

Joslin Recreation Center

Providence
17 Hyat Street

CPF award : **\$ 5,915,000**

Project is 100% funded through CPF



▲ Exterior of the existing building

Project Size: **12,830 sf** Asset Type: **Recreation Center**

Project Type: **Renovation** Asset Ownership: **Municipal**

Project Description:

- Renovation of non-recreational spaces
- Project includes new finishes, flooring, acoustical ceiling, lighting and paint, carbon neutral heating, HVAC upgrade, fire protection, security and access control, ADA accessibility.
- Cyber Lobby - computer lab: with modular furniture partitions.

0

Classroom

1

Computer Lab

4

Multipurpose


1

Telemedicine

1




'Other' Assets

▼ Repairs, framing and MEP work occurring throughout center

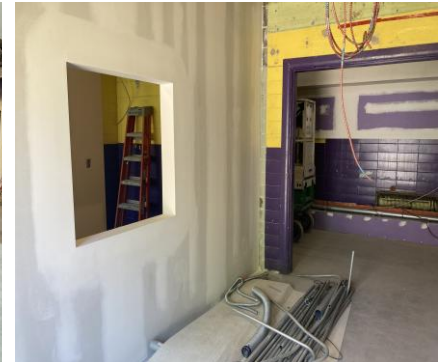

Joslin Recreation Center

Data as of FY2026 Q4

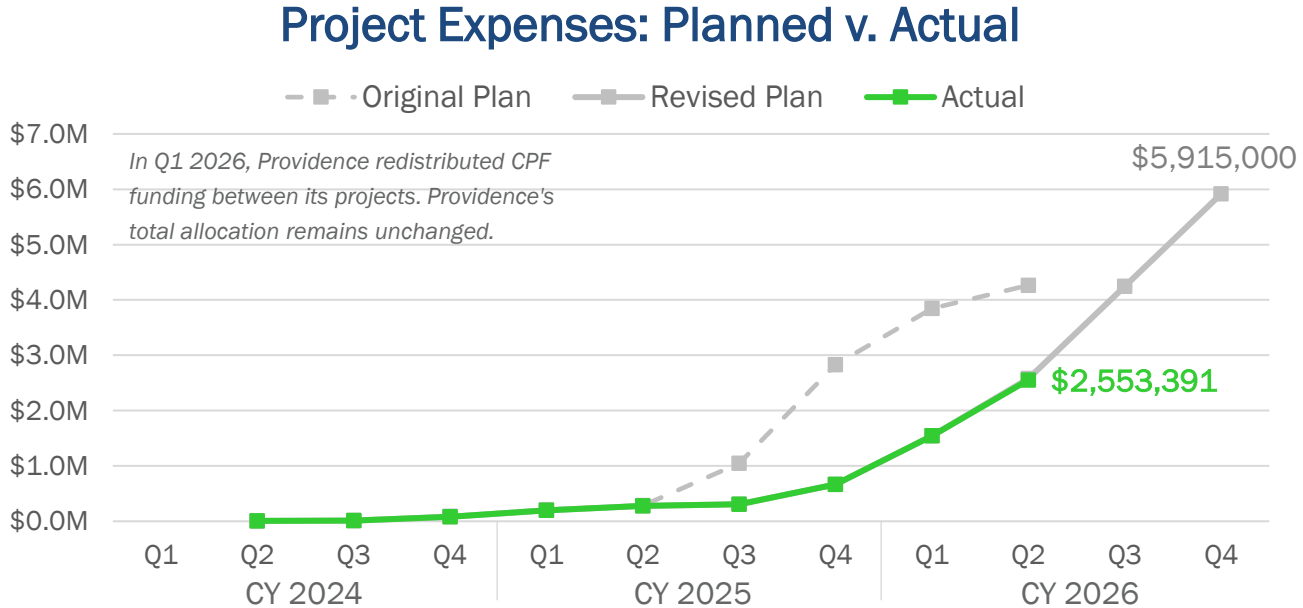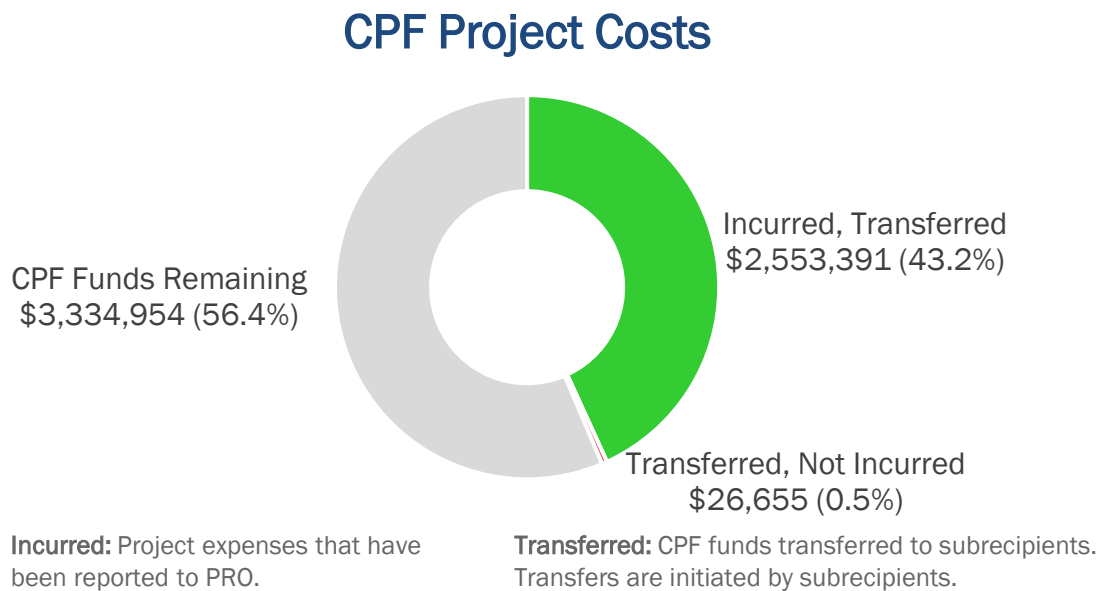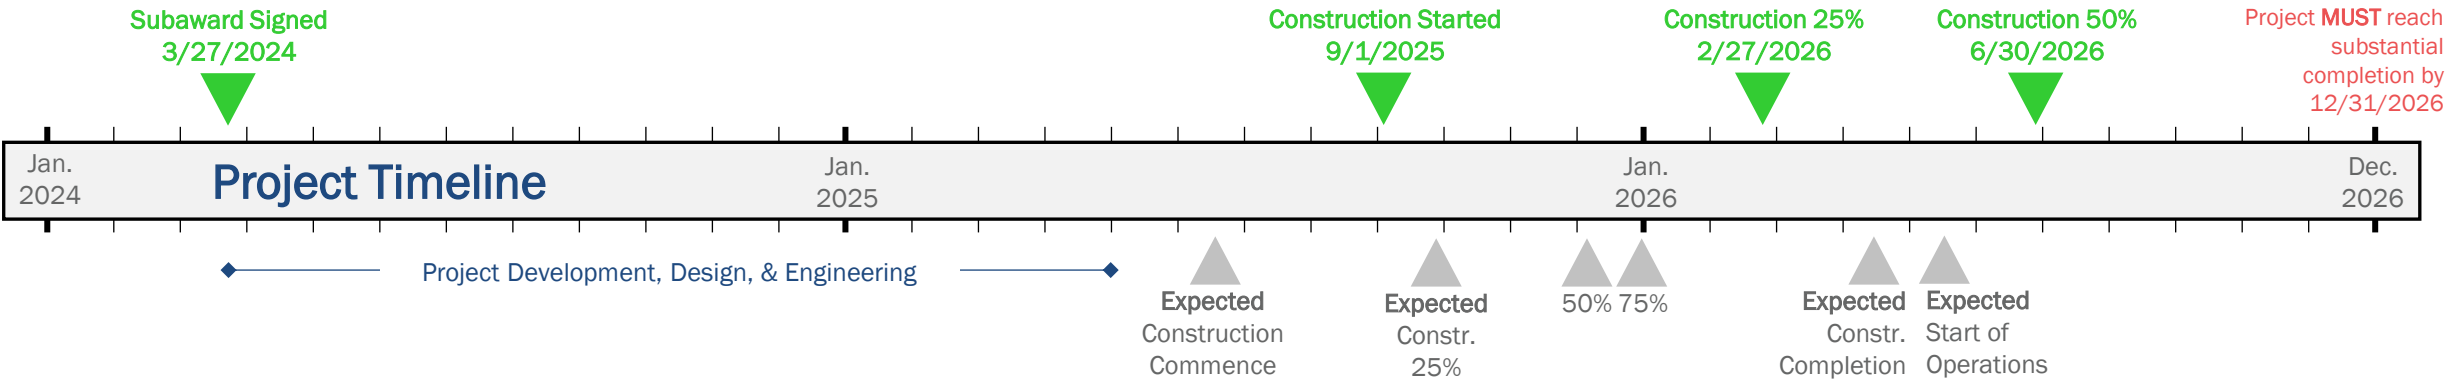

Peace Dale Library

South Kingstown
1057 Kingstown Road

CPF award : \$ 2,893,891

Total Project Cost : \$ 3,593,891

Project is funded through CPF, 81%, and a Community Development Block Grant, 19%



▲ Exterior of the library from Kingstown Road

Project Size: 3,867 sf Asset Type: Library

Project Type: Renovation Asset Ownership: Municipal

Project Description:

- Interior and exterior renovation at the Peace Dale Library Main Branch to create ADA accessible community learning center with a paramedic office, and enhanced parking and garden.
- Build out of mezzanine space and renovation of secondary balcony to create additional supportive and grant compliant spaces.

0

Classroom

0

Computer Lab

6

Multipurpose


1

Telemedicine


3

'Other' Assets


▼ Framing throughout the library is ongoing. A new staircase has been installed to access the mezzanine in the front room which will be open to the public once completed.

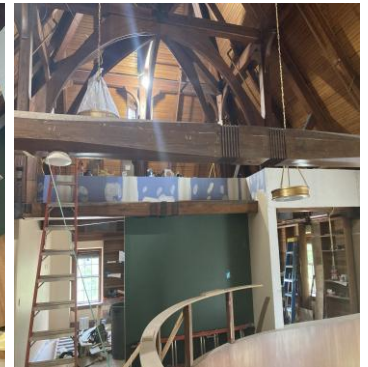


Peace Dale Library

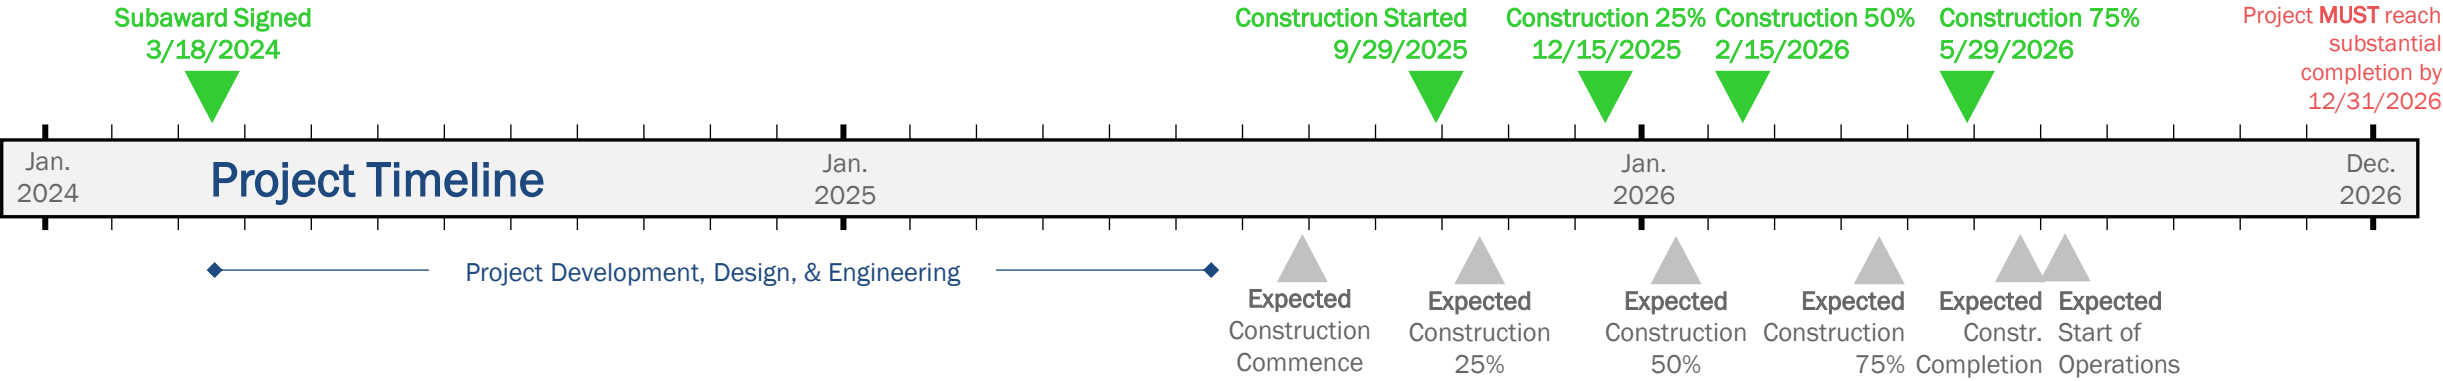

CPF Project Costs

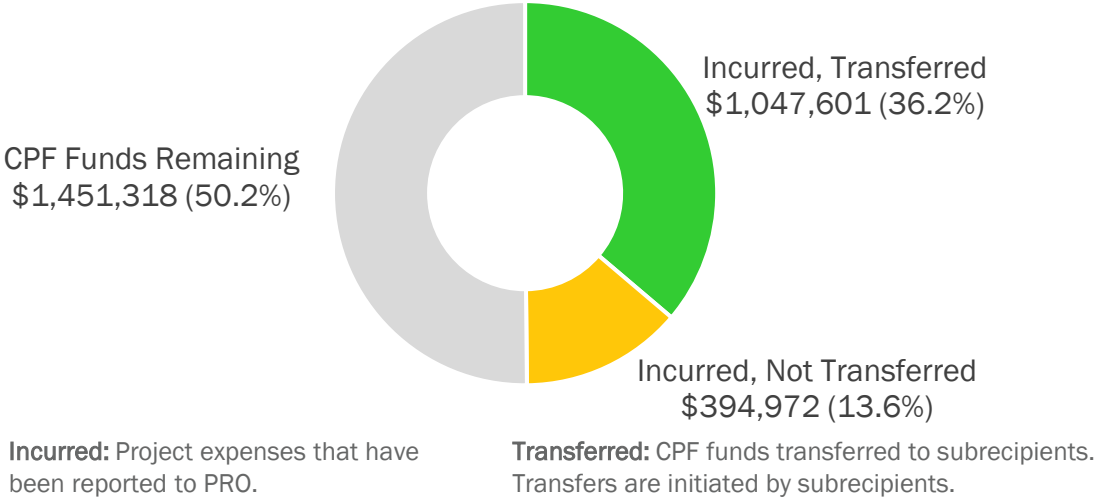

Project Expenses: Planned v. Actual

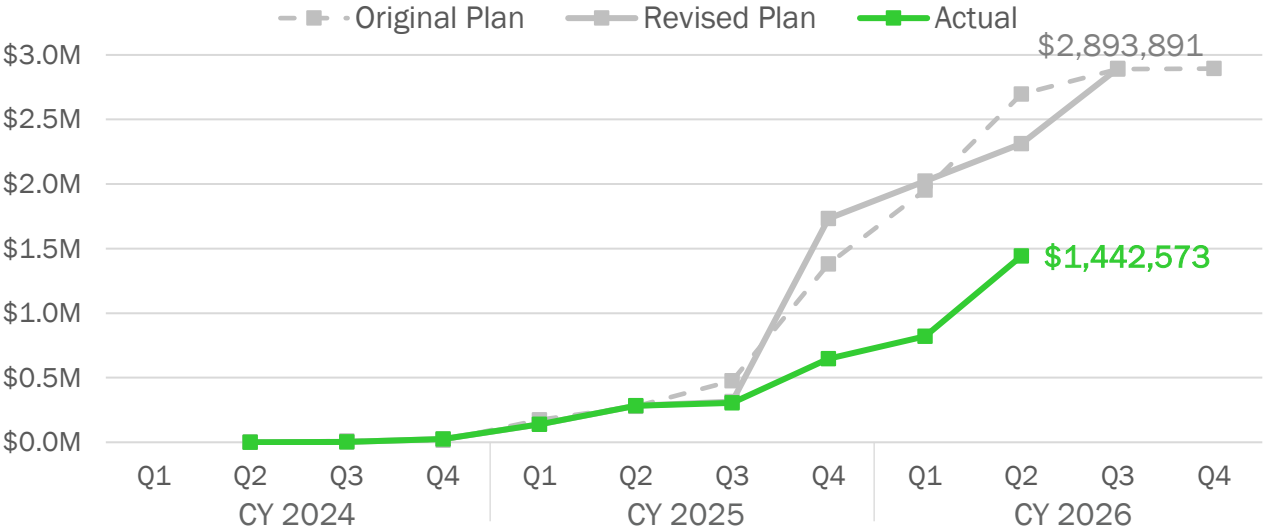

Tower Street Community Center

Westerly
83 Tower Street

CPF award : **\$ 3,819,120**

Total Project Cost : **\$ 7,031,199.88**

Project is funded through CPF, 54%, and other federal funds, private donations and town resources, 46%



▲ Exterior rendering from Entry Drive

Project Size: **8,000 sf** Asset Type: **Community Center**

Project Type: **New Build** Asset Ownership: **Private**

Project Description:

- Single story, new construction on the site of the former Tower Street Elementary School.
- 8,000 square foot building divided between the Westerly Education Center, Wood River Health Services, and the Town of Westerly.

3

Classroom

0

Computer Lab

2

Multipurpose

3

Telemedicine

21


'Other' Assets

▼ *Frame of the building and roof trusses are erected. Interior framing, mechanical, plumbing, and electrical work is ongoing.*




Tower Street Community Center


Data as of FY2026 Q4

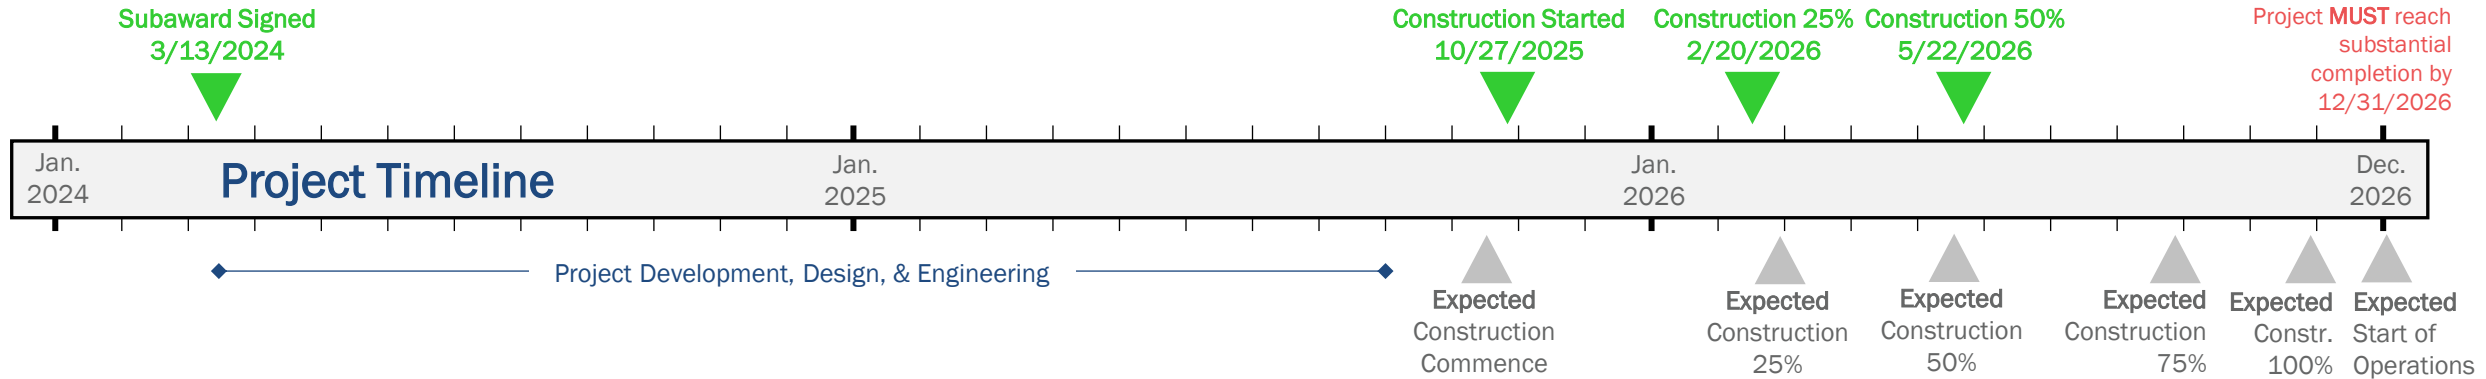

CPF Project Costs

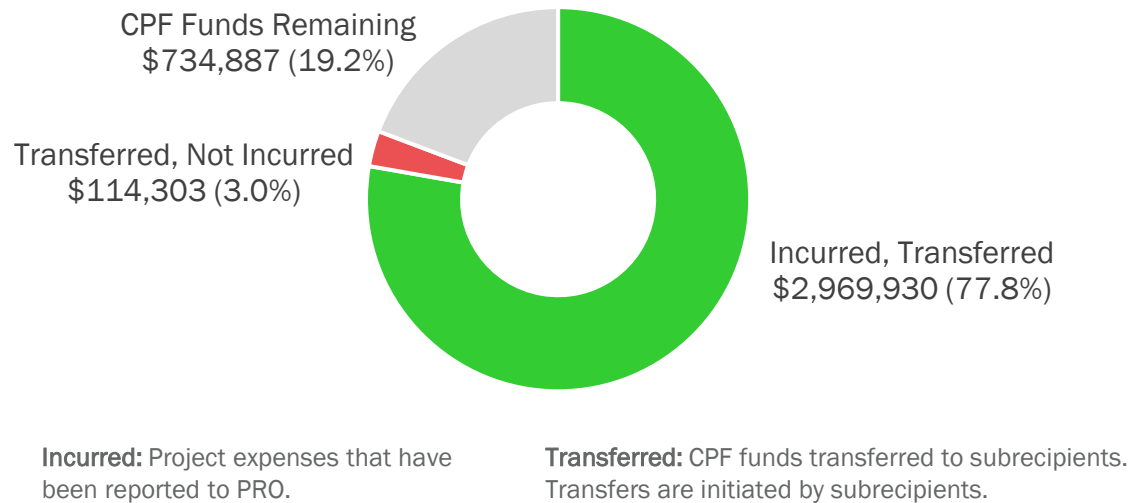

Project Expenses: Planned v. Actual

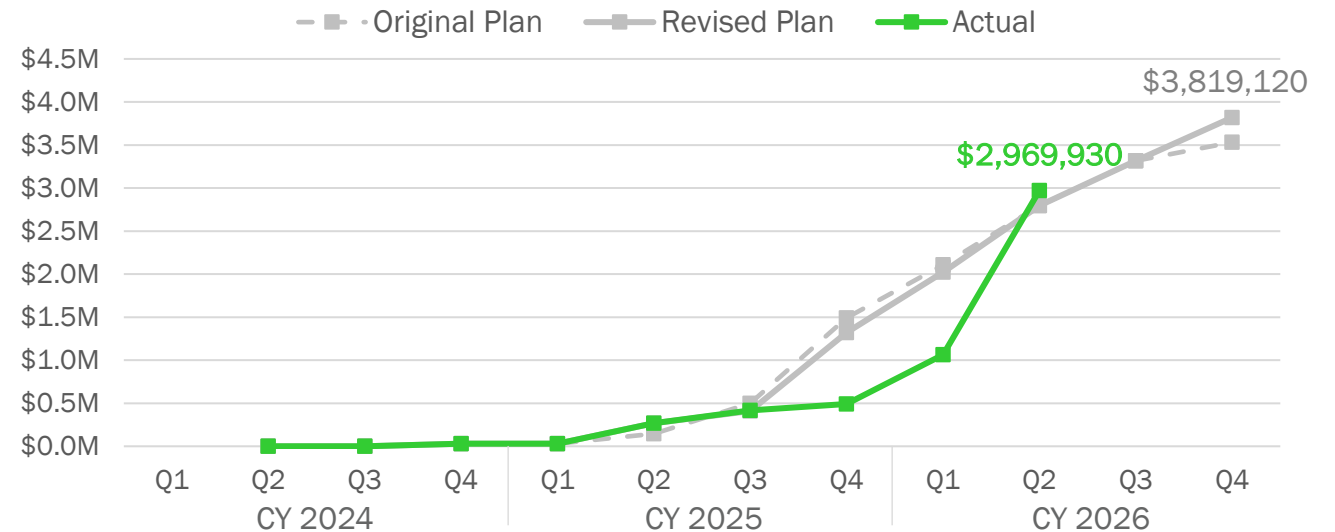

Multipurpose Center at Cass Park

Woonsocket
366 Cumberland Hill Road

CPF award : **\$ 7,143,500**

Project is 100% funded through CPF



▲ *Rendering of the new multipurpose center at Cass Park*

Project Size: **14,000 sf** Asset Type: **Multipurpose Center**

Project Type: **New Build** Asset Ownership: **Municipal**

Project Description:

- New construction consisting of a concrete slab on grade floor with a prefabricated metal building structure.
- Project located next to new athletic center currently under construction.

3

Classroom

1

Computer Lab

3

Multipurpose



5

Telemedicine




13

'Other' Assets

▼ *Steel building erection is ongoing.*

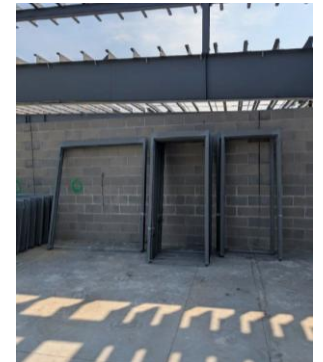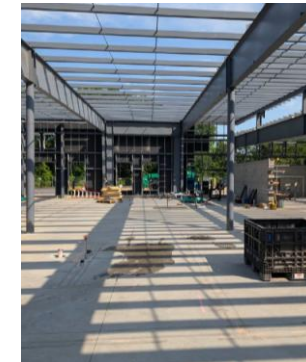

Multipurpose Center at Cass Park

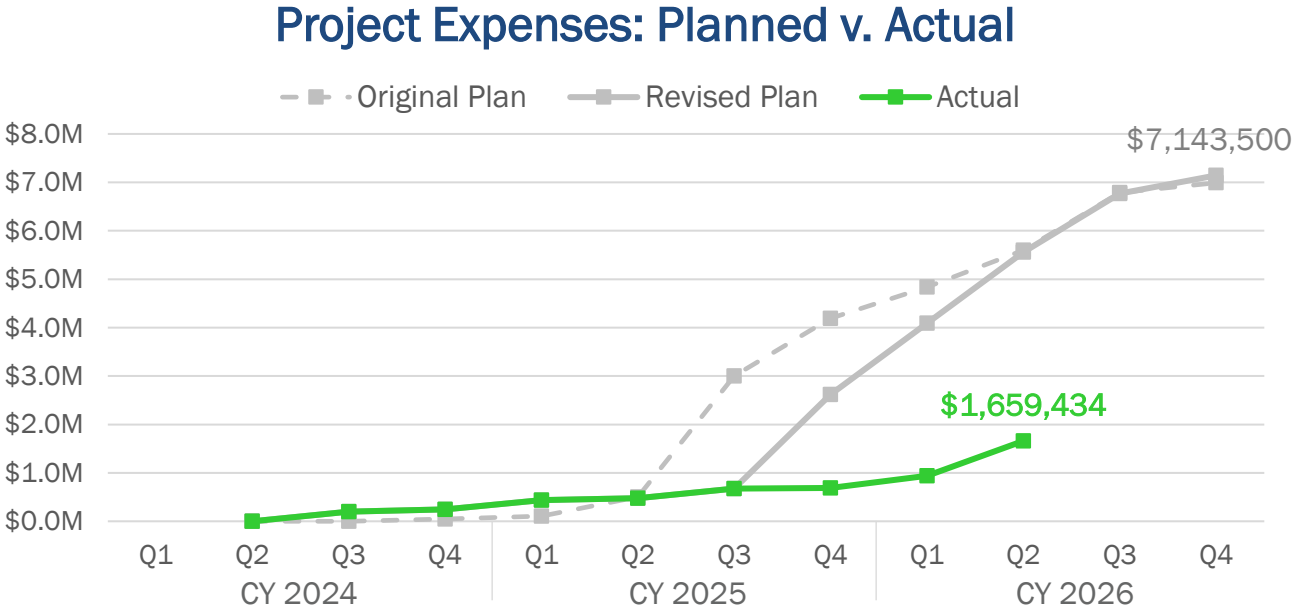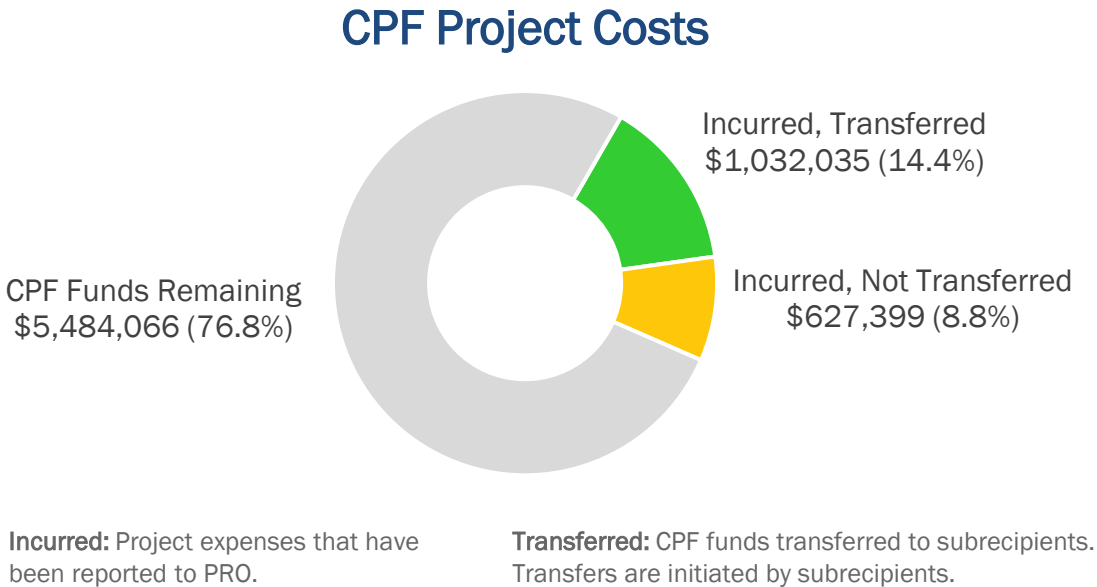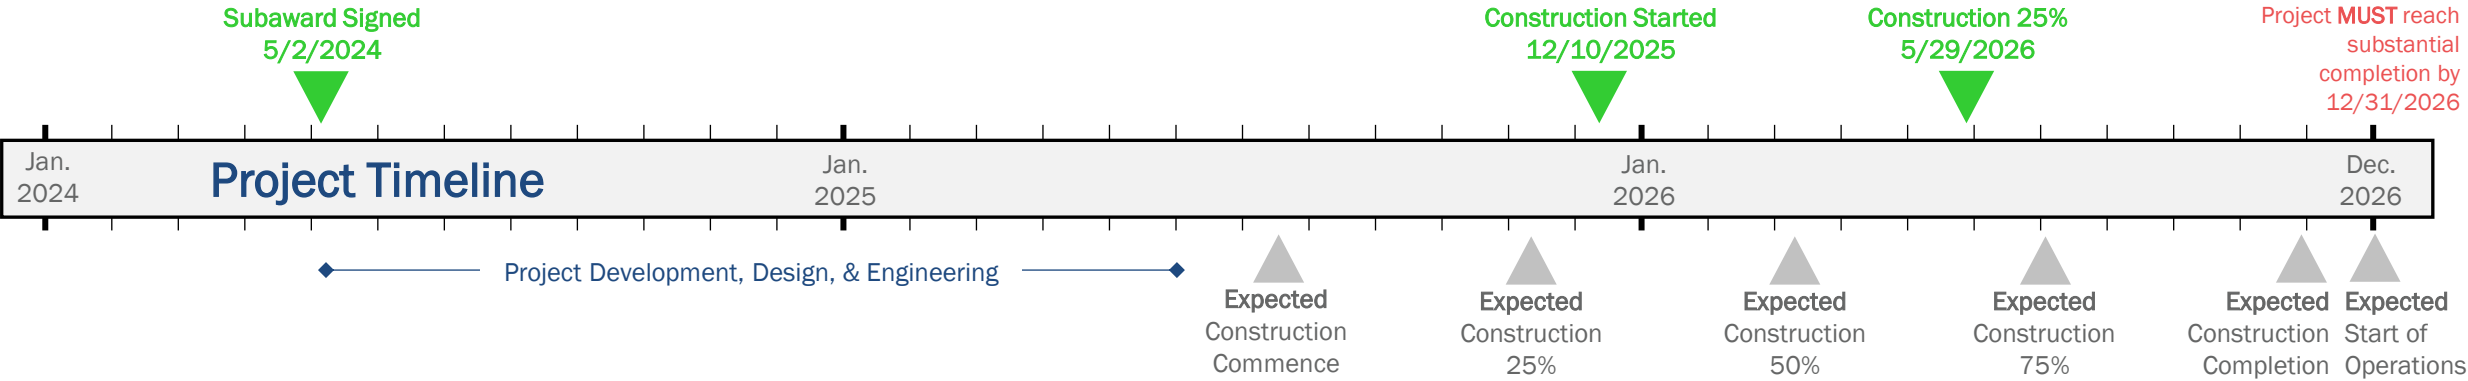




Community Library Municipal Grant

Round 2 Project Update

As of June 30, 2026

Community Library Municipal Grant Locations

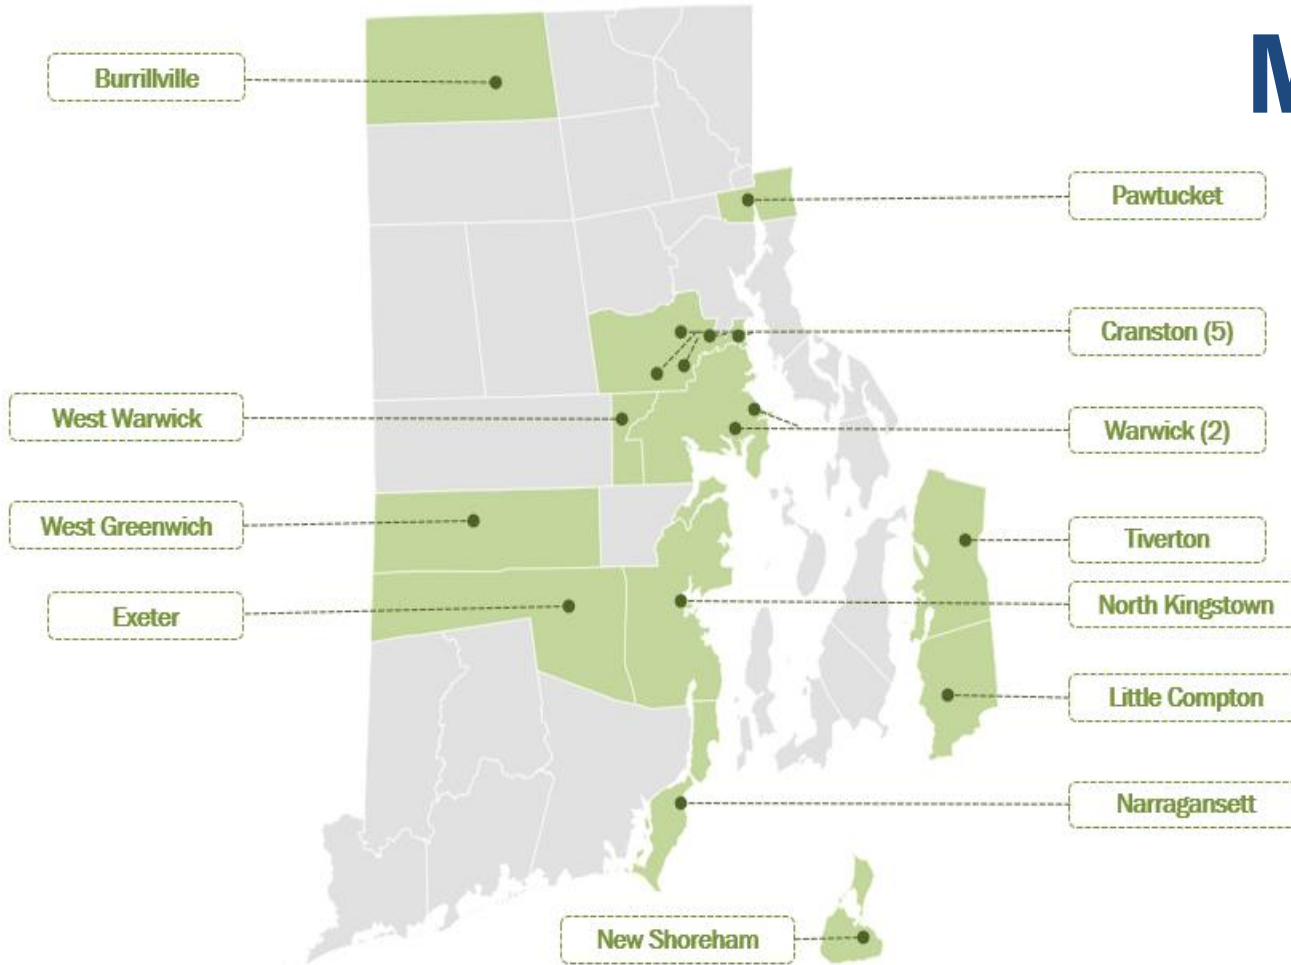

- Current Amount Subawarded: **\$973,175**
- Twelve municipalities are participating in round 2 and are enhancing 17 community libraries across the State of Rhode Island.
- Municipalities that participated in round 1 were deemed ineligible for round 2.

Budgets & Expenditures

Data as of FY2026 Q4

Municipality	Project	Total Project Cost	CPF Award	Reported Expenses	CPF Funds Transferred	CPF Funds Remaining
Burrillville	Jesse M. Smith Memorial Library	\$493,000	\$39,670	\$0	\$0	\$39,670
Cranston	Cranston Public Library - Auburn	\$21,704	\$21,704	\$0	\$0	\$21,704
	Cranston Public Library - Central	\$147,853	\$147,853	\$0	\$0	\$147,853
	Cranston Public Library - Knightsville	\$12,438	\$12,438	\$0	\$0	\$12,438
	Cranston Public Library - Oaklawn	\$10,000	\$10,000	\$0	\$0	\$10,000
	Cranston Public Library - William Hall	\$18,010	\$18,010	\$0	\$0	\$18,010
Exeter	Exeter Public Library	\$26,965	\$26,965	\$0	\$0	\$26,965
Little Compton	Brownell Library	\$25,000	\$25,000	\$0	\$0	\$25,000
Narragansett	Maury Loontjens Memorial Library	\$25,000	\$25,000	\$0	\$0	\$25,000

Budgets & Expenditures

Data as of FY2026 Q4

Municipality	Project	Total Project Cost	CPF Award	Reported Expenses	CPF Funds Transferred	CPF Funds Remaining
New Shoreham	Island Free Library	\$150,000	\$25,475	\$0	\$0	\$25,475
North Kingstown	North Kingstown Free Library	\$59,502	\$51,644	\$0	\$0	\$51,644
Pawtucket	Pawtucket Public Library	\$1,295,978	\$242,226	\$0	\$0	\$242,226
Tiverton	Tiverton Public Library	\$35,863	\$35,863	\$0	\$0	\$35,863
Warwick	Warwick Public Library - Central	\$111,489	\$111,489	\$0	\$0	\$111,489
	Warwick Public Library - Conimicut	\$69,868	\$69,868	\$0	\$0	\$69,868
West Greenwich	Louitt Library	\$26,834	\$26,834	\$0	\$0	\$26,834
West Warwick	West Warwick Public Library	\$83,136	\$83,136	\$0	\$0	\$83,136
TOTAL		\$2,612,640	\$973,175	\$0	\$0	\$973,175

Burrillville, RI
Jesse M. Smith Memorial Library



The Town of Burrillville is part of Providence County in Northern Rhode Island and has a population of 16,157.

The \$39,670 of CLMG funding supported the complete roof replacement at Jesse M. Smith Memorial Library. Beginning in August 2024, the library provides recreation, education, work, and health-monitoring related services including literacy and digital literacy programs, information assistance, entertainment, job search and application support, technology assistance, skills training support, health and wellness programs.

Location: **100 Tinkham Lane Harrisville, RI 02830**
CPF Funds: **\$39,670**
Status: **Construction Complete. Closeout Pending.**

Cranston, RI
Cranston Public Library – Auburn



The City of Cranston is part of Providence County in Central Rhode Island and has a population of 82,000.

The \$21,704 of CLMG funding at Cranston's Auburn Library will support the replacement of fire alarm wired connections to an AES radio box system, the purchase of furniture for the public reading area, and ADA compliant automatic door upgrades to the front door. All work is expected to be completed by October 2026.

Location: **396 Pontiac Ave Cranston, RI 02910**
CPF Funds: **\$21,704**
Status: **Less than 50% Complete**

Cranston, RI
Cranston Public Library – Central



The City of Cranston is part of Providence County in Central Rhode Island and has a population of 82,000.

The \$147,853 of CLMG funding at Cranston's Central Library will support the replacement of a rooftop RTU unit for building-wide HVAC, fire alarm wired connections to an AES radio box system, improvements to the library's security system, the digital learning lab, new study carrels, furniture, and systems for hearing accessibility in the Library's community room. All work is expected to be completed by October 2026.

Location: **140 Sockanosset Cross Rd Cranston, RI**
CPF Funds: **\$147,853**
Status: **Less than 50% Complete**

Cranston, RI
Cranston Public Library – Knightsville



The City of Cranston is part of Providence County in Central Rhode Island and has a population of 82,000.

The \$12,438 of CLMG funding at Cranston's Knightsville Library will support the replacement of fire alarm wired connections to an AES radio box system and improvements to the library's security system. All work is expected to be completed by October 2026.

Location: **1847 Cranston St Cranston, RI 02920**
CPF Funds: **\$12,438**
Status: **Less than 50% Complete**

Cranston, RI
Cranston Public Library – Oaklawn



The City of Cranston is part of Providence County in Central Rhode Island and has a population of 82,000.

The \$10,000 of CLMG funding at Cranston's Oaklawn Library will support the replacement of fire alarm wired connections to an AES radio box system. All work is expected to be completed by October 2026.

Location: **230 Wilbur Ave Cranston, RI 02921**
CPF Funds: **\$10,000**
Status: **Less than 50% Complete**

Cranston, RI
Cranston Public Library – William Hall



The City of Cranston is part of Providence County in Central Rhode Island and has a population of 82,000.

The \$18,010 of CLMG funding at Cranston's William Hall Library will support the replacement of fire alarm wired connections to an AES radio box system, improving systems for hearing accessibility in the Library's auditorium and the creation of a self-service high-speed scanning, copying and faxing station. All work is expected to be completed by October 2026.

Location: **1825 Broad St Cranston, RI 02905**
CPF Funds: **\$18,010**
Status: **Less than 50% Complete**

Exeter, RI
Exeter Public Library



The Town of Exeter is part of Washington County in Southern Rhode Island and has a population of 7,195.

The \$26,965 funding will support the modification of two public restrooms at the Exeter Public Library. These improvements will enhance the comfort, accessibility, and overall experience, supporting visitation and participation in library programs and services. The upgraded facilities will help ensure the library remains a safe, welcoming, and functional public space for all community members.

Location: **675 Ten Rod Rd Exeter, RI 02822**
CPF Funds: **\$26,965**
Status: **Less than 50% Complete**

Little Compton, RI
Brownell Library



The Town of Little Compton is part of Newport County in Eastern Rhode Island and has a population of 3,616.

The \$25,000 of funding will support the purchased of new furniture, fixtures and equipment (FF&E) at the Brownell Library. The library is one of the few community gathering spaces in Little Compton. The capital asset is used by people looking for a place to read, access the internet for school, work, and health purposes, gather for conversation, and for other various library programs. This grant will allow the library to replace old and outdated FF&E.

Location: **44 Commons St Little Compton, RI 02837**
CPF Funds: **\$25,000**
Status: **Not Started**

Narragansett, RI
Maury Loontjens Memorial Library



The Town of Narragansett is part of Washington County in Southern Rhode Island and has a population of 14,532.

The \$25,000 of CLMG funding supported the modification and updating of the Maury Loontjens Memorial Library's roof with safety railings and the installation of solar panels. The library continues to provide programming supporting work, education and health monitoring with programs such as computer classes, makerspace workshops, health and wellness sessions, among others.

Location: **25 Pier Market Pl Narragansett, RI 02882**
CPF Funds: **\$25,000**
Status: **Construction Complete. Closeout Pending.**

New Shoreham, RI Island Free Library



The Town of New Shoreham is part of Washington County in Southern Rhode Island and has a population of 1,410.

The \$25,475 of CLMG funding supported the purchase and installation of a new LULA elevator at the Island Free Library. Beginning May 2026, the Library can provide full access to all floors, programs, collections and meeting spaces in its facility representing a return to full service as a community center and hub of activities for the island community.

Location: **9 Dodge St New Shoreham, RI 02807**
CPF Funds: **\$25,475**
Status: **Construction Complete. Closeout Pending.**

North Kingstown, RI North Kingstown Free Library



The Town of North Kingstown is part of Washington County in Southern Rhode Island and has a population of 27,732.

The \$51,644 of CLMG funding supported the modification and modernization of the North Kingstown Free Library elevator. The project improved reliability and safety, ensuring that all patrons can independently access programming, private meeting spaces, public computers with reliable broadband internet access, workforce development resources, and telehealth access throughout the facility.

Location: **100 Boone St North Kingstown, RI 02852**
CPF Funds: **\$51,644**
Status: **Construction Complete. Closeout Pending.**

Pawtucket, RI Pawtucket Public Library



The City of Pawtucket is part of Providence County in Northern Rhode Island and has a population of 75,604.

The \$242,226 of CLMG funding supported the installation of a new automatic sprinkler system. This capital asset upgrade was required per the Pawtucket Fire Marshall to meet the local fire codes. The project was completed in April 2024.

Location: **13 Summer St Pawtucket, RI 02860**
CPF Funds: **\$242,226**
Status: **Construction Complete. Closeout Pending.**

Tiverton, RI
Tiverton Public Library



The Town of Tiverton is part of Newport County in Eastern Rhode Island and has a population of 16,369.

The \$35,863 of CLMG funding will support the purchase of furniture and equipment for the Learning Center, Seminar Room, and Teen Library. Funding will also go towards the creation of storage in the Learning Center. All work is expected to be completed by early October 2026.

Location: **34 Roosevelt Ave Tiverton, RI 02878**
CPF Funds: **\$35,863**
Status: **Not Started**

Warwick, RI
Warwick Public Library – Central



The City of Warwick is part of Kent County in Central Rhode Island and has a population of 84,187.

The \$111,488.80 of funding at Warwick’s Central Library supported the provision of new furniture for study rooms and program/meeting rooms, improved privacy for program/meeting rooms, carpet replacement in various high traffic spaces, installation of ADA automatic door mechanisms for the restrooms, a replacement of the library’s water heater, and a replacement of exterior doors at the main entrance

Location: **600 Sandy Lane Warwick, RI 02889**
CPF Funds: **\$111,488.80**
Status: **More than 50% Complete**

Warwick, RI
Warwick Public Library - Conimicut



The City of Warwick is part of Kent County in Central Rhode Island and has a population of 84,187.

The \$69,868.20 of funding at Warwick’s Conimicut Library supported the provision of new furniture for studying, programming, and general use within the branch. The funding will also support the painting and restoration of the exterior of the building. Replacements and repairs to the roof, chimney and gutters will also be completed within the period of performance. Roof work is expected to be completed by September 2026.

Location: **55 Beach Ave Warwick, RI 02889**
CPF Funds: **\$69,868.20**
Status: **Less than 50% Complete**

West Greenwich, RI Louttit Library



The Town of West Greenwich is part of Kent County in Central Rhode Island and has a population of 6,750.

The \$26,834 of funding will support the modification of the adult room, children's room, and circulation area by removing and replacing the old carpeting at the Louttit Library. Upon project completion, Louttit Library plans to provide programs and services that are educational for adults and children, support job searchers, and provide private spaces for telehealth appointments at the library.

Location: **274 Victory Hwy West Greenwich, RI 02817**
CPF Funds: **\$26,834**
Status: **Not Started**

West Warwick, RI West Warwick Public Library



The Town of West Warwick is part of Kent County in Western Rhode Island and has a population of 31,000.

The \$83,136 funding will support the provision of new library furniture to replace worn and outdated furniture items, as well as the removal and disposal of the old furniture at the West Warwick Public Library. After project completion, the library will be able to better serve patrons while providing a range of programs and services in multiple areas of the building which will be enhanced by the provision of new furniture at the library.

Location: **1043 Main St West Warwick, RI 02893**
CPF Funds: **\$83,136**
Status: **Not Started**

RHODE
ISLAND
